

DATE: 05-03-17

PERMIT APPLICATION

PLEASE TYPE OR PRINT CLEARLY

105446686

JOB NO: (OFFICE USE ONLY)

105336376

PERMIT NO: (OFFICE USE ONLY)

1705091064

APPLICATION TYPE

REGULAR EXPRESS 

City of Dallas

STREET ADDRESS OF PROPOSED PROJECT 3534 Espanola Dr.		SUITE/BLDG/FLOOR NO	USE OF PROPERTY Residential
APPLICANT [REDACTED]		ADDRESS [REDACTED]	CITY Farmers Branch TX
STATE TX		ZIP CODE 75234	
CONTRACTOR INDIVIDUAL [REDACTED]		CONTRACTOR NUMBER R0102598	FIN
COMPANY NAME FCL Dallas Roofing		E-MAIL ADDRESS (MAY BE USED FOR OFFICIAL COMMUNICATION)	
CURRENT HOME REPAIR LICENSE ON FILE?	<input checked="" type="checkbox"/> YES <input type="checkbox"/> NO	IF YES, LIST NUMBER 1213097	PHONE NO [REDACTED]
PROPERTY OWNER INDIVIDUAL CONTACT [REDACTED]		ADDRESS [REDACTED]	CITY Farmers Branch TX
STATE TX		ZIP CODE 75234	
PROPERTY OWNER COMPANY NAME FCL Dallas Roofing		PHONE NO	E-MAIL ADDRESS (MAY BE USED FOR OFFICIAL COMMUNICATION)
DESCRIPTION OF PROPOSED PROJECT Replace sheetrock y siding and frame work, New front door and new bathroom, new AC unit		VALUATION (\$) 8000.00	CONST AREA (sq ft) 1332 FT
NEW CONST			
MFD OTHER			
REMODEL			
TOTAL VALUATION			
TOTAL AREA			
PLEASE INDICATE ALL TYPES OF WORK THAT WILL BE PART OF THIS PROJECT BY CHECKING THE APPROPRIATE BOX			
<input checked="" type="checkbox"/> BUILDING	<input checked="" type="checkbox"/> PLUMBING	<input type="checkbox"/> FENCE	<input type="checkbox"/> DRIVE APPROACH
<input type="checkbox"/> BACKFLOW	<input type="checkbox"/> BARRICADE	<input type="checkbox"/> ENERGY	<input type="checkbox"/> PAVING/GRADING
<input checked="" type="checkbox"/> ELECTRICAL	<input type="checkbox"/> FIRE SPRKLR	<input type="checkbox"/> SIGN	<input type="checkbox"/> SWIMMING POOL
<input type="checkbox"/> CUSTOMER SVC	<input type="checkbox"/> GREEN	<input type="checkbox"/> OTHER:	
<input checked="" type="checkbox"/> MECHANICAL	<input type="checkbox"/> FIRE ALARM	<input type="checkbox"/> LANDSCAPE	<input type="checkbox"/> LAWN SPRINKLER
<input type="checkbox"/> FLAMMABLE LIQUID			
All food service establishments require a grease interceptor to be installed on site. Is there a grease interceptor on site? <input type="checkbox"/> YES <input checked="" type="checkbox"/> NO			
The following is applicable to all applications for building permits that are accepted and routed for any reviews. As required by Texas Local Government Code Section 214.904, the City of Dallas will grant (Approve) or deny your building permit application to erect or improve a building or other structure no later than the 45 th day after the application is submitted. Denial of a permit application due to time constraints may be avoided by agreeing to allow the City the following additional time to review the application:			
I hereby agree to a deadline of 14 days to grant or deny the permit after the date of the approval of all of the following reviews, as applicable, where the applicant has provided the plans examiners the requested corrections, plans and actions; and, the contractor has been named on the permit:			
Zoning, Building Code, Electrical Code, Plumbing/Mechanical Code, Green Building Code, Health, Historical/Conservation District, Engineering/Flood Plain, Water Utilities, Fire Code, Landscaping and Aviation.			
If the permit is granted (Approved) within this deadline the City will retain and/or assess all fees. If the permit is denied within this deadline, the City will retain all plan review fees and 20 percent of the permit fees. If the permit application is not granted or denied within the agreed additional time of review, the City will refund any permit fees that have been collected and the City may not collect any permit fees associated with the application.			
<input checked="" type="checkbox"/> I AGREE. <input type="checkbox"/> I DO NOT AGREE.			
I UNDERSTAND THAT THIS PERMIT APPLICATION WILL EXPIRE IN 180 DAYS FROM THE APPLICATION DATE. I MAY REQUEST IN WRITING AN ADDITIONAL 180 DAY EXTENSION OF THE PERMIT APPLICATION PRIOR TO THE APPLICATION EXPIRATION. IF THE APPLICATION IS ALLOWED TO EXPIRE, IT MAY ONLY BE REACTIVATED BY THE FILING OF A NEW APPLICATION INCLUDING APPLICABLE PLANS AND FEES			
I HAVE CAREFULLY READ THE COMPLETED APPLICATION AND KNOW THE SAME IS TRUE AND CORRECT AND HEREBY AGREE THAT IF A PERMIT IS ISSUED ALL PROVISIONS OF THE CITY ORDINANCES AND STATE LAWS WILL BE COMPLIED WITH WHETHER HEREIN SPECIFIED OR NOT. I AM THE OWNER OF THE PROPERTY OR THE DULY AUTHORIZED AGENT. PERMISSION IS HEREBY GRANTED TO ENTER PREMISES AND MAKE ALL INSPECTIONS. I ALSO AFFIRM THAT THE EMAIL ADDRESS GIVEN ABOVE MAY BE USED FOR OFFICIAL COMMUNICATION CONCERNING THIS APPLICATION AND PERMIT.			
APPLICANT'S SIGNATURE [REDACTED]		DATE OF APPLICATION SUBMISSION 05-03-17	

ONE AND TWO FAMILY DWELLINGS REMODEL/RENOVATION



APPLICATION CHECKLIST AND REQUIRED DOCUMENTS

City of Dallas

By checking each requirement, you are stating that you have supplied correct and complete information. In the event that the required information is not contained in the submitted documents, you will be notified of the deficiency. Failure to supply the additional requested information within five (5) working days after notification may result in your application being delayed and eventually discarded. A new application, the original application, complete plans and a new checklist will be required for re-submittal for plan review. This re-submittal will be treated as a new application and will be processed in the order of receipt.

- 1. Completed permit application.
- 2. Two (2) copies of fully dimensioned building plans drawn to a standard scale and legible, which include:
 - Floor plans showing the location of all existing interior walls, walls to be removed and proposed new walls. Label all rooms.
 - Location of existing smoke detectors and proposed location of new smoke detectors when required.
 - For homes with fuel-fired appliances (i. e. natural gas), location of carbon monoxide alarms in accordance with Chapter 3, Dallas Residential Code.
 - Schedule of any doors and windows being replaced. Building elevations may be required for new openings or where there is a change of size of openings.
 - Engineered construction documents are required for engineered trusses or products and non-conventional construction (e. g. steel framing, ICF, etc.) or similar construction as defined in Chapter 3, Dallas Residential Code.
- 3. For any work affecting the exterior walls, two (2) copies of a site plan are required to include:
 - Legal description on site plans (lot, block and address). Show a North or plan North arrow.
 - Drawn to a standard scale and completely dimensioned plans. Show all property lines. Indicate length, metes, bounds, building lines and easements.
 - Label footprint (outline) of all structures including all projections beyond the foundation line, showing placement on the property and front, side and rear yard setbacks.
- 4. All aspects of the construction project complies with the Environmental Protection Agency (EPA) Lead; Renovation, Repair and Painting Program Rule; 40 CFR, Part 745.

ADDITIONAL REQUIREMENTS:

1. All documents submitted for review must be drawn to a standard scale, have a minimum text size of 3/32", and a minimum drawing sheet size of 11" x 17" and a maximum drawing sheet size of 36" x 48", "E" size.
2. For projects that impact the exterior of the building (walls, windows, doors, roof, etc.) and are located in a Conservation District, a Conservation District (CD) Work Review Form must first be completed and attached to the building permit application. A CD Work Review Form may be submitted to the Permit Center; 320 E. Jefferson Blvd., Room 105.
3. For projects that impact the exterior of the building (walls, windows, doors, roof, etc.) and are located in a Historic Overlay District, a Certificate of Appropriateness (C of A) must first be issued by the Landmark Commission. C of A applications may be filed at Current Planning; 1500 Marilla St., Room 5B North.
4. Permits may only be issued to a registered contractor with the proper licenses and/or other credentials.
5. For affected projects, a *Residential Energy Compliance Certificate* must be submitted prior to final inspection (effective September 1, 2016).

I, [REDACTED] have read the above information and acknowledge that all required documents have been provided.

Signature

[REDACTED]

Date

5/8/17

Please note that staff cannot accept incomplete applications or illegible construction documents.

DATE: 5/10/17
 EXPRESS PLAN REVIEW



City of Dallas

TYPE ACTIVITY
 CHANGE ORDER
 GENERAL CONSULTING

1705091064

**BUILDING INSPECTION DIVISION
 ADDENDUM APPLICATION**

STREET ADDRESS OF PROPOSED PROJECT <u>3534 Espanola Dr</u>		SUITE/BLDG/FLOOR NO	USE OF PROPERTY <u>residential</u>
ORIG. AL PERMIT NO <u>1705091064</u>	CERTIFICATE OF OCCUPANCY NO (IF APPLICABLE)		ORIGINAL PERMIT ISSUE DATE <u>5/9/17</u>
OWNER/TENANT [REDACTED]	ADDRESS [REDACTED]	CITY <u>Farmers Branch TX</u>	STATE <u>TX</u>
A [REDACTED]	COMPANY NAME	ZIP CODE <u>75234</u>	PHONE NO [REDACTED] FAX NO [REDACTED]
ADDRESS <u>13342 Glenside Dr.</u>	CITY <u>Farmers Branch TX</u>	STATE <u>TX</u>	ZIP CODE <u>75234</u>

DESCRIPTION OF PROPOSED REVISION <u>add edge interior partition wall</u>	ORIGINAL AREA	VALUATION (\$)	ORIG VALUATION
	ADDTL AREA		ADDTL COSTS
	REVISED AREA <u>0</u>		TOTAL VALUATION <u>0</u>

PLEASE INDICATE ALL TYPES OF WORK IN THIS PROJECT THAT WILL BE REVISED BY CHECKING THE APPROPRIATE BOX AND PROVIDE CONTRACTOR/SUBCONTRACTOR INFORMATION ON THE BACK OF THIS FORM. NOTE: AN AFFIDAVIT IS REQUIRED FOR THE SALE OR SERVING OF ALCOHOL.

- BUILDING PLUMBING FENCE DRIVE APPROACH BACKFLOW GREEN BUILDING
 ELECTRICAL FIRE SPRKLR SIGN SWIMMING POOL CUSTOMER SVC HEALTH
 MECHANICAL FIRE ALARM LANDSCAPE LAWN SPRINKLER FLAMMABLE LIQUID OTHER:

WILL ALCOHOL BE SOLD/SERVED? YES NO PERSONAL SERVICE LICENSE REQUIRED FOR THE PROPOSED USE? YES NO
 WILL THERE BE A DANCE FLOOR? YES NO ARE POTENTIALLY HAZARDOUS FOODS/OPEN FOODS BEING SOLD? YES NO

I HAVE CAREFULLY READ THE COMPLETED APPLICATION AND KNOW THE SAME IS TRUE AND CORRECT AND HEREBY AGREE THAT IF A PERMIT IS ISSUED ALL PROVISIONS OF THE CITY ORDINANCES AND STATE LAWS WILL BE COMPLIED WITH WHETHER HEREIN SPECIFIED OR NOT. I AM THE OWNER OF THE PROPERTY OR THE DULY AUTHORIZED AGENT. PERMISSION IS HEREBY GRANTED TO ENTER PREMISES AND MAKE ALL INSPECTIONS.

APPLICANT SIGNATURE
 [REDACTED]

FOR OFFICE USE ONLY

ZONING				BUILDING		MISCELLANEOUS	
LAND USE	TYPE OF WORK	BASE ZONING	PD	CONSTRUCTION TYPE	OCCUPANCY	ACTIVITY	OWN
<u>1111</u>	<u>1115</u>	<u>R75</u>		<u>VB</u>	<u>R-3</u>	<u>B</u>	<u>A</u>
LOT	BLOCK	REQUIRED PARKING	PROPOSED PARKING	SPRINKLER	OCCUPANT LOAD	FLOOD PLAIN	AIRPORT
<u>8</u>	<u>12461AA</u>						
LOT AREA	BDA	SUP	RAR	STORIES	DWELLING UNITS	SPECIAL INSPECTIONS	HISTORICAL
DIR	EARLY RELEASE	PARKING AGREEMENT		NUMBER BEDROOMS	NUMBER BATHROOMS	DRY	LL

REMARKS							FEE CALCULATIONS (\$)																																																		
<table border="1"> <thead> <tr> <th>ROUTE TO</th> <th>REVIEWER</th> <th>DATE</th> <th>ROUTE TO</th> <th>REVIEWER</th> <th>DATE</th> <th>COMMENTS</th> </tr> </thead> <tbody> <tr> <td>ZONING</td> <td></td> <td></td> <td>GREEN BUILDING</td> <td></td> <td></td> <td></td> </tr> <tr> <td>BUILDING</td> <td><i>[Signature]</i></td> <td><u>5/10/17</u></td> <td>FIRE</td> <td></td> <td></td> <td></td> </tr> <tr> <td>ELECTRICAL</td> <td></td> <td></td> <td>WATER</td> <td></td> <td></td> <td></td> </tr> <tr> <td>PLUMBING/ MECHANICAL</td> <td></td> <td></td> <td>HISTORICAL/ CONSERV DISTRICT</td> <td></td> <td></td> <td></td> </tr> <tr> <td>LANDSCAPING</td> <td></td> <td></td> <td>FLOOD PLAIN/ DRAINAGE</td> <td></td> <td></td> <td></td> </tr> <tr> <td>HEALTH</td> <td></td> <td></td> <td>AVIATION/TRAFFIC/ OTHER:</td> <td></td> <td></td> <td></td> </tr> </tbody> </table>							ROUTE TO	REVIEWER	DATE	ROUTE TO	REVIEWER	DATE	COMMENTS	ZONING			GREEN BUILDING				BUILDING	<i>[Signature]</i>	<u>5/10/17</u>	FIRE				ELECTRICAL			WATER				PLUMBING/ MECHANICAL			HISTORICAL/ CONSERV DISTRICT				LANDSCAPING			FLOOD PLAIN/ DRAINAGE				HEALTH			AVIATION/TRAFFIC/ OTHER:				PERMIT FEE	
							ROUTE TO	REVIEWER	DATE	ROUTE TO	REVIEWER	DATE	COMMENTS																																												
							ZONING			GREEN BUILDING																																															
							BUILDING	<i>[Signature]</i>	<u>5/10/17</u>	FIRE																																															
							ELECTRICAL			WATER																																															
							PLUMBING/ MECHANICAL			HISTORICAL/ CONSERV DISTRICT																																															
							LANDSCAPING			FLOOD PLAIN/ DRAINAGE																																															
							HEALTH			AVIATION/TRAFFIC/ OTHER:																																															
							PLAN REVIEW FEE																																																		
							EXPRESS PLAN REVIEW RATE: \$1,000 PER HOUR																																																		
HEALTH PERMIT FEE																																																									
RECORD CHANGE FEE																																																									
ADDENDUM FEE	<u>\$25.00</u>																																																								
OTHER FEES																																																									
TOTAL FEES	<u>\$25.00</u>																																																								

DATE: 5/20/17
 EXPRESS PLAN REVIEW



TYPE ACTIVITY
 CHANGE ORDER
 GENERAL CONSULTING

City of Dallas

BUILDING INSPECTION DIVISION
 ADDENDUM APPLICATION

1705091064

STREET ADDRESS OF PROPOSED PROJECT <u>3534 Espanola Dr</u>		SUITE/BLDG/FLOOR NO	USE OF PROPERTY
ORIGINAL PERMIT NO <u>1705091064</u>	CERTIFICATE OF OCCUPANCY NO (IF APPLICABLE)		ORIGINAL PERMIT ISSUE DATE
OWNER/TENANT [REDACTED]	ADDRESS [REDACTED]	CITY <u>Farmers Branch</u>	STATE <u>TX</u>
APPLICANT [REDACTED]	COMPANY NAME	E-MAIL ADDRESS	ZIP CODE <u>75234</u>
ADDRESS [REDACTED]	CITY <u>Farmers Branch</u>	STATE <u>TX</u>	ZIP CODE <u>75234</u>
DESCRIPTION OF PROPOSED REVISION <u>1. Add New window to bathroom</u> <u>2. New footing and brick to front of SFD</u> <u>1705091064</u>		CONST AREA (sq ft)	VALUATION (\$)
		ORIGINAL AREA	ORIG VALUATION
		ADDTL AREA	ADDTL COSTS
		REVISED AREA	TOTAL VALUATION

PLEASE INDICATE ALL TYPES OF WORK IN THIS PROJECT THAT WILL BE REVISED BY CHECKING THE APPROPRIATE BOX AND PROVIDE CONTRACTOR/SUBCONTRACTOR INFORMATION ON THE BACK OF THIS FORM. NOTE: AN AFFIDAVIT IS REQUIRED FOR THE SALE OR SERVING OF ALCOHOL.

BUILDING PLUMBING FENCE DRIVE APPROACH BACKFLOW GREEN BUILDING
 ELECTRICAL FIRE SPRKLR SIGN SWIMMING POOL CUSTOMER SVC HEALTH
 MECHANICAL FIRE ALARM LANDSCAPE LAWN SPRINKLER FLAMMABLE LIQUID OTHER:

WILL ALCOHOL BE SOLD/SERVED? YES NO PERSONAL SERVICE LICENSE REQUIRED FOR THE PROPOSED USE? YES NO
 WILL THERE BE A DANCE FLOOR? YES NO ARE POTENTIALLY HAZARDOUS FOODS/OPEN FOODS BEING SOLD? YES NO

I HAVE CAREFULLY READ THE COMPLETED APPLICATION AND KNOW THE SAME IS TRUE AND CORRECT AND HEREBY AGREE THAT IF A PERMIT IS ISSUED ALL PROVISIONS OF THE CITY ORDINANCES AND STATE LAWS WILL BE COMPLIED WITH WHETHER HEREIN SPECIFIED OR NOT. I AM THE OWNER OF THE PROPERTY OR THE DULY AUTHORIZED AGENT. PERMISSION IS HEREBY GRANTED TO ENTER PREMISES AND MAKE ALL INSPECTIONS.

APPLICANT SIGNATURE
 [REDACTED]

FOR OFFICE USE ONLY							
ZONING				BUILDING		MISCELLANEOUS	
LAND USE	TYPE OF WORK	BASE ZONING	PD	CONSTRUCTION TYPE	OCCUPANCY	ACTIVITY	OWN
<u>1111</u>	<u>1115</u>	<u>R7.5</u>		<u>T/B</u>	<u>R-3</u>	<u>B</u>	<u>A</u>
LOT	BLOCK	REQUIRED PARKING	PROPOSED PARKING	SPRINKLER	OCCUPANT LOAD	FLOOD PLAIN	AIRPORT
<u>8</u>	<u>12/6/14</u>						
LOT AREA	BDA	SUP	RAR	STORIES	DWELLING UNITS	SPECIAL INSPECTIONS	HISTORICAL
DIR	EARLY RELEASE	PARKING AGREEMENT		NUMBER BEDROOMS	NUMBER BATHROOMS	DRY	LL

REMARKS							FEE CALCULATIONS (\$)																																																		
<table border="1"> <thead> <tr> <th>ROUTE TO</th> <th>REVIEWER</th> <th>DATE</th> <th>ROUTE TO</th> <th>REVIEWER</th> <th>DATE</th> <th>COMMENTS</th> </tr> </thead> <tbody> <tr> <td>ZONING</td> <td>[Signature]</td> <td><u>05/19/17</u></td> <td>GREEN BUILDING</td> <td></td> <td></td> <td></td> </tr> <tr> <td>BUILDING</td> <td>[Signature]</td> <td><u>05/19/17</u></td> <td>FIRE</td> <td></td> <td></td> <td></td> </tr> <tr> <td>ELECTRICAL</td> <td></td> <td></td> <td>WATER</td> <td></td> <td></td> <td></td> </tr> <tr> <td>PLUMBING/MECHANICAL</td> <td></td> <td></td> <td>HISTORICAL/CONSERV DISTRICT</td> <td></td> <td></td> <td></td> </tr> <tr> <td>LANDSCAPING</td> <td></td> <td></td> <td>FLOOD PLAIN/DRAINAGE</td> <td></td> <td></td> <td></td> </tr> <tr> <td>HEALTH</td> <td></td> <td></td> <td>AVIATION/TRAFFIC/OTHER</td> <td></td> <td></td> <td></td> </tr> </tbody> </table>							ROUTE TO	REVIEWER	DATE	ROUTE TO	REVIEWER	DATE	COMMENTS	ZONING	[Signature]	<u>05/19/17</u>	GREEN BUILDING				BUILDING	[Signature]	<u>05/19/17</u>	FIRE				ELECTRICAL			WATER				PLUMBING/MECHANICAL			HISTORICAL/CONSERV DISTRICT				LANDSCAPING			FLOOD PLAIN/DRAINAGE				HEALTH			AVIATION/TRAFFIC/OTHER				PERMIT FEE	
							ROUTE TO	REVIEWER	DATE	ROUTE TO	REVIEWER	DATE	COMMENTS																																												
							ZONING	[Signature]	<u>05/19/17</u>	GREEN BUILDING																																															
							BUILDING	[Signature]	<u>05/19/17</u>	FIRE																																															
							ELECTRICAL			WATER																																															
							PLUMBING/MECHANICAL			HISTORICAL/CONSERV DISTRICT																																															
LANDSCAPING			FLOOD PLAIN/DRAINAGE																																																						
HEALTH			AVIATION/TRAFFIC/OTHER																																																						
PLAN REVIEW FEE																																																									
EXPRESS PLAN REVIEW RATE: \$1,000 PER HOUR																																																									
HEALTH PERMIT FEE																																																									
RECORD CHANGE FEE																																																									
ADDENDUM FEE	<u>\$25.00</u>																																																								
OTHER FEES																																																									
TOTAL FEES	<u>\$25.00</u>																																																								

DATE: 05/31/17

EXPRESS PLAN REVIEW



TYPE ACTIVITY

CHANGE ORDER

GENERAL CONSULTING

City of Dallas

BUILDING INSPECTION DIVISION
ADDENDUM APPLICATION

STREET ADDRESS OF PROPOSED PROJECT 3534 Espanola Dr		SUITE/BLDG/FLOOR NO	USE OF PROPERTY SFD	
ORIGINAL PERMIT NO 1705091064	CERTIFICATE OF OCCUPANCY NO (IF APPLICABLE)		ORIGINAL PERMIT ISSUE DATE	
CITY Farmers Branch TX		STATE TX	ZIP CODE 75234	
COMPANY NAME		E-MAIL ADDRESS		
ADDRESS Farmers Branch TX		CITY Farmers Branch TX	STATE TX	ZIP CODE 75234
DESCRIPTION OF PROPOSED REVISION Change dimensions in laundry closet Modify openings from living room to binning room		CONST AREA (sq ft) 1352	ORIGINAL AREA	ORIG VALUATION
		ADDTL AREA	ADDTL COSTS	
		REVISED AREA	TOTAL VALUATION	8,000.00

PLEASE INDICATE ALL TYPES OF WORK IN THIS PROJECT THAT WILL BE REVISED BY CHECKING THE APPROPRIATE BOX AND PROVIDE CONTRACTOR/SUBCONTRACTOR INFORMATION ON THE BACK OF THIS FORM. NOTE: AN AFFIDAVIT IS REQUIRED FOR THE SALE OR SERVING OF ALCOHOL.

BUILDING PLUMBING FENCE DRIVE APPROACH BACKFLOW GREEN BUILDING
 ELECTRICAL FIRE SPRKLR SIGN SWIMMING POOL CUSTOMER SVC HEALTH
 MECHANICAL FIRE ALARM LANDSCAPE LAWN SPRINKLER FLAMMABLE LIQUID OTHER:

WILL ALCOHOL BE SOLD/SERVED? YES NO PERSONAL SERVICE LICENSE REQUIRED FOR THE PROPOSED USE? YES NO

WILL THERE BE A DANCE FLOOR? YES NO ARE POTENTIALLY HAZARDOUS FOODS/OPEN FOODS BEING SOLD? YES NO

I HAVE CAREFULLY READ THE COMPLETED APPLICATION AND KNOW THE SAME IS TRUE AND CORRECT AND HEREBY AGREE THAT IF A PERMIT IS ISSUED ALL PROVISIONS OF THE CITY ORDINANCES AND STATE LAWS WILL BE COMPLIED WITH WHETHER HEREIN SPECIFIED OR NOT. I AM THE OWNER OF THE PROPERTY OR THE DULY AUTHORIZED AGENT. PERMISSION IS HEREBY GRANTED TO ENTER PREMISES AND MAKE ALL INSPECTIONS.

APPLICANT SIGNATURE

FOR OFFICE USE ONLY

ZONING				BUILDING		MISCELLANEOUS	
LAND USE	TYPE OF WORK	BASE ZONING	PD	CONSTRUCTION TYPE	OCCUPANCY	ACTIVITY	OWN
1111		R-7.5(A)		JB	R3	B	A.
LOT 8.	BLOCK 12/6144	REQUIRED PARKING	PROPOSED PARKING	SPRINKLER	OCCUPANT LOAD	FLOOD PLAIN	AIRPORT
LOT AREA	BDA	SUP	RAR	STORIES	DWELLING UNITS	SPECIAL INSPECTIONS	HISTORICAL
DIR	EARLY RELEASE	PARKING AGREEMENT		NUMBER BEDROOMS	NUMBER BATHROOMS	DRY	LL

REMARKS ADDENDUM #3

FEE CALCULATIONS (\$)

PERMIT FEE

PLAN REVIEW FEE

EXPRESS PLAN REVIEW RATE: \$1,000 PER HOUR

HEALTH PERMIT FEE

RECORD CHANGE FEE

ADDENDUM FEE 25.00

OTHER FEES

TOTAL FEES \$ 25.06

ROUTE TO	REVIEWER	DATE	ROUTE TO	REVIEWER	DATE	COMMENTS
ZONING			GREEN BUILDING			
BUILDING			FIRE			
ELECTRICAL			WATER			
PLUMBING/MECHANICAL			HISTORICAL/CONSERV DISTRICT			
LANDSCAPING			FLOOD PLAIN/DRAINAGE			
HEALTH			AVIATION/TRAFFIC/OTHER:			



City of Dallas

Customer Service Inspection Certification

Address of Inspection: 3534 ESPANOLA DR
Permit/Validation: #1705091064001

Upon inspection of the private water distribution facilities connected to the City of Dallas public water supply, I do hear certify that, to the best of my knowledge:

<u>Inspection</u>	<u>Compliance</u>	<u>Non-Compliance</u>
1. No direct connection between the public drinking water supply and a potential source of contamination exist. Potential sources of contamination are isolated from the public water system by an air gap or an appropriate backflow prevention assembly in accordance with State and Local regulations.	<input type="checkbox"/>	<input checked="" type="checkbox"/>
2. No cross-connection between the public drinking and a private water system exist. Where an actual air gap is not maintained between the public water supply and a private water supply, an approved reduced pressure-zone backflow prevention assembly is properly installed and service agreement exist for annual inspection and testing by a certified backflow device tester.	<input type="checkbox"/>	<input checked="" type="checkbox"/>
3. No connection exist which would allow the return of water used for condensing, cooling, or industrial processing back in to the public water supply	<input type="checkbox"/>	<input checked="" type="checkbox"/>
4. No pipe or pipe fitting which contains more than 8.0% lead exist in private water distribution facilities installed on or after July 1, 1988.	<input type="checkbox"/>	<input checked="" type="checkbox"/>
5. No solder or flux which contains more than 0.2% lead exist in private water distribution facilities on or after July 1, 1988.	<input type="checkbox"/>	<input checked="" type="checkbox"/>

Water service shall not be provided or restored to the private water distribution facilities until the above conditions are determined to be in compliance.

I further certify the following materials were used in the installation of the water distribution facilities:

Service Line	Lead	<input type="checkbox"/>	Copper	<input type="checkbox"/>	PVC	<input type="checkbox"/>	Other	<input type="checkbox"/>
Solder	Lead	<input type="checkbox"/>	Lead Free	<input type="checkbox"/>	Solvent Weld	<input type="checkbox"/>	Other	<input type="checkbox"/>

I recognize that this document shall become a permanent record of the City of Dallas and that I am legally responsible for the validity of the information I have provided.

Signature of C.S.I Inspector: _____ **Title:** ME/PL Inspector

Type of Registration: City Of Dallas **C.S.I Registration #:** 122247

Finalled Date: 10/19/2017



City of Dallas

Customer Service Inspection Certification

Address of Inspection: 3534 ESPANOLA DR
Permit/Validation: #1705091064001

Upon inspection of the private water distribution facilities connected to the City of Dallas public water supply, I do hear certify that, to the best of my knowledge:

<u>Inspection</u>	<u>Compliance</u>	<u>Non-Compliance</u>
1. No direct connection between the public drinking water supply and a potential source of contamination exist. Potential sources of contamination are isolated from the public water system by an air gap or an appropriate backflow prevention assembly in accordance with State and Local regulations.	<input checked="" type="checkbox"/>	<input type="checkbox"/>
2. No cross-connection between the public drinking and a private water system exist. Where an actual air gap is not maintained between the public water supply and a private water supply, an approved reduced pressure-zone backflow prevention assembly is properly installed and service agreement exist for annual inspection and testing by a certified backflow device tester.	<input checked="" type="checkbox"/>	<input type="checkbox"/>
3. No connection exist which would allow the return of water used for condensing, cooling, or industrial processing back in to the public water supply	<input checked="" type="checkbox"/>	<input type="checkbox"/>
4. No pipe or pipe fitting which contains more than 8.0% lead exist in private water distribution facilities installed on or after July 1, 1988.	<input checked="" type="checkbox"/>	<input type="checkbox"/>
5. No solder or flux which contains more than 0.2% lead exist in private water distribution facilities on or after July 1, 1988.	<input checked="" type="checkbox"/>	<input type="checkbox"/>

Water service shall not be provided or restored to the private water distribution facilities until the above conditions are determined to be in compliance.

I further certify the following materials were used in the installation of the water distribution facilities:

Service Line	Lead <input type="checkbox"/>	Copper <input type="checkbox"/>	PVC <input type="checkbox"/>	Other <input checked="" type="checkbox"/>
Solder	Lead <input type="checkbox"/>	Lead Free <input checked="" type="checkbox"/>	Solvent Weld <input type="checkbox"/>	Other <input type="checkbox"/>

I recognize that this document shall become a permanent record of the City of Dallas and that I am legally responsible for the validity of the information I have provided.

Signature of C.S.I Inspector: _____ **Title:** ME/PL Inspector

Type of Registration: City Of Dallas **C.S.I Registration #:** 122247

Finalled Date: 10/25/2017

Permit # 1705091064

Issue Date: 05/09/2017

Sustainable Construction and Development | Building Inspection Division | 214/948-4480 | www.dallascityhall.com

Address: **3534 ESPANOLA DR 75220**

Land Use Description: SINGLE FAMILY DWELLING

Work Description: INTERIOR REMODEL ONLY

Value Of Work: \$8,000.00

Owner Or Tenant: [REDACTED]
FARMERS BRANCH, TX 75234

Applicant: [REDACTED]
Contractor: FCL DALLAS ROOFING
Business Address: [REDACTED] FARMERS BRANCH, TX 75234
Telephone: [REDACTED] Fax:

Lot: 8	Block: 12/614	Zoning: R-7.5(A)	PDD:	SUP:
Historic Dist:	Consv Dist:	Pro Park:	Req Park:	Park Agrmt: N
Dwlg Units:	Stories:	New Area:	Lot Area: 8480	Total Area: 1352
Type Const: VB	Sprinkler:	Occ Code: R3	Occ Load:	
Inches Of Removed Trees:				

ALL WORK SUBJECT TO FIELD INSPECTOR APPROVAL

This document is issued on the basis of information furnished in the application and is subject to the provisions of all governing ordinances, which must be complied with, whether or not herein specified.

THIS DOCUMENT SHALL BE POSTED AT WORK SITE AND IS SUBJECT TO CANCELLATION UPON NOTICE.

Contractor's Authorization

Trade Type: Building

Sustainable Development and Construction | Building Inspection Division | www.dallascityhall.com

District Office NW

Validation #: 1705091064101
Address: 3534 ESPANOLA DR 75220
Issue Date: 05/09/2017
Land Use Description: SINGLE FAMILY DWELLING
Work Description: 1115-INTERIOR REMODEL ONLY

Authorized Date: 05/09/2017
Owner Or Tenant: [REDACTED]
FARMERS BRANCH, TX 75234
Applicant: [REDACTED]
Contractor: FCL DALLAS ROOFING
Business Address: [REDACTED]
Telephone: [REDACTED] Fax:

Lot:	8	Block:	12/6144	Zoning:	R-7.5(A)	PDD:	SUP:
Historic Dist:		Consv Dist:		Pro Park:		Req Park:	Park Agrmt: N
Dwg Units:		Stories:		New Area:		Lot Area: 8480	Total Area: 1352
Type Const:	VB	Sprinkler:		Occ Code: R3		Occ Load:	

For inspections call 214/670-5313, 24 hours. You will need your validation number 1705091064101 and one of the inspection types from the list below.

120 Pier, Foundation, Excavation	123 Floor Joists	127 Frame Walls
130 Frame All	132 Frame Other	140 Final

Your inspector is: Carlton King at [REDACTED]

Note: 7 AM cut-off for same day inspections!! Reinspection fees will be charged if the work is not ready or property is inaccessible. For partial inspection of area or additional assistance, call (214) 671-0720 from 8 AM to 4:30 PM Monday through Friday.

Contractor's Authorization

Trade Type: Plumbing

Sustainable Development and Construction | Building Inspection Division | www.dallascityhall.com

District Office NW

Validation #: 1705091064201
Address: 3534 ESPANOLA DR 75220
Issue Date: 05/09/2017
Land Use Description: SINGLE FAMILY DWELLING
Work Description: 2001-REMODEL EXISTING PLUMBING

Authorized Date: 05/16/2017
Owner Or Tenant: [REDACTED]
FARMERS BRANCH, TX 75234

Applicant: [REDACTED]
Contractor: GAMEZ PLUMBING
Business Address: 3234 CORAL ROCK LN,
Telephone: [REDACTED] Fax:

Lot: 8	Block: 12/6144	Zoning: R-7.5(A)	PDD:	SUP:
Historic Dist:	Consrv Dist:	Pro Park:	Req Park:	Park Agrmt: N
Dwlg Units:	Stories:	New Area:	Lot Area: 8480	Total Area: 1352
Type Const: VB	Sprinkler:	Occ Code: R3	Occ Load:	

For inspections call 214/670-5313, 24 hours. You will need your validation number 1705091064201 and one of the inspection types from the list below.

210 Utility service sewer-water-gas	212 Swimming Pool (Plumbing)	220 Rough below floor level, DWV, water, etc.
230 Rough above floor level, top out, shower pan	231 Temporary Heat	240 Final

Your inspector is: Reggie Slagle at [REDACTED]

Note: 7 AM cut-off for same day inspections!! Reinspection fees will be charged if the work is not ready or property is inaccessible. For partial inspection of area or additional assistance, call (214) 671-0720 from 8 AM to 4:30 PM Monday through Friday.

Contractor's Authorization

Trade Type: Electrical

Sustainable Development and Construction | Building Inspection Division | www.dallascityhall.com

District Office NW

Validation #: 1705091064301
Address: 3534 ESPANOLA DR 75220
Issue Date: 05/09/2017
Land Use Description: SINGLE FAMILY DWELLING
Work Description: 3009-ELECTRICAL REMODEL

Authorized Date: 05/15/2017
Owner Or Tenant: [REDACTED]
FARMERS BRANCH, TX 75234

Applicant: [REDACTED]
Contractor: ELECTRA PLUS
Business Address: [REDACTED]
Telephone: [REDACTED] Fax: 0 / -

Lot:	8	Block:	12/6144	Zoning:	R-7.5(A)	PDD:	SUP:
Historic Dist:		Consv Dist:		Pro Park:		Req Park:	Park Agrmt: N
Dwlg Units:		Stories:		New Area:		Lot Area: 8480	Total Area: 1352
Type Const:	VB	Sprinkler:		Occ Code: R3		Occ Load:	

For inspections call 214/670-5313, 24 hours. You will need your validation number 1705091064301 and one of the inspection types from the list below.

305 Structural Pool Shell	310 Electrical Service	311 Landscape Lighting (Underground)
312 Pool Bonding	314 T-Pole	320 Rough below floor level
321 Rough Walls	322 Rough Ceiling	323 (UFER) Concrete Encase Electrode
330 Rough all above floor level	340 Final	

Your inspector is: Mike Anguiano at [REDACTED]

Note: 7 AM cut-off for same day inspections!! Reinspection fees will be charged if the work is not ready or property is inaccessible. For partial inspection of area or additional assistance, call (214) 671-0720 from 8 AM to 4:30 PM Monday through Friday.



Permit # 1705091064

City of Dallas

Issue Date: 05/09/2017

Sustainable Construction and Development | Building Inspection Division | 214/948-4480 | www.dallascityhall.com

Address: 3534 ESPANOLA DR 75220

Land Use Description: SINGLE FAMILY DWELLING

Work Description: INTERIOR REMODEL ONLY

Value Of Work: \$8,000.00

Owner Or Tenant: [REDACTED]
FARMERS BRANCH, TX 75234

Applicant: [REDACTED]
Contractor: FCL DALLAS ROOFING
Business Address: [REDACTED] FARMERS BRANCH, TX 75234
Telephone: [REDACTED] **Fax:** [REDACTED]

Lot: 8	Block: 12/614	Zoning: R-7.5(A)	PDD:	SUP:
Historic Dist:	Consv Dist:	Pro Park:	Req Park:	Park Agrmt: N
Dwlg Units:	Stories:	New Area:	Lot Area: 8480	Total Area: 1352
Type Const: VB	Sprinkler:	Occ Code: R3	Occ Load:	
Inches Of Removed Trees:				

ALL WORK SUBJECT TO FIELD INSPECTOR APPROVAL

This document is issued on the basis of information furnished in the application and is subject to the provisions of all governing ordinances, which must be complied with, whether or not herein specified.

THIS DOCUMENT SHALL BE POSTED AT WORK SITE AND IS SUBJECT TO CANCELLATION UPON NOTICE.



City of Dallas

Contractor's Authorization

Trade Type: Building

Sustainable Development and Construction | Building Inspection Division | www.dallascityhall.com

District Office NW

Validation #: 1705091064101

Address: 3534 ESPANOLA DR 75220

Issue Date: 05/09/2017

Land Use Description: SINGLE FAMILY DWELLING

Work Description: 1115-INTERIOR REMODEL ONLY

Authorized Date: 05/09/2017

Owner Or Tenant: [REDACTED]

FARMERS BRANCH, TX 75234

Applicant: [REDACTED]

Contractor: FCL DALLAS ROOFING

Business Address: [REDACTED]

Telephone: [REDACTED] Fax:

Lot: 8	Block: 12/6144	Zoning: R-7.5(A)	PDD:	SUP:
Historic Dist:	Consv Dist:	Pro Park:	Req Park:	Park Agrmt: N
Dwlg Units:	Stories:	New Area:	Lot Area: 8480	Total Area: 1352
Type Const: VB	Sprinkler:	Occ Code: R3	Occ Load:	

For inspections call 214/670-5313, 24 hours. You will need your validation number 1705091064101 and one of the inspection types from the list below.

- | | | |
|----------------------------------|------------------|-----------------|
| 120 Pier, Foundation, Excavation | 123 Floor Joists | 127 Frame Walls |
| 130 Frame All | 132 Frame Other | 140 Final |

Your inspector is: Carlton King at [REDACTED]

Note: 7 AM cut-off for same day inspections!! Reinspection fees will be charged if the work is not ready or property is inaccessible. For partial inspection of area or additional assistance, call (214) 671-0720 from 8 AM to 4:30 PM Monday through Friday.



City of Dallas

Contractor's Authorization

Trade Type: Plumbing

Sustainable Development and Construction | Building Inspection Division | www.dallascityhall.com

District Office NW

Validation #: 1705091064201

Address: 3534 ESPANOLA DR 75220

Issue Date: 05/09/2017

Land Use Description: SINGLE FAMILY DWELLING

Work Description: 2001-REMODEL EXISTING PLUMBING

Authorized Date: 05/16/2017

Owner Or Tenant: [REDACTED]

FARMERS BRANCH, TX 75234

Applicant: [REDACTED]

Contractor: GAMEZ PLUMBING

Business Address: [REDACTED]

Telephone: [REDACTED] Fax: [REDACTED]

Lot: 8	Block: 12/6144	Zoning: R-7.5(A)	PDD:	SUP:
Historic Dist:	Consv Dist:	Pro Park:	Req Park:	Park Agrmt: N
Dwlg Units:	Stories:	New Area:	Lot Area: 8480	Total Area: 1352
Type Const: VB	Sprinkler:	Occ Code: R3	Occ Load:	

For inspections call 214/670-5313, 24 hours. You will need your validation number 1705091064201 and one of the inspection types from the list below.

- | | | |
|--|------------------------------|---|
| 210 Utility service sewer-water-gas | 212 Swimming Pool (Plumbing) | 220 Rough below floor level, DWV, water, etc. |
| 230 Rough above floor level, top out, shower pan | 231 Temporary Heat | 240 Final |

Your inspector is: Reggie Slagle at [REDACTED]

Note: 7 AM cut-off for same day inspections!! Reinspection fees will be charged if the work is not ready or property is inaccessible. For partial inspection of area or additional assistance, call (214) 671-0720 from 8 AM to 4:30 PM Monday through Friday.



City of Dallas

Contractor's Authorization

Trade Type: Mechanical

Sustainable Development and Construction | Building Inspection Division | www.dallascityhall.com

District Office NW

Validation #: 1705091064401

Address: 3534 ESPANOLA DR 75220

Issue Date: 05/09/2017

Land Use Description: SINGLE FAMILY DWELLING

Work Description: 4001-INSTALL NEW HVAC

Authorized Date: 07/12/2017

Owner Or Tenant: [REDACTED]

FARMERS BRANCH, TX 75234

Applicant: [REDACTED]

Contractor: A V EXCEL AIR SERVICES

Business Address: [REDACTED]

Telephone: [REDACTED] Fax: 469/533-0391

Lot: 8	Block: 12/6144	Zoning: R-7.5(A)	PDD:	SUP:
Historic Dist:	Consv Dist:	Pro Park:	Req Park:	Park Agrmt: N
Dwlg Units:	Stories:	New Area:	Lot Area: 8480	Total Area: 1352
Type Const: VB	Sprinkler:	Occ Code: R3	Occ Load:	

For inspections call 214/670-5313, 24 hours. You will need your validation number 1705091064401 and one of the inspection types from the list below.

- 420 Rough below floor
- 430 Rough above floor
- 431 Commercial kitchen exhaust
- 440 Final

Your inspector is: Reggie Slagle at [REDACTED]

Note: 7 AM cut-off for same day inspections!! Reinspection fees will be charged if the work is not ready or property is inaccessible. For partial inspection of area or additional assistance, call (214) 671-0720 from 8 AM to 4:30 PM Monday through Friday.



City of Dallas

Contractor's Authorization

Trade Type: Electrical

Sustainable Development and Construction | Building Inspection Division | www.dallascityhall.com

District Office NW

Validation #: 1705091064301

Address: 3534 ESPANOLA DR 75220

Issue Date: 05/09/2017

Land Use Description: SINGLE FAMILY DWELLING

Work Description: 3009-ELECTRICAL REMODEL

Authorized Date: 05/15/2017

Owner Or Tenant: [REDACTED]
FARMERS BRANCH, TX 75234

Applicant: [REDACTED]

Contractor: ELECTRA PLUS

Business Address: [REDACTED]

Telephone: [REDACTED] Fax: 0 / -

Lot: 8	Block: 12/6144	Zoning: R-7.5(A)	PDD:	SUP:
Historic Dist:	Consv Dist:	Pro Park:	Req Park:	Park Agrmt: N
Dwig Units:	Stories:	New Area:	Lot Area: 8480	Total Area: 1352
Type Const: VB	Sprinkler:	Occ Code: R3	Occ Load:	

For inspections call 214/670-5313, 24 hours. You will need your validation number 1705091064301 and one of the inspection types from the list below.

- | | | |
|---------------------------------|------------------------|--------------------------------------|
| 305 Structural Pool Shell | 310 Electrical Service | 311 Landscape Lighting (Underground) |
| 312 Pool Bonding | 314 T-Pole | 320 Rough below floor level |
| 321 Rough Walls | 322 Rough Ceiling | 323 (UFER) Concrete Encase Electrode |
| 330 Rough all above floor level | 340 Final | |

Your inspector is: Mike Anguiano at [REDACTED]

Note: 7 AM cut-off for same day inspections!! Reinspection fees will be charged if the work is not ready or property is inaccessible. For partial inspection of area or additional assistance, call (214) 671-0720 from 8 AM to 4:30 PM Monday through Friday.

**Job Edit with
Issue Date**

Master Permit

Job 105475209-002 (1705091064)

Building (BU) CS, PL, ME, EL 1115-INTERIOR REMODEL ONLY

Status:	Complete	Created By:	JLABORDA	Date Created:	May 09, 2017
		Date Issued:	May 09, 2017	Date Completed:	Dec 19, 2017
Parent Job:	105475209-001 (20170509 - 0122)				
Specific Location:					

Details

Access Control
Activity (B) Renovation
Address Lookup 3534 ESPANOLA DR
AddressType1
AddressType2
Airport
Alcohol N
Applicant Name Lookup... [REDACTED]
3534 ESPANOLA DR
DALLAS, TX 75234
[REDACTED]
Base Zoning R-7.5(A)
Bathrooms
Bedrooms
BI Flag N
BI Flag Comments
BI Flag Override N
Block 6144
Board of Adjustment N
CandoME N
CandoMR N
Conditions ALL WORK SUBJECT TO FIELD INSPECTOR APPROVAL
Construction Type VB
Consultant
Contractor Name... FCL DALLAS ROOFING
13342 GLENSIDE DR
FARMERS BRANCH, TX 75234
[REDACTED]
Contractor Registration Number
Dance Floor N
Deed Restriction
Description of Proposed Project INTERIOR REMODEL ONLY - REPLACE FRONT DOOR, ADD NEW BATHROOM, REPLACE DRYWALL, DAMAGE STUDS & SIDING, NEW AC UNIT
Development Impact Review
DevImpactCharge N
District 1
District Office OCMC
Doing Business As
Double Permit Fee N
Dry N
Dwelling Units
Email Notify [REDACTED]
Escarpment N
Flood Plain N
Fraction
GIS Flagged Area
GIS NSOName
Health Application Fee Total
Health Fee to Use
Health Permit Charged
Health Permit Number
Health Review N
Historic
Homestead Exemption Y
Job Value \$8000.00
Land Use (1111) SINGLE FAMILY DWELLING

Job 105475209-002 (1705091064)

Lot	8
Lot Area	8,480
Lot Area	8480 SQUARE FEET
MD Overlay	
Moratorium Override	N
New Construction Cost	
New Square Feet	
No Trades Allowed	N
Notify Applicant	N
Notify Owner	N
Number of Unity Agreements	
Occupancy	R3
Occupancy Load	
OverBlock	12
Override CA Requirement	N
Override Early Release Requirement	N
Override PDD/SUP Surcharge	N
Owner Address Lookup	3534 ESPANOLA DR , DALLAS TEXAS 752203638 UNITED STATES OF AMERICA
Owner Address Override	13342 GLENSIDE DR FARMERS BRANCH, TX 75234
Owner As Applicant	N
Owner As Contractor	N
Owner Code	PRIVATE
Owner EMail	
Owner Fax Number	
Owner Name Lookup	HALL E N
Owner Name Override	JOSE A FISCAL QUINTO
Owner Phone Number	
Parking Agreement	N
PDD	
Permit Type	Building (BU)
PIN/SSN	
Plan Review	Y
Plan Review Fee	150
Postage	N
Proposed Parking	
PWeb Is A Web Application	N
Reason CA Not Required	
Reason For Early Release Override	
Remodel Construction Cost	\$8000.00
Remodel Square Feet	1352
Required Parking	
Selling Potentially Hazardous Foods	N
Sprinkler	
Stories	
Suite 1	
Suite 2	
SUP	
TaxParcelLegal5	6144 012 008 1006144 012
Temporary Address	
Total Square Feet	1352
Work Code	1115-INTERIOR REMODEL ONLY
Work Description	

Details



Applicant: [REDACTED]
3534 ESPANOLA DR
DALLAS TX 75204 (214) 504-8100



Address: Tax Parcel
3534 ESPANOLA DR



Contractor: FCL DALLAS ROOFING
13342 GLENSIDE DR
FARMERS BRANCH TX 75044 (214) 504-8100



Parcel: 3534 ESPANOLA DR Mapsco:23-V
0000052309000000

Contractor Registration (FIL): Business Roofing (RO) - FCL DALLAS ROOFING - RO102598

Contractor Registration (FIL): Business Building (BU) - FCL DALLAS ROOFING - BU123566

Processes

Assigned To	Status	Outcome	Scheduled		Actual	
			Start	Completed	Start	Completed
Enter Permit Application Details						
John LaBorda	Complete	Details Entered	May 09, 2017		May 09, 2017 12:18:52	
Review Permit Application						
John LaBorda	Complete	Approved	May 09, 2017		May 09, 2017 12:19:00	
System Fee Collection						
SICASHIERINTERFACE	Complete	Partially Collected			May 09, 2017 12:39:39	
Auto generated System Fee Collection						
System Fee Collection						
SICASHIERINTERFACE	Complete	Collected			May 09, 2017 12:40:10	
Auto generated System Fee Collection						
Produce Permit Document						
POSSE system power user	Complete	Saved	May 09, 2017		May 09, 2017 12:40:10	
Setup Addendum Routings						
John LaBorda	Complete	Routings Selected	May 10, 2017		May 10, 2017 10:00:00	
Building Plans Review Monitor						
John LaBorda	Complete	Reviews Completed			May 10, 2017 10:01:57	
PR Building Code Review						
John LaBorda	Complete	Approved	May 10, 2017		May 10, 2017 10:01:59	
ADDING INTERIOR PARTITION WALLS TO CREATE A CLOSET FOR WASHER & DRYER						
Notify of Addendum						
Carlton King	Complete	Notified	May 10, 2017		May 10, 2017 10:31:54	
Notify Applicant of Plan Review Completion						
	Scheduled		May 10, 2017			
System Fee Collection						
SICASHIERINTERFACE	Complete	Collected			May 10, 2017 10:14:52	
Auto generated System Fee Collection						
Produce New Authorization and Permit						
POSSE system power user	Complete	Saved	May 15, 2017		May 15, 2017 10:21:42	
Produce New Authorization and Permit						
POSSE system power user	Complete	Saved	May 16, 2017		May 16, 2017 21:46:45	
Request Inspection						
DALLASIVR	Complete	Requested	May 18, 2017		May 17, 2017 22:11:24	
IVR Request on May 17, 2017.						
Perform Plumbing Inspection						
Reggie Slagle	Complete	Red Tag	May 18, 2017		May 18, 2017 15:12:34	
220 Rough below floor level, DWV, water, etc.						
Request Inspection						
DALLASIVR	Complete	Requested	May 18, 2017		May 17, 2017 22:12:10	
IVR Request on May 17, 2017.						
Perform Plumbing Inspection						
Reggie Slagle	Complete	Red Tag	May 18, 2017		May 18, 2017 15:11:55	
210 Utility service sewer-water-gas						
Setup Addendum Routings						
John LaBorda	Complete	Routings Selected	May 19, 2017		May 19, 2017 09:20:20	
Building Plans Review Monitor						
John LaBorda	Complete	Reviews Completed			May 19, 2017 09:21:46	

Job 105475209-002 (1705091064)

Assigned To	Status	Outcome	Scheduled		Actual	
			Start	Completed	Start	Completed
PR Building Code Review						
John LaBorda	Complete	Approved	May 19, 2017		May 19, 2017 09:20:36	
ADDENDUM - ADD NEW WINDOW TO BATHROOM AND BRICK TO FRONT OF THE HOUSE WITH FOUNDATION						
Notify of Addendum						
Carlton King	Complete	Notified	May 19, 2017		May 19, 2017 10:57:53	
Notify Applicant of Plan Review Completion						
	Scheduled		May 19, 2017			
System Fee Collection						
SICASHIERINTERFACE	Complete	Collected			May 19, 2017 09:32:29	
Auto generated System Fee Collection						
Request Inspection						
DALLASIVR	Complete	Requested	May 24, 2017		May 23, 2017 22:01:02	
IVR Request on May 23, 2017.						
Perform Plumbing Inspection						
Reggie Slagle	Complete	Green Tag	May 24, 2017		May 24, 2017 15:32:48	
220 Rough below floor level, DWV, water, etc.						
Request Inspection						
DALLASIVR	Complete	Requested	May 24, 2017		May 23, 2017 22:02:00	
IVR Request on May 23, 2017.						
Perform Plumbing Inspection						
Reggie Slagle	Complete	Green Tag	May 24, 2017		May 24, 2017 15:33:39	
210 Utility service sewer-water-gas						
Notify Utility Verification						
Reggie Slagle	Complete	Confirmed	May 24, 2017		May 25, 2017 08:10:47	
Relay - Single Family Sewer Release						
Setup Addendum Routings						
Carolina Yumet	Complete	Routings Selected	May 31, 2017		May 31, 2017 13:16:33	
ADDENDUM # 3						
Building Plans Review Monitor						
Carolina Yumet	Complete	Reviews Completed			May 31, 2017 13:18:29	
PR Building Code Review						
Carolina Yumet	Complete	Approved	May 31, 2017		May 31, 2017 13:17:35	
ADDENDUM # 3- CHANGE DIMENSIONS IN LAUNDRY CLOSET & MODIFY OPENINGS FROM LIVING ROOM TO DINING ROOM (ARCH)						
Notify of Addendum						
Carlton King	Complete	Notified	May 31, 2017		May 31, 2017 15:02:39	
Notify Applicant of Plan Review Completion						
	Scheduled		May 31, 2017			
System Fee Collection						
SICASHIERINTERFACE	Complete	Collected			May 31, 2017 13:27:00	
Auto generated System Fee Collection						
Request Inspection						
DALLASIVR	Complete	Requested	Jun 01, 2017		May 31, 2017 15:04:13	
IVR Request on May 31, 2017.						
Perform Building Inspection						
Carlton King	Complete	Red Tag	Jun 01, 2017		Jun 01, 2017 08:46:11	
132 Frame Other						
Request Inspection						
DALLASIVR	Complete	Requested	Jun 01, 2017		May 31, 2017 15:07:13	
IVR Request on May 31, 2017.						

Job 105475209-002 (1705091064)

Assigned To	Status	Outcome	Scheduled		Actual	
			Start	Completed	Start	Completed
Perform Building Inspection						
Carlton King 127 Frame Walls	Complete	Red Tag	Jun 01, 2017		Jun 01, 2017 08:45:34	
Request Inspection						
105401	Complete	Requested	Jun 06, 2017		Jun 05, 2017 14:54:35	
Perform Electrical Inspection						
Mike Anguiano 330 Rough all above floor level	Complete	Red Tag	Jun 06, 2017		Jun 06, 2017 14:24:31	
Request Inspection						
DALLASIVR IVR Request on Jun 12, 2017.	Complete	Requested	Jun 13, 2017		Jun 12, 2017 21:53:55	
Perform Plumbing Inspection						
Reggie Slagle 230 Rough above floor level, top out, shower pan	Complete	Red Tag	Jun 13, 2017		Jun 13, 2017 12:55:57	
Request Inspection						
DALLASIVR IVR Request on Jun 15, 2017.	Complete	Requested	Jun 15, 2017		Jun 15, 2017 06:26:13	
Perform Plumbing Inspection						
Reggie Slagle 230 Rough above floor level, top out, shower pan	Complete	Red Tag	Jun 15, 2017		Jun 15, 2017 14:50:07	
Request Inspection						
DALLASIVR IVR Request on Jun 18, 2017.	Complete	Requested	Jun 19, 2017		Jun 18, 2017 22:38:19	
Perform Plumbing Inspection						
Reggie Slagle 230 Rough above floor level, top out, shower pan	Complete	Green Tag	Jun 19, 2017		Jun 19, 2017 13:21:06	
Request Inspection						
DALLASIVR IVR Request on Jun 28, 2017.	Complete	Requested	Jun 29, 2017		Jun 28, 2017 13:00:45	
Perform Building Inspection						
Carlton King 132 Frame Other	Complete	Red Tag	Jun 29, 2017		Jun 29, 2017 10:54:31	
Request Inspection						
DALLASIVR IVR Request on Jun 28, 2017.	Complete	Requested	Jun 29, 2017		Jun 28, 2017 13:06:07	
Perform Building Inspection						
Carlton King 120 Pier, Foundation, Excavation	Complete	Red Tag	Jun 29, 2017		Jun 29, 2017 10:53:36	
Request Inspection						
DALLASIVR IVR Request on Jun 28, 2017.	Complete	Requested	Jun 29, 2017		Jun 28, 2017 13:07:18	
Perform Building Inspection						
Carlton King 130 Frame All	Complete	Red Tag	Jun 29, 2017		Jun 29, 2017 10:54:49	
Request Inspection						
DALLASIVR IVR Request on Jun 28, 2017.	Complete	Requested	Jun 29, 2017		Jun 28, 2017 13:08:22	
Perform Building Inspection						
Carlton King 127 Frame Walls	Complete	Red Tag	Jun 29, 2017		Jun 29, 2017 10:54:09	

Job 105475209-002 (1705091064)

Assigned To	Status	Outcome	Scheduled		Actual	
			Start	Completed	Start	Completed
Request Inspection						
DALLASIVR	Complete	Requested	Jul 03, 2017		Jun 30, 2017 21:52:33	
IVR Request on Jun 30, 2017.						
Perform Building Inspection						
Jimmy Potter	Complete	Red Tag	Jul 03, 2017		Jul 03, 2017 08:13:46	
127 Frame Walls						
Request Inspection						
DALLASIVR	Complete	Requested	Jul 03, 2017		Jun 30, 2017 21:53:49	
IVR Request on Jun 30, 2017.						
Perform Building Inspection						
Jimmy Potter	Complete	Red Tag	Jul 03, 2017		Jul 03, 2017 08:14:09	
132 Frame Other						
Request Inspection						
DALLASIVR	Complete	Requested	Jul 07, 2017		Jul 06, 2017 07:03:05	
IVR Request on Jul 06, 2017.						
Perform Building Inspection						
Carlton King	Complete	Red Tag	Jul 07, 2017		Jul 07, 2017 08:24:18	
127 Frame Walls						
Request Inspection						
DALLASIVR	Complete	Requested	Jul 07, 2017		Jul 06, 2017 07:04:23	
IVR Request on Jul 06, 2017.						
Perform Building Inspection						
Carlton King	Complete	Red Tag	Jul 07, 2017		Jul 07, 2017 08:15:11	
132 Frame Other						
Request Inspection						
DALLASIVR	Complete	Requested	Jul 07, 2017		Jul 06, 2017 07:05:25	
IVR Request on Jul 06, 2017.						
Perform Building Inspection						
Carlton King	Complete	Red Tag	Jul 07, 2017		Jul 07, 2017 08:24:00	
130 Frame All						
Request Inspection						
DALLASIVR	Complete	Requested	Jul 07, 2017		Jul 06, 2017 07:06:23	
IVR Request on Jul 06, 2017.						
Perform Building Inspection						
Carlton King	Complete	Red Tag	Jul 07, 2017		Jul 07, 2017 08:24:34	
120 Pier, Foundation, Excavation						
Request Inspection						
DALLASIVR	Complete	Requested	Jul 10, 2017		Jul 09, 2017 15:00:18	
IVR Request on Jul 09, 2017.						
Perform Electrical Inspection						
Mike Anguiano	Complete	Green Tag	Jul 10, 2017		Jul 10, 2017 12:15:21	
330 Rough all above floor level						
Request Inspection						
Melanee Gonzalez	Complete	Requested	Jul 11, 2017		Jul 10, 2017 15:02:50	
Perform Building Inspection						
Carlton King	Complete	Red Tag	Jul 11, 2017		Jul 11, 2017 09:15:20	
130 Frame All						
Produce New Authorization and Permit						
POSSE system power user	Complete	Saved	Jul 12, 2017		Jul 12, 2017 10:04:49	

Job 105475209-002 (1705091064)

Assigned To	Status	Outcome	Scheduled		Actual	
			Start	Completed	Start	Completed
Request Inspection						
Melanee Gonzalez	Complete	Requested	Jul 14, 2017		Jul 13, 2017 08:00:53	
Perform Building Inspection						
Carlton King	Complete	Red Tag	Jul 14, 2017		Jul 14, 2017 08:17:03	
130 Frame All						
Request Inspection						
9513801	Complete	Requested	Jul 18, 2017		Jul 17, 2017 10:44:02	
Perform Mechanical Inspection						
Dale Taylor	Complete	Green Tag	Jul 18, 2017		Jul 18, 2017 11:54:55	
430 Rough above floor						
Request Inspection						
Melanee Gonzalez	Complete	Requested	Jul 19, 2017		Jul 18, 2017 14:06:22	
Perform Building Inspection						
Carlton King	Complete	Green Tag	Jul 19, 2017		Jul 19, 2017 13:40:02	
130 Frame All						
Request Inspection						
DALLASIVR	Complete	Requested	Oct 19, 2017		Oct 18, 2017 20:01:55	
IVR Request on Oct 18, 2017.						
Perform Plumbing Inspection						
Randall McLemore	Complete	Red Tag	Oct 19, 2017		Oct 19, 2017 12:49:16	
240 Final (Final)						
Perform Customer Service Inspection						
Randall McLemore	Complete	Red Tag	Oct 19, 2017		Oct 19, 2017 12:48:11	
240 Final (Final)						
Send CSI Report						
POSSE system power user	Complete	Sent			Oct 19, 2017 12:48:12	
Request Inspection						
DALLASIVR	Complete	Requested	Oct 25, 2017		Oct 24, 2017 21:42:27	
IVR Request on Oct 24, 2017.						
Perform Plumbing Inspection						
Randall McLemore	Complete	Green Tag	Oct 25, 2017		Oct 25, 2017 15:21:26	
240 Final (Final)						
Perform Customer Service Inspection						
Randall McLemore	Complete	Green Tag	Oct 25, 2017		Oct 25, 2017 15:19:59	
240 Final (Final)						
Send CSI Report						
POSSE system power user	Complete	Sent			Oct 25, 2017 15:20:00	
Notify Utility Verification						
Randall McLemore	Complete	Confirmed	Oct 25, 2017		Oct 26, 2017 08:23:53	
Gas Relay Gas Release						
Request Inspection						
DALLASIVR	Complete	Requested	Nov 09, 2017		Nov 08, 2017 20:57:24	
IVR Request on Nov 08, 2017.						
Perform Electrical Inspection						
Mike Anguiano	Complete	Green Tag	Nov 09, 2017		Nov 09, 2017 12:04:56	
310 Electrical Service						
Notify Utility Verification						
Mike Anguiano	Complete	Confirmed	Nov 09, 2017		Nov 09, 2017 16:05:29	
C-Perm Electrical Release						

Job 105475209-002 (1705091064)

Assigned To	Status	Outcome	Scheduled		Actual	
			Start	Completed	Start	Completed
Request Inspection						
DALLASIVR	Complete	Requested	Dec 08, 2017		Dec 07, 2017 18:19:10	
IVR Request on Dec 07, 2017.						
Perform Electrical Inspection						
Mike Anguiano	Complete	Green Tag	Dec 08, 2017		Dec 08, 2017 15:55:28	
340 Final (Final)						
Notify Utility Verification						
Mike Anguiano	Complete	Confirmed	Dec 08, 2017		Dec 11, 2017 08:33:11	
Perm Electrical Release						
Request Inspection						
Melanee Gonzalez	Complete	Requested	Dec 13, 2017		Dec 12, 2017 12:58:16	
Perform Mechanical Inspection						
Randall McLemore	Complete	Red Tag	Dec 13, 2017		Dec 13, 2017 10:26:48	
440 Final (Final)						
Request Inspection						
Melanee Gonzalez	Complete	Requested	Dec 18, 2017		Dec 15, 2017 08:27:23	
Perform Mechanical Inspection						
Randall McLemore	Complete	Green Tag	Dec 18, 2017		Dec 18, 2017 14:28:35	
440 Final (Final)						
Request Inspection						
Melanee Gonzalez	Complete	Requested	Dec 18, 2017		Dec 15, 2017 08:29:32	
Perform Building Inspection						
Carlton King	Complete	Red Tag	Dec 18, 2017		Dec 18, 2017 08:38:31	
140 Final (Final)						
Request Inspection						
Melanee Gonzalez	Complete	Requested	Dec 19, 2017		Dec 18, 2017 15:25:05	
Perform Building Inspection						
Carlton King	Complete	Green Tag	Dec 19, 2017		Dec 19, 2017 10:43:38	
140 Final (Final)						
System Decision						
Carlton King	Complete	Completed	Dec 19, 2017		Dec 19, 2017 10:43:38	

Inspections

Relationship: Perform Building Inspection (EXT):
Completed Jun 29, 2017
Inspection Comments Need electrical inspection
Inspection Type 130 Frame All
Inspector CAKING
Result Red Tag
Scheduled Jun 29, 2017

Relationship: Perform Building Inspection (EXT):
Completed Jul 14, 2017
Inspection Comments need mechanical rough
Inspection Type 130 Frame All
Inspector CAKING
Result Red Tag
Scheduled Jul 14, 2017

Relationship: Perform Building Inspection (EXT):
Completed Jul 07, 2017
Inspection Comments need electrical rough
Inspection Type 127 Frame Walls
Inspector CAKING
Result Red Tag
Scheduled Jul 07, 2017

Relationship: Perform Building Inspection (EXT):
Completed Jun 29, 2017
Inspection Comments No foundation work
Inspection Type 120 Pier, Foundation, Excavation
Inspector CAKING
Result Red Tag
Scheduled Jun 29, 2017

Relationship: Perform Building Inspection (EXT):
Completed Jul 07, 2017
Inspection Comments need electrical rough
Inspection Type 130 Frame All
Inspector CAKING
Result Red Tag
Scheduled Jul 07, 2017

Relationship: Perform Building Inspection (EXT):
Completed Jun 29, 2017
Inspection Comments Need electrical inspection
Inspection Type 127 Frame Walls
Inspector CAKING
Result Red Tag
Scheduled Jun 29, 2017

Relationship: Perform Building Inspection (EXT):
Completed Jul 19, 2017
Inspection Comments Framing ok
Inspection Type 130 Frame All
Inspector CAKING
Result Green Tag
Scheduled Jul 19, 2017

Relationship: Perform Building Inspection (EXT):
Completed Jul 07, 2017
Inspection Comments need electrical rough

Job 105475209-002 (1705091064)

Relationship: Perform Building Inspection (EXT):
Inspection Type 132 Frame Other
Inspector CAKING
Result Red Tag
Scheduled Jul 07, 2017

Relationship: Perform Building Inspection (EXT):
Completed Jun 01, 2017
Inspection Comments need electrical and plumbing rough
Inspection Type 127 Frame Walls
Inspector CAKING
Result Red Tag
Scheduled Jun 01, 2017

Relationship: Perform Building Inspection (EXT):
Completed Dec 19, 2017
Inspection Comments Final ok
Inspection Type 140 Final (Final)
Inspector CAKING
Result Green Tag
Scheduled Dec 19, 2017

Relationship: Perform Building Inspection (EXT):
Completed Dec 18, 2017
Inspection Comments open trade
Inspection Type 140 Final (Final)
Inspector CAKING
Result Red Tag
Scheduled Dec 18, 2017

Relationship: Perform Electrical Inspection (EXT):
Completed Jul 10, 2017
Inspection Comments rough all above ok
Inspection Type 330 Rough all above floor level
Inspector MANGUIANO
Result Green Tag
Scheduled Jul 10, 2017

Relationship: Perform Electrical Inspection (EXT):
Completed Jun 06, 2017
Inspection Comments Need to post site management sign including rest breaks section.
Inspection Type 330 Rough all above floor level
Inspector MANGUIANO
Result Red Tag
Scheduled Jun 06, 2017

Relationship: Perform Electrical Inspection (EXT):
Completed Dec 08, 2017
Inspection Comments EL final ok
Inspection Type 340 Final (Final)
Inspector MANGUIANO
Result Green Tag
Scheduled Dec 08, 2017

Relationship: Perform Electrical Inspection (EXT):
Completed Nov 09, 2017
Inspection Comments 310 power release ok
Inspection Type 310 Electrical Service
Inspector MANGUIANO
Result Green Tag
Scheduled Nov 09, 2017

Job 105475209-002 (1705091064)

Relationship: Notify Utility Verification (EXT):
Completed May 25, 2017
Inspection Type Notify Utility Verification
Result Confirmed
Scheduled May 24, 2017

Relationship: Notify Utility Verification (EXT):
Completed Nov 09, 2017
Inspection Type Notify Utility Verification
Result Confirmed
Scheduled Nov 09, 2017

Relationship: Notify Utility Verification (EXT):
Completed Oct 26, 2017
Inspection Type Notify Utility Verification
Result Confirmed
Scheduled Oct 25, 2017

Relationship: Notify Utility Verification (EXT):
Completed Dec 11, 2017
Inspection Type Notify Utility Verification
Result Confirmed
Scheduled Dec 08, 2017

Relationship: Perform Customer Service Inspection (EXT):
Completed Oct 19, 2017
Inspection Comments Need PL final
Inspection Type 240 Final (Final)
Inspector RMCLEMORE
Result Red Tag
Scheduled Oct 19, 2017

Relationship: Perform Customer Service Inspection (EXT):
Completed Oct 25, 2017
Inspection Comments CSI OK
Inspection Type 240 Final (Final)
Inspector RMCLEMORE
Result Green Tag
Scheduled Oct 25, 2017

Relationship: Perform Mechanical Inspection (EXT):
Completed Jul 18, 2017
Inspection Comments duct dryer vent rrexhaust cond drain
Inspection Type 430 Rough above floor
Inspector DTAYLOR
Result Green Tag
Scheduled Jul 18, 2017

Relationship: Perform Mechanical Inspection (EXT):
Completed Dec 18, 2017
Inspection Comments Final ok
Inspection Type 440 Final (Final)
Inspector RMCLEMORE
Result Green Tag
Scheduled Dec 18, 2017

Relationship: Perform Mechanical Inspection (EXT):
Completed Dec 13, 2017
Inspection Comments Need overflow switch for condensate. Condensate must drain to approved location. Need locking caps
Inspection Type 440 Final (Final)
Inspector RMCLEMORE
Result Red Tag

Job 105475209-002 (1705091064)

Relationship: Perform Mechanical Inspection (EXT):
Scheduled Dec 13, 2017

Relationship: Perform Plumbing Inspection (EXT):
Completed May 18, 2017
Inspection Comments Gas test down
Inspection Type 220 Rough below floor level, DWV, water, etc.
Inspector RSLAGLE
Result Red Tag
Scheduled May 18, 2017

Relationship: Perform Plumbing Inspection (EXT):
Completed Jun 15, 2017
Inspection Comments Need backing around shower pan
Inspection Type 230 Rough above floor level, top out, shower pan
Inspector RSLAGLE
Result Red Tag
Scheduled Jun 15, 2017

Relationship: Perform Plumbing Inspection (EXT):
Completed May 18, 2017
Inspection Comments Gas test down
Inspection Type 210 Utility service sewer-water-gas
Inspector RSLAGLE
Result Red Tag
Scheduled May 18, 2017

Relationship: Perform Plumbing Inspection (EXT):
Completed Jun 19, 2017
Inspection Comments Topout ok-dwv,domestic water,gas,40 mil pan
Inspection Type 230 Rough above floor level, top out, shower pan
Inspector RSLAGLE
Result Green Tag
Scheduled Jun 19, 2017

Relationship: Perform Plumbing Inspection (EXT):
Completed May 24, 2017
Inspection Comments Sewer,water service and gas service
Inspection Type 210 Utility service sewer-water-gas
Inspector RSLAGLE
Result Green Tag
Scheduled May 24, 2017

Relationship: Perform Plumbing Inspection (EXT):
Completed Jun 13, 2017
Inspection Comments Need backing around shower pan-slope 1/4" per foot to drain, under pan-retest pan
Inspection Type 230 Rough above floor level, top out, shower pan
Inspector RSLAGLE
Result Red Tag
Scheduled Jun 13, 2017

Relationship: Perform Plumbing Inspection (EXT):
Completed May 24, 2017
Inspection Comments Rough ok-dwv,domestic water,gas
Inspection Type 220 Rough below floor level, DWV, water, etc.
Inspector RSLAGLE
Result Green Tag
Scheduled May 24, 2017

Relationship: Perform Plumbing Inspection (EXT):
Completed Oct 19, 2017
Inspection Comments Need lower combustion air for w/h needs whas on all self closing valves

Job 105475209-002 (1705091064)

Relationship: Perform Plumbing Inspection (EXT):
Inspection Type 240 Final (Final)
Inspector RMCLEMORE
Result Red Tag
Scheduled Oct 19, 2017

Relationship: Perform Plumbing Inspection (EXT):
Completed Oct 25, 2017
Inspection Comments Final ok
Inspection Type 240 Final (Final)
Inspector RMCLEMORE
Result Green Tag
Scheduled Oct 25, 2017

Relationship: Perform Building Inspection (EXT):
Completed Jul 03, 2017
Inspection Comments Need electrical inspection
Inspection Type 132 Frame Other
Inspector JPOTTER
Result Red Tag
Scheduled Jul 03, 2017

Relationship: Perform Building Inspection (EXT):
Completed Jul 11, 2017
Inspection Comments No city plans, seal all penetrations
Inspection Type 130 Frame All
Inspector CAKING
Result Red Tag
Scheduled Jul 11, 2017

Relationship: Perform Building Inspection (EXT):
Completed Jun 29, 2017
Inspection Comments Need electrical inspection
Inspection Type 132 Frame Other
Inspector CAKING
Result Red Tag
Scheduled Jun 29, 2017

Relationship: Perform Building Inspection (EXT):
Completed Jun 01, 2017
Inspection Comments need electrical and plumbing rough
Inspection Type 132 Frame Other
Inspector CAKING
Result Red Tag
Scheduled Jun 01, 2017

Relationship: Perform Building Inspection (EXT):
Completed Jul 03, 2017
Inspection Comments Need electrical inspection
Inspection Type 127 Frame Walls
Inspector JPOTTER
Result Red Tag
Scheduled Jul 03, 2017

Relationship: Perform Building Inspection (EXT):
Completed Jul 07, 2017
Inspection Comments no foundation work being done
Inspection Type 120 Pier, Foundation, Excavation
Inspector CAKING
Result Red Tag
Scheduled Jul 07, 2017

Trades

Relationship: Trade Permit:
Contr. #
Contractor... A V EXCEL AIR SERVICES
Finaled Y
Last Update By Randall McLemore
PIN
Removed N
Type Mechanical (ME)
Validation Number 1705091064401
Withdrawn N
Work Description 4001-INSTALL NEW HVAC

Relationship: Primary Trade:
Contr. #
Contractor... FCL DALLAS ROOFING
Finaled Y
Last Update By Carlton King
PIN
Removed N
Type Building (BU)
Validation Number 1705091064101
Withdrawn N
Work Description 1115-INTERIOR REMODEL ONLY

Relationship: Trade Permit:
Contr. #
Contractor... ELECTRA PLUS
Finaled Y
Last Update By Mike Anguiano
PIN
Removed N
Type Electrical (EL)
Validation Number 1705091064301
Withdrawn N
Work Description 3009-ELECTRICAL REMODEL

Relationship: Trade Permit:
Contr. #
Contractor...
Finaled Y
Last Update By Randall McLemore
PIN
Removed N
Type Customer Service (CS)
Validation Number 1705091064001
Withdrawn N
Work Description

Relationship: Trade Permit:
Contr. #
Contractor... GAMEZ PLUMBING
Finaled Y
Last Update By Randall McLemore
PIN
Removed N
Type Plumbing (PL)
Validation Number 1705091064201

Job 105475209-002 (1705091064)

Relationship: Trade Permit:
 Withdrawn N
 Work Description 2001-REMODEL EXISTING PLUMBING

Fees

Description	Posted Date	Amount	Tax	Total	Balance
Remodel Building Permit Fee, Residential		\$400.00	\$0.00	\$400.00	\$0.00
Receipt Number: 355614	\$60.00	(\$60.00)	\$0.00	(\$60.00)	
Receipt Number: 355615	\$505.00	(\$340.00)	\$0.00	(\$340.00)	
Customer Service Filing Fee		\$15.00	\$0.00	\$15.00	\$0.00
Receipt Number: 355615	\$505.00	(\$15.00)	\$0.00	(\$15.00)	
Building Plan Review Fee		\$150.00	\$0.00	\$150.00	\$0.00
Receipt Number: 355615	\$505.00	(\$150.00)	\$0.00	(\$150.00)	
Addendum Plan Review Fee		\$25.00	\$0.00	\$25.00	\$0.00
Receipt Number: 355859	\$25.00	(\$25.00)	\$0.00	(\$25.00)	
Addendum Plan Review Fee		\$25.00	\$0.00	\$25.00	\$0.00
Receipt Number: 358009	\$25.00	(\$25.00)	\$0.00	(\$25.00)	
Addendum Plan Review Fee		\$25.00	\$0.00	\$25.00	\$0.00
Receipt Number: 360275	\$25.00	(\$25.00)	\$0.00	(\$25.00)	
					\$0.00

Holds

Document List

Relationship:	Files:	
Created By		JLABORDA
Created Date		May 9, 2017
Description		DRAWING
Last Update By		JLABORDA
Subject		DRAWING
Type		PLAN
Relationship:	Files:	
Created By		JLABORDA
Created Date		May 19, 2017
Description		ADDENDUM APPLICATION #2
Last Update By		JLABORDA
Subject		ADDENDUM APPLICATION #2
Type		DOCUMENT
Relationship:	Report:	
Created Date		Jul 12, 2017
Description		Master Permit and Contractor
Last Update By		PSERVERONBASE
Relationship:	Files:	
Created By		JLABORDA
Created Date		May 9, 2017
Description		PERMIT APPLICATION
Last Update By		JLABORDA
Subject		PERMIT APPLICATION
Type		DOCUMENT
Relationship:	Files:	
Created By		JLABORDA
Created Date		May 10, 2017
Description		ADDENDUM DRAWING
Last Update By		JLABORDA
Subject		ADDENDUM DRAWINGS
Type		PLAN
Relationship:	Report:	
Created Date		May 31, 2017
Description		Master Permit and Contractor Authorization
Last Update By		JHERNAN
Relationship:	Report:	
Created Date		Oct 25, 2017
Description		Customer Service Inspection Form
Last Update By		PSERVERONBASE
Relationship:	Files:	
Created By		JLABORDA
Created Date		May 10, 2017
Description		ADDENDUM APPLICATION
Last Update By		JLABORDA
Subject		ADDENDUM APPLICATION
Type		DOCUMENT
Relationship:	Files:	
Created By		JJUAREZ
Created Date		May 31, 2017
Description		
Last Update By		JJUAREZ

Job 105475209-002 (1705091064)

Relationship: Files:
Subject: ADDENDUM #3
Type:

Relationship: Report:
Created Date: Oct 19, 2017
Description: Customer Service Inspection Form
Last Update By: PSERVERONBASE

Approved Plans

Project

Job	Type	Created	Issued	Completed	Status
105475209-001	Customer Log-In	May 09, 2017		May 09, 2017	Complete
	Time Registered: 11:49:56 am Time Served: 12:04:33 pm Registration Type: Permit Center				
105475209-002	Master Permit	May 09, 2017	May 09, 2017	Dec 19, 2017	Complete
	Building (BU) CS, PL, ME, EL 1115-INTERIOR REMODEL ONLY				

Airport	
Base Zoning	R-7.5(A)
BI Flag	N
BI Flag Comments	
Block	12/6144
Board of Adjustment	N
Census Tract	0098.02
Council District	2
Deed Restriction	
Development Impact Review	
DevImpactCharge	N
District	1
Dry	N
Escarpment	N
Flood Plain	N
GIS Flagged Area	
GIS NSOName	
GISConsvDist	
Historic	
Homestead Exemption	Y
IsBuildingProject	N
Lot	8
Lot Area	8480 SQUARE FEET
Mapsco	23-V
Parking Agreement	N
ParkingAgreementAFIL	
ParkingAgreementBFIL	
PD/SUP/Deed Restriction Surcharge Fee	\$0.00
PDD	
SUP	
Zip Code	75220

Notes

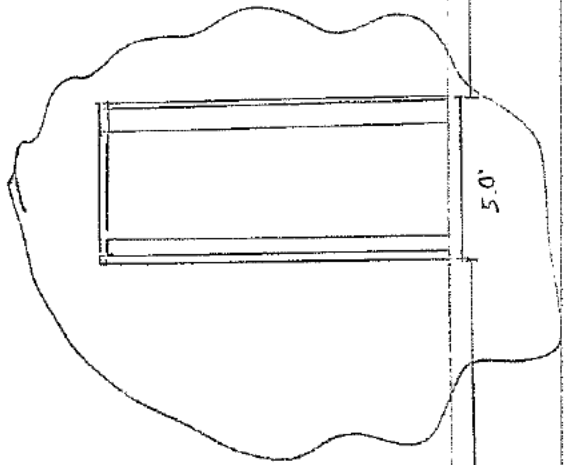
Audit

Addressing	N
Building Comments	
Credit Development Fee	N
Development Meeting Fee	
DevelopmentDate	
Electrical Code Comments	
Engineering Drainage Comments	
Engineering Water Comments	
Expedited Plan Review	N
Express Charge Fee	N
Final Total No Credit	0
Final Total With Credit	0
Fire Protection	N
Fire Sprinkler Plan Review	N
Fire Sprinkler Plan Review Fee	
Formal Drainage	N
Green Comments	
Historic Comments	
IsDevelopmentMeeting	N
Landscaping Comments	
License Abandonment	N
Mechanical/Plumbing Comments	
Mitigation	N
Overtime Review	N
Parking	N
Partial Team Review	N
Plan Review	Y
Platting/Early Release	N
Real Estate Comments	
Rezoning	N
Sanitarian Comments	
Subdivision Comments	
Substandard Water	N
TIF Comments	
Upload Allow	N
Upload Docs	Y
Zoning Comments	

SUBJECT TO FIELD INSPECTOR'S APPROVAL

COMPOSITION ROOF

NEW FRONT DOOR w/ (2) SIDE LITE



PERMITS REVIEWED BY THE BUILDING DEPARTMENT, HAWAIIAN ISLANDS, DEPARTMENT OF CONSTRUCTION, HONOLULU, HAWAII. THESE PERMITS WERE ISSUED BY [Redacted] BY [Redacted] THE PERMIT IS SUBJECT PERMIT THE CITY OF HONOLULU, HAWAII.

17.6'







5.0'




11.0'

33.6'

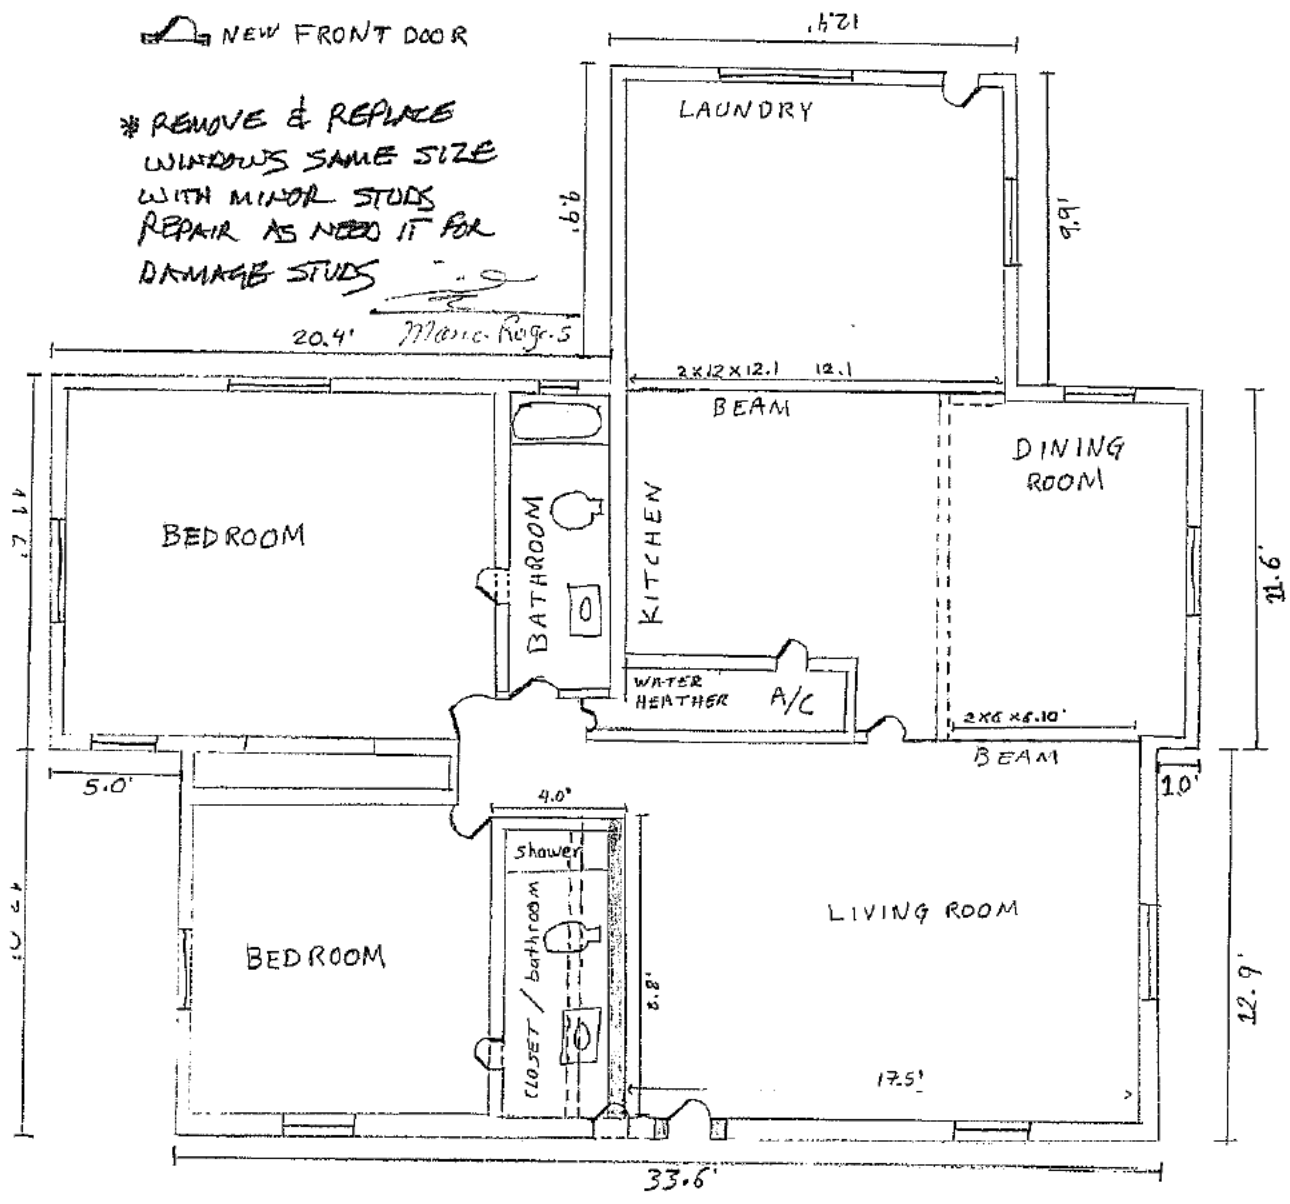
FRONT

30'x6.7' SIZE DOOR EXISTING
5.0'x6.7' NEW SIZE DOOR

 Existing wall
 Demo wall
 New wall
 Existing BEAM
 DEMO BEAM
 NEW BEAM

 Existing Front Door
 DEMO FRONT DOOR
 NEW FRONT DOOR

* REMOVE & REPLACE
 WINDOWS SAME SIZE
 WITH MINOR STUDS
 REPAIR AS NEED IT FOR
 DAMAGE STUDS












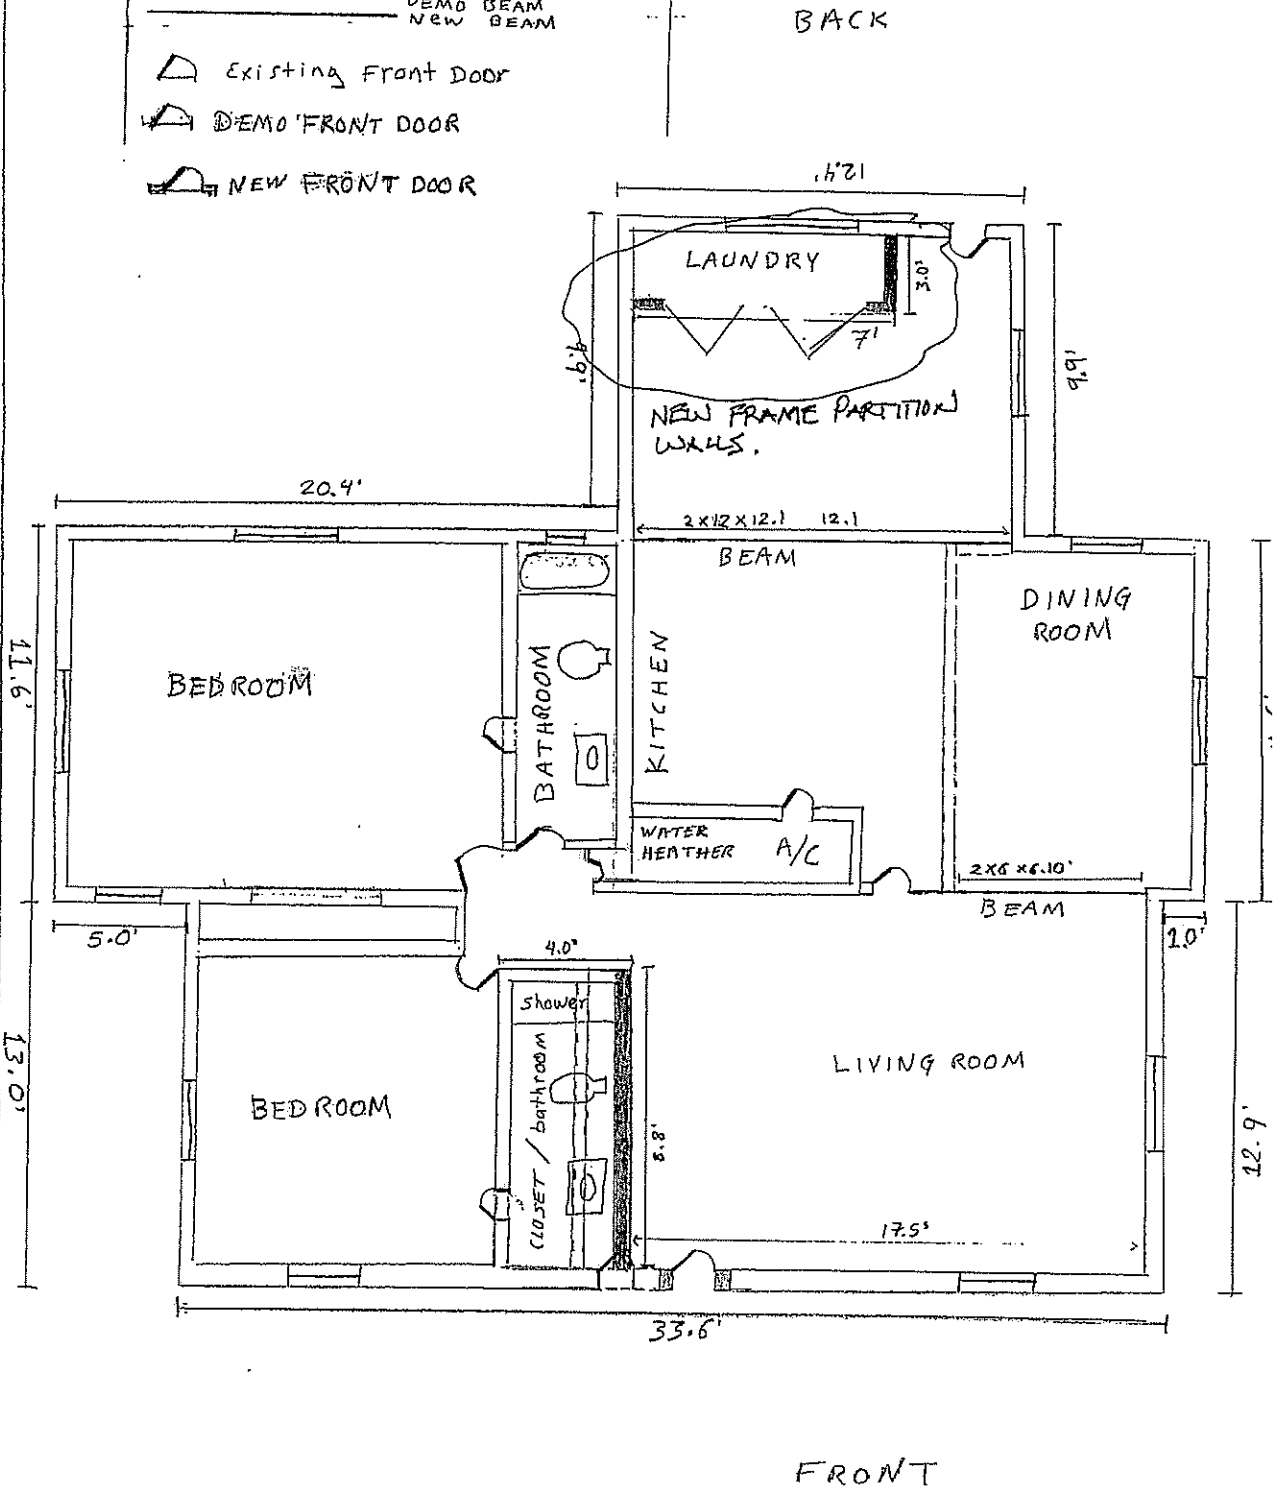
FRONT

RECEIVED BY
 NAME AND ADDRESS
 CITY AND STATE
 ZIP CODE
 DATE
 TIME
 PERMIT
 NO.

5/11/17

SUBJECT TO FIELD INSPECTOR'S APPROVAL

-  Existing wall
-  Demo wall
-  New wall
-  Existing BEAM
-  DEMO BEAM
-  NEW BEAM
-  Existing Front Door
-  DEMO FRONT DOOR
-  NEW FRONT DOOR



3534 Espanola Dr
 Dallas Tx. 75220
