


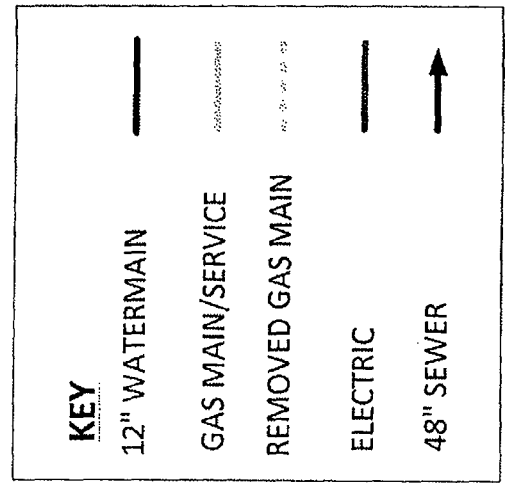

~~2.1~~

Date: 3/23/2014 (Sun)
Loc #: 154
Contract #: GE351

SKETCH:

NY NFP REP.

CONTRACTOR REP:

**NEW YORK CITY DEP.
TIME AND MATERIAL INSPECTOR'S DAILY REPORT**

Weather: Sunny 25°
 Location: Park Ave. bet. E. 116th St. & E. 117th St.
 Borough: MANHATTAN Contractor: J P PICONE

Date: Mon. 3-24-14
 Loc #: 154
 Contract #: GE-351

LABOR / NAME	LOCAL	TITLE	TIME		DEP		UTIL 1		UTIL 2		EQUIPMENT	QTY	DEP	UTIL 1	UTIL 2
			IN	OUT	ST	OT	ST	OT	ST	OT					
1 A. VIMAZ		Super	7:00 AM	9:00 AM	1 1/2						Cat 446 Backhoe	1	6 1/2	2	7
2 A. Pirrone	731	Foreman	7:00 AM	11:00 AM	6 1/2	2			6	1	Compressor 185	1	5		1
3	1536	Timberman									Cut-Off Saw	1	2	2	4
4 D. Buconfrisco	731	Laborer	7:00 AM	11:00 AM	6 1/2	2			6	1	Chain Saw	1	2	2	4
5 M. DeLrio	731	Laborer	7:00 AM	11:00 AM	6 1/2	2			6	1	Target Saw / Size =				
6 D. Dzadosky Jr.	731	Laborer	7:00 AM	11:00 AM	6 1/2	2			6	1	3" Trash Pump (w/ hoses)				
7 C. Todd	731	Laborer	7:00 AM	11:00 AM	6 1/2	2			6	1	3" Mudsucker (w/ hoses)				
8 J. Urli	731	Laborer	7:00 AM	11:00 AM	6 1/2	2			6	1	Roller 5T / Walk Behind				
9 P. Garibaldi	731	LAB	3:30 PM	11:00 PM	6 1/2						Plate Tamper				
10 F. Arena	731	LAB	3:30 PM	11:00 PM	6 1/2						Jumping Jack Tamper				
11 C. Almeida	1010	F/M	3:30 PM	11:00 PM	6 1/2						Utility Truck	1	6 1/2	2	7
12 A. Casillo	15	Backhoe	7:00 AM	11:00 AM	6 1/2	2			6	1	Boom Truck	1	6 1/2	2	7
13 D. Dzadosky	282	Boom Truck	7:00 AM	11:00 AM	6 1/2	2			6	1	2" Pump (w/ hose)	1	2	2	4
14	15	Lights									10-WH Dump Truck	1	6 1/2	2	7
15	15	Pumpman									6-WH Dump Truck				
16 P. Hall	14	Compressor	3:30 PM	9:30 PM	5						Furnace / Weedburner				
17 R. Erga		Safety	7:00 AM	7:00 PM	11 1/2						Tar Kettle - Trailer				
18 A. Natile	282	VAN	5:00 PM	11:00 PM	6						Welder with Truck				
19 C. Pereira	282	Dump Truck	7:00 AM	11:00 AM	6 1/2	2			6	1	Generator 5000 W	1	2	2	4
20											Light Stands				

MATERIALS: Pollard # 5369276
 4- 12" hand tight plugs
 All City Recycling
 16 yds. debris # 106820
 Picone yard
 20- 3" x 10" x 16" lumber
 7 lbs. 40 lb nails
 1- 2" tap w/ goose neck
 1- 3/4" tap w/ goose neck
 5- gal 5 Cl2
 Pollard # 5369255
 5 gal. super dechlorinating
 140 tabs LPD D-Chlor PAI

Light Tower			
Traffic Signs (sf)	9	6 1/2	2 7
Arrow Board			
Traffic Cones	20	6 1/2	2 7
Traffic Barrels			
Bicycle Racks			
Timber Barricade			
Flashing Lights			
Steel Plates	80	8	
Wind Stands	1	6 1/2	2 7
VAN	1	6	
tap machine	1	8	
Air monitor	1	8	
hydrostatic pump	1	8	

SUBCONTRACTORS: Mr. John

DESCRIPTION OF WORK: Broke up + dug out (2) R/W tracks
 10' x 6' + 5' x 5' to locate 12" C.T. water
 main to make ready to cut + cap, set
 sheeting in trench + cut + cap water main + installed (1)
 2" tap + (1) 3/4" tap to chlorinate, injected Cl2 into water
 main + flushed out + took water samples + water main back
 in service. cleaned up job site + set plate over 5' x 5' +
 fenced 10' x 6'. cleaned up job site + made safe, building #
 1652 Park Ave. back in service, notified

SKETCH:

I hereby certify that I inspected the work described hereto, that the time and material records are accurate and correct, that the work was done in an expeditious manner and that the contractor is responsible for the proper execution of the work, except as noted.

CONTRACTOR REP:

Date: 3/25/14
Loc #: 154
Contract #: GE851

I hereby certify that I inspected the work described hereto, that the time and material records are accurate and correct, that [REDACTED] performed this work in an expeditious manner and the labor and equipment shown here were necessary for the proper execution of the work, except [REDACTED]

CONTRACTOR REF.

Weather: SUNNY 35°
Location: PARK Ave. bet. E. 116th St. + E. 117th St.
Borough: MANHATTAN Contractor: J P PICONE

LABOR / NAME	LOCAL	TITLE	TIME		DEP		UTIL 1		UTIL 2		EQUIPMENT	QTY	DEP	UTIL 1	UTIL 2
			IN	OUT	ST	OT	ST	OT	ST	OT					
1 A. YIMAZ		Super	7:00 AM	11:00 PM	4						Cat 446 Backhoe	1	10/2		
2 A. Pirrone	731	Foreman	7:00 AM	6:00 PM	8	2 1/2					Compressor 185	1	8		
3	1536	Timberman									Cut-Off Saw	1	8		
4 O. Buenfrisco	731	Laborer	7:00 AM	6:00 PM	8	2 1/2					Chain Saw	1	8		
5 M. Delrio	731	Laborer	7:00 AM	6:00 PM	8	2 1/2					Target Saw / Size =				
6 D. Dzadosky Jr.	731	Laborer	7:00 AM	6:00 PM	8	2 1/2					3" Trash Pump (w/ hoses)				
7 C. Todd	731	Laborer	7:00 AM	6:00 PM	8	2 1/2					3" Mudsucker (w/ hoses)				
8 J. Lrli	731	Laborer	7:00 AM	6:00 PM	8	2 1/2					Roller 5T / Walk Behind				
9 S. Sinanovic	731	LAB	7:00 AM	6:00 PM	8	2 1/2					Plate Tamper				
10 M. Magnotha	157	Carp.	7:00 AM	6:00 PM	8	2 1/2					Jumping Jack Tamper				
11											Utility Truck	1	10/2		
12 A. Cassillo	15	Backhoe	7:00 AM	6:00 PM	8	2 1/2					Boom Truck	1	10/2		
13 D. Dzadosky	282	Boom Truck	7:00 AM	6:00 PM	8	2 1/2					2" Pump (w/ hose)				
14	15	Lights									10-WH Dump Truck	1	10/2		
15	15	Pumpman									6-WH Dump Truck				
16	14	Compressor									Furnace / Weedburner				
17											Tar Kettle - Trailer				
18											Welder with Truck				
19 C. Pereira	282	Dump Truck	7:00 AM	6:00 PM	8	2 1/2					Generator 5000 W	1	8		
20											Light Stands				

Light Tower	
Traffic Signs (sf)	
Arrow Board	
Traffic Cones	2010/2
Traffic Barrels	
Bicycle Racks	
Timber Barricade	
Flashing Lights	
Steel Plates	8024
Wind Stands	
Steel plate	8024
Left on job	
site 2-dny	
3-25-14	
3-26-14	

Move Backhoe				
Move				
DOT PERMIT #				
CODE 53 #				

UNUSUAL CONDITIONS

SKETCH:

CONTRACTOR REP:

**NEW YORK CITY DEP.
TIME AND MATERIAL INSPECTOR'S DAILY REPORT**

Weather: _____ Date: 3/28/14
 Location: Park Ave b/t E 116 ST & E 117 ST Loc #: 154
 Borough: Manhattan Contractor: J P PICONE Contract #: GE-381

LABOR / NAME	LOCAL	TITLE	TIME		DEP		UTIL 1		UTIL 2		EQUIPMENT	QTY	DEP	UTIL 1	UTIL 2
			IN	OUT	ST	OT	ST	OT	ST	OT					
1		Super									Cat 446 Backhoe				
2	731	Foreman									Compressor 185				
3	1536	Timberman									Cut-Off Saw				
4	731	Laborer									Chain Saw				
5	731	Laborer									Target Saw / Size =				
6		Laborer									3" Trash Pump (w/ hoses)				
7		Laborer									3" Mudsucker (w/ hoses)				
8		Laborer									Roller 5T / Walk Behind				
9											Plate Tamper				
10	<u>Gerry Biltz</u>	<u>ISO Survey</u>	<u>7AM</u>	<u>11AM</u>	<u>4</u>						Jumping Jack Tamper				
11	<u>Len Klausser</u>	<u>ISO Survey</u>	<u>7AM</u>	<u>11AM</u>	<u>4</u>						Utility Truck				
12	15	Backhoe									Boom Truck				
13	282	Boom Truck									2" Pump (w/ hose)				
14	15	Lights									10-WH Dump Truck				
15	15	Pumpman									6-WH Dump Truck				
16	14	Compressor									Furnace / Weedburner				
17											Tar Kettle - Trailer				
18											Welder with Truck				
19	282	Dump Truck									Generator 5000 W				
20											Light Stands				
MATERIALS:											Light Tower				
											Traffic Signs (sf)				
											Arrow Board				
											Traffic Cones				
											Traffic Barrels				
											Bicycle Racks				
											Timber Barricade				
											Flashing Lights				
											Steel Plates				
											Wind Stands				
SUBCONTRACTORS:															
DESCRIPTION OF WORK: <u>Worked on the sewer</u> <u>As built drawings on Auto cad.</u>											Move Backhoe				
											Move				
											DOT PERMIT #				
											CODE 53 #				
UNUSUAL CONDITIONS - Was Included in Tom Delaney's Inspector's Daily Report 3/28/14															
SKETCH:															

I hereby certify that I inspected the work described hereto, that the time and material records are accurate and correct, and that the work was done in an expeditious manner and the labor and equipment shown here were necessary for the proper execution of the work, except as noted.

NY DEP REP: _____ CONTRACTOR REP: _____

**NEW YORK CITY DEP.
TIME AND MATERIAL INSPECTOR'S DAILY REPORT**

Weather: 50° Clouds/RAIN

Date: 3-28-14

Location: PARK AVE B/T 6116th and 6117th ST.

Loc #: 154

Borough: MANHATTAN

Contractor: J P PICONE

Contract #: BE-351

LABOR / NAME	LOCAL	TITLE	TIME		DEP		UTIL 1		UTIL 2		EQUIPMENT	QTY	DEP	UTIL 1	UTIL 2
			IN	OUT	ST	OT	ST	OT	ST	OT					
1 A. YIMAZ		Super	7AM	6PM	10 1/2						Cat 446 Backhoe	1	10 1/2		
2 A. PIRONE	731	Foreman	7AM	6PM	8 3/4						Compressor 185	1	8		
3	1536	Timberman									Cut-Off Saw	2	8		
4 D. BUONFRISCO	731	Laborer	7AM	6PM	8 3/4						Chain Saw	1	8		
5 M. DEL RIO	731	Laborer	7AM	6PM	8 2 1/2						Target Saw / Size =				
6 S. SINANOUIC	731	Laborer	7AM	6PM	8 2 1/2						3" Trash Pump (w/ hoses)				
7 J. URLI	731	Laborer	7AM	6PM	8 2 1/2						3" Mudsucker (w/ hoses)				
8 D. ZADOWSKY JR	731	Laborer	7AM	6PM	8 2 1/2						Roller 5T / Walk Behind				
9 C. TOPP	731	Laborer	7AM	6PM	8 2 1/2						Plate Tamper				
10 M. MAGNOTTA	157	CARDP	7AM	6PM	8 2 1/2						Jumping Jack Tamper				
11 GERRY BUTZ	Survey		7AM	3:30	8 3/4						Utility Truck	1	11 1/2		
12 A. CASILLO	15	Backhoe	7AM	6PM	8 2 1/2						Boom Truck	1	11 1/2		
13 D. DRADOWSKY	282	Boom Truck	7AM	6PM	8 3 1/2						2" Pump (w/ hose)				
14	15	Lights									10-WH Dump Truck	1	10 1/2		
15	15	Pumpman									8-WH Dump Truck				
16	14	Compressor									Furnace / Weedburner				
17 LEWY KRAUSER	Survey		7AM	3:30	8						Tar Kettle - Trailer				
18											Welder with Truck				
19 C. PEREIRA	282	Dump Truck	7AM	6PM	8 2 1/2						Generator 5000 W	1	8		
20 J. Pernochia	282	Dump	7AM	6PM	8 2 1/2						Light Stands				
MATERIALS: 8 2" W/KNAP STRAP															
2EA. 2 1/2" LONG 5/16 BOX DECKSCREWS															
ACR SAND TICKET #1107096 18 yd SAND															
#107110 18 yd SAND															
FELDMAN LUMBER - order #1755652 24EA 2x4x16' lumber															
2EA 1/2x4x8' ply / 12EA 2x6x16' lumber / 12EA 2x10x16'															
Siegel Bros. 4EA 2"x12' 2PLY + 4 NYLON															
12EA 1"x4'x8' Plywood / 12EA 4"x4'x16' lumber															
HENRY QUENTZEL PLUMBING															
4EA. 12" WING NUT TEST BLOCK															
TICKET #1130724															
AUSTER RUBBER #358100 2EA. 2"x50' mil hose															
3EA. Neoprene 12"x120' / 1EA. Redspot Smooth 1/8"x36'															
1EA. Redspot Smooth 1/4"x36' / 2EA. Polyethylene 100LF															
SUBCONTRACTORS: MR. John.															
CM TESTING (Soil Compaction)															
DESCRIPTION OF WORK: CREW HAND EXCAVATES TO BOTTOM OF PIPE. OBJECTIVE OF DAY WAS TO REMOVE DAMAGED PIPE GROUND W/OUT DISTURBING THE LOCATION OF BREAK ONCE PIPE WAS REMOVED (CUT INTO 2-PORTIONS) THE PIPE WAS PLACED IN BOX BUILT ON SITE. 1ST PIECE OF PIPE MEASURED 6' LONG (3' ON EACH SIDE OF BREAK) 2ND PIECE MEASURED 8'4" AND INCLUDED W/C FROM BUILDING #1642.															
UNUSUAL CONDITIONS															
SKETCH:															

I hereby certify that I inspected the work described hereto, that the time and material records are accurate and correct, that this work in an expeditious manner and that the work was necessary for the proper execution of the work, except as

NY DEP REP:

CONTRACTOR REP:

**NEW YORK CITY DEP.
TIME AND MATERIAL INSPECTOR'S DAILY REPORT**

Weather: 45° RAIN/CLOUD

Date: 3-31-14

Location: PARK AVE 81st E116th and E117th

Loc #: 154

Borough: MANHATTAN

Contractor: J.P. PICONE

Contract #: 65-351

LABOR / NAME	LOCAL	TITLE	TIME		DEP		UTIL 1		UTIL 2		EQUIPMENT	QTY	DEP	UTIL 1	UTIL 2
			IN	OUT	ST	OT	ST	OT	ST	OT					
1 A. Yilmaz		Super	7AM	11AM	4						Cat 446 Backhoe	1	8		
2 A. PIRRONE	731	Foreman	7AM	3:30PM	8						Compressor 185	1	4		
3	1536	Timberman									Cut-Off Saw				
4 D. BOUNFRISCO	731	Laborer	7AM	3:30PM	8						Chain Saw				
5 M. DEL RIO	731	Laborer	7AM	3:30PM	8						Target Saw / Size =				
6 CARODD	731	Laborer	7AM	3:30PM	8						3" Trash Pump (w/ hoses)				
7 J. URLI	731	Laborer	7AM	3:30PM	8						3" Mudsucker (w/ hoses)				
8 D. DZALOUSKY JR	731	Laborer	7AM	3:30	8						Roller 5T / Walk Behind				
9											Plate Tamper	1	8		
10											Jumping Jack Tamper	1	8		
11											Utility Truck	1	8		
12 A. CASILLO	15	Backhoe	7AM	3:30PM	8						Boom Truck	1	8		
13 R. LABERGE	282	Boom Truck	7AM	3:30PM	8						2" Pump (w/ hose)				
14	15	Lights									10-WH Dump Truck	1	8		
15	15	Pumpman									6-WH Dump Truck				
16	14	Compressor									Furnace / Weedburner				
17											Tar Kettle - Trailer				
18											Welder with Truck				
19 CARLOS PEREIRA	282	Dump Truck	7AM	3:30PM	8						Generator 5000 W				
20											Light Stands				

MATERIALS:

- Durante Bros Ticket # 652776
SAND 18 yds.

- Willet Point 19.88 TONS COLD PATCH #48112

Light Tower		
Traffic Signs (sf)	9	8
Arrow Board		
Traffic Cones	25	8
Traffic Barrels		
Bicycle Racks		
Timber Barricade		
Flashing Lights		
Steel Plates		
Wind Stands	1	8
STEEL PLATES	80	24
6 DAYS		
3/25/14 3/31/14		

SUBCONTRACTORS:

MR. JOHN.

Move Backhoe	1	1
Move		

DESCRIPTION OF WORK:

- CREW BACKFILLED 3 TRENCHES and
COMPACTED SOIL w/ COMPACTOR


SIZE OF TRENCHES = 5'x4', 6 1/2'x8 1/2', 28'x17'

- PLACED COLD PATCH AND CLEANED UP STREET

DOT PERMIT #	
CODE 53 #	

UNUSUAL CONDITIONS

SKETCH:

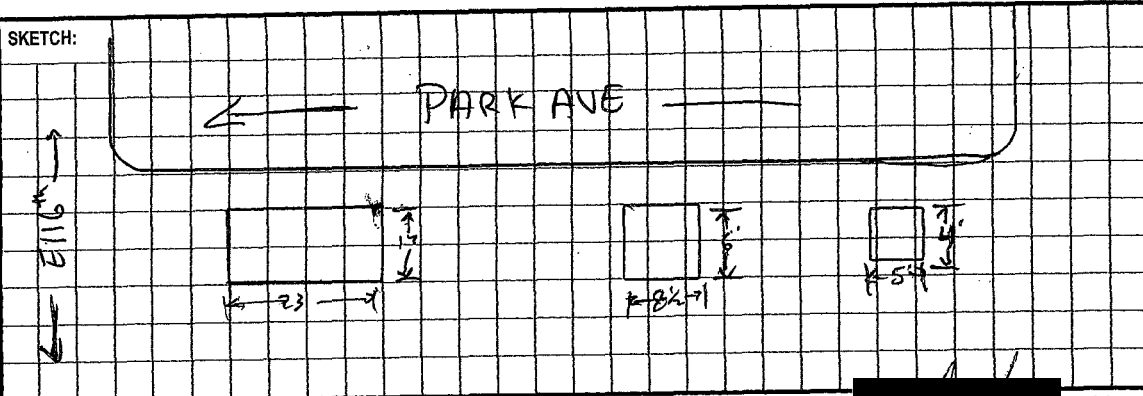

I hereby certify that I inspected the work described hereto, that the time and material records are accurate and correct, that the work was done in an expeditious manner and that the necessary precautions were necessary for the proper execution of the work, except as noted.

NY DEP REP: _____

CONTRACTOR REP: _____
