

**NEW YORK CITY DEP.
TIME AND MATERIAL INSPECTOR'S DAILY REPORT**

Weather: SUNNY 40°
Location: Park Ave. + E 116th St.
Borough: MANHATTAN

Date: Thurs. 4-17-14
Loc #: 154
Contract #: GE-351

Contractor: J P PICONE

3 07	LABOR / NAME	LOCAL	TITLE	TIME		DEP		UTIL 1 ECS		UTIL 2 EP7		EQUIPMENT	QTY	DEP	UTIL 1	UTIL 2	UT:7
				IN	OUT	ST	OT	ST	OT	ST	OT						
1	A. Yimaz		Super	7:00 AM	1:00 PM	4						Cat 446 Backhoe	1	5 1/2	2	2	2
2	A. Pirrone	731	Foreman	7:00 AM	7:00 PM	2	3 1/2	2		2		Compressor 185	1		2	1 1/2	2
3		1536	Timberman									Cut-Off Saw	1	2	2	2	2
4	D. Buonfrisco	731	Laborer	7:00 AM	7:00 PM	2	3 1/2	2		2		Chain Saw					
5	D. Dzadosky Jr.	731	Laborer	7:00 AM	7:00 PM	2		2		2		Target Saw / Size = 36"	1	2	2	2	2
6	M. De/nio	731	Laborer	7:00 AM	7:00 PM	2	3 1/2	2		2		3" Trash Pump (w/ hoses)					
7	J. Urli	731	Laborer	7:00 AM	7:00 PM	2	3 1/2	2		2		3" Mudsucker (w/ hoses)					
8	C. Todd	731	Laborer	7:00 AM	7:00 PM	2	3 1/2	2		2		Roller 5T / Walk Behind					
9												Plate Tamper	1	2			
10												Jumping Jack Tamper					
11												Utility Truck	1	5 1/2	2	2	2
12	A. Casillo	15	Backhoe	7:00 AM	7:00 PM	2	3 1/2	2		2		Boom Truck	1		2	1 1/2	2
13	D. Dzadosky	282	Boom Truck	7:00 AM	1:00 PM			2		1 1/2		2" Pump (w/ hose)					
14		15	Lights									10-WH Dump Truck	1	5 1/2	2	2	2
15		15	Pumpman									6-WH Dump Truck					
16	P. Hall	14	Compressor	7:00 AM	1:00 PM			2		1 1/2		Furnace / Weedburner					
17												Tar Kettle - Trailer					
18												Welder with Truck					
19	C. Pereira	282	Dump Truck	7:00 AM	7:00 PM	2	3 1/2	2		2		Generator 5000 W	1	2			
20												Light Stands					

MATERIALS: All City Recycling
18 yds. sand # 108278
18 yds. sand # 108225
6 yds. blend # 108305
18 yds. blend # 108293
1 yd. debris # 108293

PICONE YARD
6 - R.R. SPIKES
8 - BAGS COLD PATCH
3 - SUPER SACK BAGS

SUBCONTRACTORS: Mr. John

DESCRIPTION OF WORK: Removed 4w plates from tree
+ cut out + removed existing 12" 3-way M.J. +
cleared up, laved 16" 11" of 12" D.I.P. with
(1) 12" sleeve M.J. + (1) 12" 3-way M.J. with 12" plug M.J. on one
side, opened water to check joints + removed slooting +
started to backfill with sand + blend to make ready for cold
patch tomorrow. Saw cut 4w from intersection into black up
to sewer excavation. cleared up job site +
reset plates + made safe.

SKETCH:

I hereby certify that I inspected the work described hereto, that the time and material records are accurate and correct, that the work was done in an expeditious manner and the

work in an

NEW YORK CITY DEP.
TIME AND MATERIAL INSPECTOR'S DAILY REPORT

Weather: Sunny 40°

Location: Park Ave. bet. E. 116th St. + E. 117th St.

Borough: Manhattan

Contractor: J P PICONE

Date: Thurs: 4-17-14

Loc #: 157

Contract #: GE-351

			TIME		DEP		UTIL 1 CON-Ed		UTIL 2						
LABOR / NAME	LOCAL	TITLE	IN	OUT	ST	OT	ST	OT	ST	OT	EQUIPMENT	QTY	DEP	UTIL 1	UTIL 2
1 A. Yim Az		Super	12:00 PM	3:20 PM	4						Cat 335 Backhoe	315	1	8 1/2	3
2 C. Almeida	1010	Foreman	7:00 AM	7:00 PM	6	2 1/2	2	1			Compressor 185		1	3	3
3 D. Reyes	1535	Timberman	7:00 AM	7:00 PM	6	2 1/2	2	1			Cut-Off Saw				
4 V. SAUME	1586	Timberman	7:00 AM	7:00 PM	6	2 1/2	2	1			Chain Saw		2	8 1/2	3
5 P. Garibaldi	731	Laborer	7:00 AM	7:00 PM	6	2 1/2	2	1			Target Saw / Size =				
6 F. ARENA	731	Laborer	7:00 AM	7:00 PM	6	2 1/2	2	1			3" Trash Pump (w/ hoses)				
7 F. SILVA	731	Laborer	7:00 AM	7:00 PM	6	2 1/2	2	1			3" Mudsucker (w/ hoses)				
8 V. Pineda	731	Laborer	7:00 AM	7:00 PM	6	2 1/2	2	1			Roller 5T / Walk Behind				
9											Plate Tamper				
10											Jumping Jack Tamper				
11											Utility Truck		1	8 1/2	3
12 R. MAZZAFERRO	15	Backhoe	7:00 AM	7:00 PM	6	2 1/2	2	1			Boom Truck		1	3	3
13 D. MADOVSKY	282	Boom Truck	1:00 PM	7:50 PM	1/2	2 1/2	2	1			2" Pump (w/ hose)				
14	15	Lights									10-WH Dump Truck		1	8 1/2	3
15	15	Pumpman									6-WH Dump Truck				
16 R. HALL	14	Compressor	1:00 PM	7:00 PM	1/2	2 1/2	2	1			Furnace / Weederburner				
17											Tar Kettle - Trailer				
18											Welder with Truck				
19 J. PENNOCCHIA	282	Dump Truck	7:00 AM	7:00 PM	6	2 1/2	2	1			Generator 5000 W		1	8 1/2	3
20											Light Stands				

MATERIALS: All City Recycling
10 yds. debris # 108308

Piccone yard
4- 2" x 10" x 16' lumber
4- 3" x 10" x 16' lumber

SUBCONTRACTORS: Mr. John

DESCRIPTION OF WORK:	Lower crew continuing to	Move
	excavate 4' x 11 1/2' x 11 1/2' to locate	DOT PERMIT #
	sewer correction for building # 1642	CODE 53 #

Park Ave, located sewer correction 8" C.T. & top of brick sewer 19' to top, took pictures, everything looks good, cleared up job site & made safe.

UNUSUAL CONDITIONS

SKETCH:

I hereby certify that I inspected the work described hereto, that the time and material records are accurate and correct, that expeditious manner and the labor and equipment shown here were necessary for the proper execution of the work, except

this work in an

Weather: SUNNY 40°
Location: Park Ave. bet. E. 116th St. + E. 117th St.
Borough: MANHATTAN Contractor: J.P. PICONE

Date: Fri 4-18-14
Loc #: 154
Contract #: GE-351

[illegible]

I hereby certify that I inspected the work described hereto, that the time and material records are accurate and correct, that the work was done in an expeditious manner and the labor was properly executed, except as noted below:

NEW YORK CITY DEP.
TIME AND MATERIAL INSPECTOR'S DAILY REPORT

Weather: SUNNY 40°
Location: PARK Ave. bet. E. 116th St. + E. 117th St.
Borough: MANHATTAN Contractor: J.P. PICONE

Date: Fri. 4-18-14

Loc #: 154

Contract #: GE-351

[illegible]

I hereby certify that I inspected the work described hereto, that the time and material records are accurate and correct, that the expeditious manner and the [REDACTED] necessary for the proper execution of the work, except as n

**NEW YORK CITY DEP.
TIME AND MATERIAL INSPECTOR'S DAILY REPORT**

Weather: 65° CLEAR
Location: PARK AVE and E 116th ST.
Borough: MANHATTAN

Date: 4-19-14
Loc #: 154
Contract #: GE-351

Contractor: J.P. PICONE

LABOR / NAME	LOCAL	TITLE	TIME		DEP		UTIL 1		UTIL 2		EQUIPMENT	QTY	DEP	UTIL 1		UTIL 2
			IN	OUT	ST	OT	ST	OT	ST	OT				ST	OT	
1 A. VILMAZ.		Super	7AM	7PM							Cat 446 Backhoe	1	6			5 1/2
2 A. PIRRONE	731	Foreman	7AM	7AM			6	5 1/2			Compressor 185	1	4			4
3	1536	Timberman									Cut-Off Saw	1	4			4
4 D. BIANFRISCO	731	Laborer	7AM	7PM			6	5 1/2			Chain Saw	2	4			4
5 M. DEL RIO	731	Laborer	7AM	7 PM			6	5 1/2			Target Saw / Size =					
6 C. JORD	731	Laborer	7AM	7 PM			6	5 1/2			3" Trash Pump (w/ hoses)					
7 D. CESTIA	731	Laborer	7AM	7 PM			6	5 1/2			3" Mudsucker (w/ hoses)					
8 S. SINANOVIC	731	Laborer	7AM	7 PM			6	5 1/2			Roller 5T / Walk Behind					
9											Plate Tamper	1	4			4
10											Jumping Jack Tamper					
11											Utility Truck	1	6			5 1/2
12 A. CASSILLO	15	Backhoe	7AM	7 PM			6	5 1/2			Boom Truck					
13	282	Boom Truck									2" Pump (w/ hose)					
14	15	Lights									10-WH Dump Truck					
15	15	Pumpman									6-WH Dump Truck					
16	14	Compressor									Furnace / Weedburner					
17											Tar Kettle - Trailer					
18											Welder with Truck					
19 C. PEREIRA	282	Dump Truck	7AM	7 PM			6	5 1/2			Generator 5000 W					
20											Light Stands					

MATERIALS:

ACR 11yd MIX (cont) 108304.
24 EA 3"x10"x16' TIMBER.
10 POUND 16 D NAILS.
10 POUND 40 D NAILS.

Light Tower			
Traffic Signs (sf)			
Arrow Board	1	6	5 1/2
Traffic Cones	20	6	5 1/2
Traffic Barrels			
Bicycle Racks			
Timber Barricade			
Flashing Lights			
Steel Plates	55	180	18 1/2
Wind Stands			

SUBCONTRACTORS:


MR. JOHN

DESCRIPTION OF WORK: - CREW CONTINUES EXCAVATION TO INSTALL
W/M. STARTED LAYING 12" PIPE @ STA 0+12 N/N CL ON E116"
CREW INSTALLED 111' OF 12" DIP @ C=3'6"
- TRENCH EXCAVATED AT 4' and 8' off WCL ON PARK AVE

Move Backhoe			
Move			
DOT PERMIT #			
CODE 53 #			

UNUSUAL CONDITIONS

SKETCH:

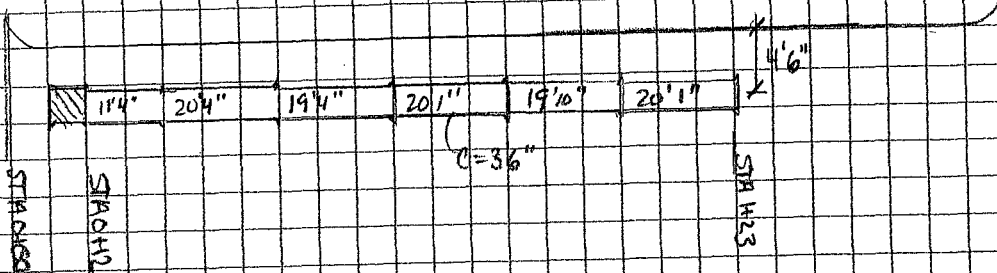

I hereby certify that I inspected the work described hereto, that the time and material records are accurate and correct, that the work was done in an expeditious manner and that the materials were necessary for the proper execution of the work, except

CONTRACTOR REP:

NEW YORK CITY DEP.
TIME AND MATERIAL INSPECTOR'S DAILY REPORT

Weather: 65° CLEAR
Location: PARK AVE + E 116th ST.
Borough: MANHATTAN

Date: 4-19-14
Loc #: 154
Contract #: GE-351

LABOR / NAME	LOCAL	TITLE	TIME		DEP		UTIL 1 OT+EO		UTIL 2		EQUIPMENT	QTY	DEP	UTIL 1	UTIL 2
			IN	OUT	ST	OT	ST	OT	ST	OT					
1		Super									Cat 446 Backhoe	1	5 1/2		6
2 C. ALUEIDA	731	Foreman	7	7			5 1/2		6		Compressor 185	1	5 1/2		6
3 D. REYES	1536	Timberman	7	7			5 1/2		6		Cut-Off Saw	1	5 1/2		6
4 F. ARENA	731	Laborer	7	7			5 1/2		6		Chain Saw	1	5 1/2		6
5 F. SILVA	731	Laborer	7	7			5 1/2		6		Target Saw / Size =				
6 D. GARIBALDI	731	Laborer	7	7			5 1/2		6		3" Trash Pump (w/ hoses)				
7		Laborer									3" Mudsucker (w/ hoses)				
8		Laborer									Roller ST / Walk Behind				
9 V. SAUME	1536	TIMBER	7	7			5 1/2		6		Plate Tamper				
10											Jumping Jack Tamper				
11											Utility Truck	1	5 1/2		6
12 ROCCO MAZZELLA	15	Backhoe	7	7			5 1/2		6		Boom Truck	1	5 1/2		6
13 R. LABERGE	282	Boom Truck	7	7			5 1/2		6		2" Pump (w/ hose)				
14	15	Lights									10-WH Dump Truck	1	5 1/2		6
15	15	Pumpman									6-WH Dump Truck				
16 P. HALL	14	Compressor	7AM	7-PM			5 1/2		6		Furnace / Weedburner				
17											Tar Kettle - Trailer				
18											Welder with Truck				
19 A. PENNACCHIA	282	Dump Truck	7AM	7			5 1/2		6		Generator 5000 W				
20											Light Stands				
MATERIALS:											Light Tower				
ACR 18 YDS MIX (out) #108397											Traffic Signs (sf)				
108889											Arrow Board				
108887											Traffic Cones				
108393											Traffic Barrels				
DURANTE 18 YDS MIX (out) #129487											Bicycle Racks				
ACR 10 YDS SAND (in) #108388											Timber Barricade				
10 EA 2"x10" x 16'											Flashing Lights				
16 EA 3"x10" x 16'											Steel Plates				
											Wind Stands				
SUBCONTRACTORS:															
MR. JOHN.											Move Backhoe				
DESCRIPTION OF WORK: - SAW CUT AND EXTENDED TRENCH											Move				
CREW INSTRUCTED TO SAW CUT AND EXCAVATE TRENCH											DOT PERMIT #				
@ 4' and 8' OFF W/L of PARK AVE. THIS WAS TO											CODE 53 #				
ACCOMMODATE AGREEMENT w/ CON ED FOR COMMON TRENCH.															
UNUSUAL CONDITIONS															
SKETCH:															

I hereby certify that I inspected the work described hereto, that the time and material records are accurate and correct, that the cost of the work was reasonable, and that the work was completed in an expeditious manner. [REDACTED] were necessary for the proper execution of the work, except as noted above. [REDACTED] and this work in an

NEW YORK CITY DEP.
TIME AND MATERIAL INSPECTOR'S DAILY REPORT

Weather: Clear SS-F

Location: Park Ave b/t E 116 St & E 117 St

Borough: Manhattan

Date: 4/21/19, Monday

Loc #: 154

Contract #: CE 351

LABOR / NAME			LOCAL	TITLE	TIME		DEP		UTIL 1		UTIL 2		EQUIPMENT	QTY	DEP	UTIL 1	UTIL 2
					IN	OUT	ST	OT	ST	OT	ST	OT					
1	A. Pinaz			Super	7 AM	3 PM	4						Cat 400 Backhoe	1	5 1/2	6	
2	Cyrus Almeida	1010		Foreman	7 AM	7 PM	4	1 1/2	4	2			Compressor 185	-			
3	A. Reyes	1556		Timberman	7 AM	7 PM	4	1 1/2	4	2			Cut-Off Saw	1	5 1/2	6	
4	F. Caribaldi	731		Laborer	7 AM	7 PM	4	1 1/2	4	2			Chain Saw	1	5 1/2	6	
5	F. Silva	731		Laborer	7 AM	7 PM	4	1 1/2	4	2			Target Saw / Size = 3 6	1	12	8	
6	V. Pineda	731		Laborer	7 AM	7 PM	4	1 1/2	4	2			3" Trash Pump (w/ hoses)				
7	R. Arena	731		Laborer	7 AM	7 PM	4	1 1/2	4	2			3" Mudsucker (w/ hoses)				
8	V. Saume	1556		Laborer	7 AM	7 PM	4	1 1/2	4	2			Roller ST / Walk Behind				
9													Plate Tamper				
10													Jumping Jack Tamper	1	5 1/2	6	
11													Utility Truck	1	5 1/2	6	
12	R. Mazzafro	15		Backhoe	7 AM	7 PM	4	1 1/2	4	2			Boom Truck				
13		282		Boom Truck									2" Pump (w/ hose)				
14		15		Lights									10-WH Dump Truck	1	4	5	
15		15		Pumpman									6-WH Dump Truck				
16		14		Compressor									Furnace / Weedburner				
17													Tar Kettle - Trailer				
18													Welder with Truck				
19	J. Pennacchia	282		Dump Truck	7 AM	5 PM	4	1/2	4	1			Generator 5000 W				
20													Light Stands				
MATERIALS:													Light Tower				
* All City Recycling # 108481 (18' x 6' Cont.)													Traffic Signs (sf)				
- 12 ea 3" x 12" x 16'													Arrow Board				
- Saw cut 40 L# @ 3 6" Diamond Blade													Traffic Cones	9	9	6	6
													Traffic Barrels				
													Bicycle Racks				
													Timber Barricade				
													Flashing Lights				
													Steel Plates				
													Wind Stands				
SUBCONTRACTORS: Mr. John																	
													Move Backhoe				
													Move				
DESCRIPTION OF WORK: - Crew helped Con Ed install 120' of 8" plastic													DOT PERMIT #				
- Move a box (sheeted) met connection location info bldg # 1642													CODE 53 #				
- Saw cut 40 L# if bldg # 1642 in preparation for																	
- Existing down to the Series to check its integrity																	
- Split hours in half between Con Ed																	
UNUSUAL CONDITIONS																	
SKETCH:																	

I hereby certify that I inspected the work described hereto, that the time and material records are accurate and correct, that the expeditious manner and the labor and equipment shown here were necessary for the proper execution of the work, except as

**NEW YORK CITY DEP.
TIME AND MATERIAL INSPECTOR'S DAILY REPORT**

Weather: Clear 60°F
 Location: Park Ave 616 E 116 St & E 117 St
 Borough: Manhattan

Date: 4/22/14, Tuesday
 Loc #: _____
 Contract #: GE 351

Contractor: **J P PICONE**

LABOR / NAME	LOCAL	TITLE	TIME		DEP		UTIL 1 CoEd		UTIL 2 EP-7		EQUIPMENT	QTY	DEP	UTIL 1 CoEd	UTIL 2 EP-7
			IN	OUT	ST	OT	ST	OT	ST	OT					
1 A. Yilmaz		Super	11 AM	3 PM							Cat 315	1	6 1/2	3	2
2 Carlos Almeida	1530	Foreman	7 AM	7 PM	4	2 1/2	3		1		Compressor 185	1	6 1/2	3	2
3 D. Reyes	1530	Timberman	7 AM	7 PM	4	2 1/2	3		1	1	Cut-Off Saw	1	6 1/2	3	2
4 P. Caribaldi	731	Laborer	7 AM	7 PM	4	2 1/2	3		1	1	Chain Saw	1	6 1/2	3	2
5 F. Silva	731	Laborer	7 AM	7 PM	4	2 1/2	3		1	1	Target Saw / Size =				
6 V. Pineda	731	Laborer	7 AM	7 PM	4	2 1/2	3		1	1	3" Trash Pump (w/ hoses)				
7 F. Ariza	731	Laborer	7 AM	7 PM	4	2 1/2	3		1	1	3" Mudsucker (w/ hoses)				
8 V. Sane	1530	Timberman	7 AM	7 PM	4	2 1/2	3		1	1	Roller 5T / Walk Behind				
9											Plate Tamper	1	3	3	2
10											Jumping Jack Tamper	1	3	3	2
11											Utility Truck	1	6 1/2	3	2
12 R. Mazzafro	15	Backhoe	7 AM	7 PM	4	2 1/2	3		1	1	Boom Truck				
13	202	Boom Truck									2" Pump (w/ hose)				
14	15	Lights									10-WH Dump Truck	1	6 1/2	3	2
15	15	Pumpman									6-WH Dump Truck				
16	14	Compressor									Furnace / Weedburner				
17											Tar Kettle - Trailer				
18											Welder with Truck				
19 A. Natale	202	Dump Truck	7 AM	7 PM	4	2 1/2	3		1	1	Generator 5000 W				
20											Light Stands				
MATERIALS: - 1/2 CoEd			All DEP												
All City Recycling: 12 yds Sand # 108502			10 yds debris # 108552												
18 yds blend # 108508			12 yds debris # 108584												
18 yds blend # 108533			18 yds debris # 108594												
12 yds blend # 108544															
- 16' of 3"x10"x16' long															
- 5 ea super sack bags															
SUBCONTRACTORS: Mr. Sohn															
DESCRIPTION OF WORK: - Backfilled trench used to place ^{New 8" DEP} Water main															
and New 8" CoEd plastic pipe, then taped.															
- Backfilled around sheeted trench containing end of coed New 8" pipe															
- Placed plate over sheeted trench containing DEP location of future wet connection for bldg # 1612															
- 7:30 AM - 11:30 PM, split time in 1/2 with CoEd because backfill of common trench															
- Excavation of trench where sewer will be investigated. Used straps to secure New CoEd 8" plastic															
- 22"x10' trench															
UNUSUAL CONDITIONS															
SKETCH:															

I hereby certify that I inspected the work described hereto, that the time and material records are accurate and correct, that the work was done in an expeditious manner and the labor and equipment shown here were necessary for the proper execution of the work, except as noted.

**NEW YORK CITY DEP.
TIME AND MATERIAL INSPECTOR'S DAILY REPORT**

Weather: SUNNY 58°
 Location: PARK Ave. bet. E. 116th St. & E. 117th St.
 Borough: MANHATTAN Contractor: J P PICONE

Date: Tues. 4-22-17
 Loc #: 157
 Contract #: GE-357

LABOR / NAME	LOCAL	TITLE	TIME		DEP		UTIL 1 Con-Ed		UTIL 2		EQUIPMENT	QTY	DEP	UTIL 1	UTIL 2		
			IN	OUT	ST	OT	ST	OT	ST	OT							
1 <u>A. YIMAZ</u>		Super	<u>7:00 AM</u>	<u>12:00 PM</u>							Cat 446 Backhoe	1	5 1/2	6			
2 <u>A. Pirrone</u>	731	Foreman	<u>7:00 AM</u>	<u>7:00 PM</u>	4	1 1/2	4	2			Compressor 185	1	4	4			
3	1536	Timberman									Cut-Off Saw	1	4	4			
4 <u>D. BUONFRISCO</u>	731	Laborer	<u>7:00 AM</u>	<u>7:00 PM</u>	4	1 1/2	4	2			Chain Saw						
5 <u>M. Delrio</u>	731	Laborer	<u>7:00 AM</u>	<u>7:00 PM</u>	4	1 1/2	4	2			Target Saw / Size =						
6 <u>D. DZADOUSKY JR.</u>	731	Laborer	<u>7:00 AM</u>	<u>7:00 PM</u>	4	1 1/2	4	2			3" Trash Pump (w/ hoses)						
7 <u>J. Uli</u>	731	Laborer	<u>7:00 AM</u>	<u>7:00 PM</u>	4	1 1/2	4	2			3" Mudsucker (w/ hoses)						
8 <u>C. Todd</u>	731	Laborer	<u>7:00 AM</u>	<u>3:30 PM</u>	4		4				Roller 5T / Walk Behind						
9											Plate Tamper						
10											Jumping Jack Tamper						
11											Utility Truck	1	5 1/2	6			
12 <u>A. CASILLO</u>	15	Backhoe	<u>7:00 AM</u>	<u>7:00 PM</u>	4	1 1/2	4	2			Boom Truck	1	4 1/2	5			
13 <u>D. DZADOUSKY</u>	282	Boom Truck	<u>7:00 AM</u>	<u>5:00 PM</u>	4	1 1/2	4	2			2" Pump (w/ hose)						
14	15	Lights									10-WH Dump Truck	1	5 1/2	6			
15	15	Pumpman									6-WH Dump Truck						
16 <u>P. Hall</u>	14	Compressor	<u>7:00 AM</u>	<u>3:30 PM</u>	4		4				Furnace / Weeburner						
17											Tar Kettle - Trailer						
18											Weider with Truck						
19 <u>C. Pereira</u>	282	Dump Truck	<u>7:00 AM</u>	<u>7:00 PM</u>	4	1 1/2	4	2			Generator 5000 W						
20											Light Stands						
MATERIALS: <u>All City Recycling</u> <u>7 yds. debris # 108565</u> <u>CON Ed</u> <u>5 yds. sand # 108565</u> <u>50%</u> <u>18 yds. debris # 108654</u>																	
												Light Tower					
												Traffic Signs (sf)					
												Arrow Board	1	18	6		
												Traffic Cones					
												Traffic Barrels					
												Bicycle Racks					
												Timber Barricade					
												Flashing Lights					
												Steel Plates	640	18	6		
												Wind Stands					
SUBCONTRACTORS: <u>Mr. John</u>																	
												Move Backhoe					
												Move					
DESCRIPTION OF WORK: <u>Continued digging R/W trench</u> <u>& layered 24" 10" of 12" D.E.P.</u> <u>covered pipe with sand & continued</u> <u>digging & layered around 8" C.T. gas</u> <u>main to make ready for removal.</u> <u>cleaned up job site & heat plates</u> <u>& made safe.</u>												DOT PERMIT #	<u>14012014083004</u>				
												CODE 53 #	<u>091046</u>				
													<u>048</u>				
													<u>082</u>				
UNUSUAL CONDITIONS																	
SKETCH:																	

I hereby certify that I inspected the work described hereto, that the time and material records are accurate and correct, that the work was done in an expeditious manner and the labor and equipment shown here were necessary for the proper execution of the work, except as noted.

**NEW YORK CITY DEP.
TIME AND MATERIAL INSPECTOR'S DAILY REPORT**

Weather: Clean, 55°F
 Location: Park Ave b/w E 116 St & E 117 St
 Borough: Manhattan

Date: 4/23/14, Wednesday
 Loc #: 154
 Contract #: GE 3 S1

Contractor: J P PICONE

LABOR / NAME	LOCAL	TITLE	TIME		DEP		UTIL 1 EPA 88 EP-7		UTIL 2		EQUIPMENT	QTY	DEP	UTIL 1	UTIL 2
			IN	OUT	ST	OT	ST	OT	ST	OT					
1 A. Vilmarz		Super	11AM	3:30PM	4						Cat 400 Backhoe 36" Flyer Exc	1	8 1/2	3	
2 Carlos Almeida	11010	Foreman	7AM	7PM	6	2 1/2	2	1			Compressor 185	1	5	3	
3 A. Reyes	1536	Timberman	7AM	7PM	6	2 1/2	2	1			Cut-Off Saw	2			
4 P. Contreras	731	Laborer	7AM	7PM	6	2 1/2	2	1			Chain Saw	2	8 1/2	3	
5 F. Silva	731	Laborer	7AM	7PM	6	2 1/2	2	1			Target Saw / Size =				
6 V. Pineda	731	Laborer	7AM	7PM	6	2 1/2	2	1			3" Trash Pump (w/ hoses)				
7 F. Anela	731	Laborer	7AM	7PM	6	2 1/2	2	1			3" Mudsucker (w/ hoses)				
8 V. Saume	1536	Laborer	7AM	7PM	6	2 1/2	2	1			Roller 5T / Walk Behind				
9											Plate Tamper				
10											Jumping Jack Tamper				
11											Utility Truck	1	8 1/2	3	
12 R. Mazzaferro	15	Backhoe	7AM	7PM	6	2 1/2	2	1			Boom Truck				
13	282	Boom Truck									2" Pump (w/ hose)				
14	15	Lights									10-WH Dump Truck	1	8 1/2	3	
15	15	Pumpman									6-WH Dump Truck				
16	14	Compressor									Furnace / Weederburner				
17											Tar Kettle - Trailer				
18											Welder with Truck				
19 R. Cherubini	282	Dump Truck	7AM	7PM	6	2 1/2	2	1			Generator 5000 W				
20											Light Stands				

MATERIALS:

All city Recycling # 108767, 10 yds M/S
 # 108674, 10 yds M/S
 # 108740, 10 M/S
 87 ea 3" x 10" x 20' timber
 6 ea 2" x 10" x 16'
 6 ea 12" x 12" x 20'
 10 lbs 40 lb nails
 10 lbs 16 lb nails

Light Tower
 Traffic Signs (sf)
 Arrow Board
 Traffic Cones 15 8 1/2 3
 Traffic Barrels
 Bicycle Racks
 Timber Barricade
 Flashing Lights
 Steel Plates
 Wind Stands

SUBCONTRACTORS: Mr. Sohn

DESCRIPTION OF WORK: - Continued excavating sewer trench, sleeved installed.
 Depth is at: 8' - Con Ed 8" plastic hand dug around it and supported it with traps in the trench.
 - Con Ed 8" plastic pipe supported (EP-7 345), (Con Ed Ins - Riser CH 1646-737-23PS)

UNUSUAL CONDITIONS: - Lot of rocks are discovered

SKETCH:

I hereby certify that I inspected the work described hereto, that the time and material records are accurate and correct, that the work was done in an expeditious manner and the labor and equipment shown here were necessary for the proper execution of the work, except as noted.

TIME AND MATERIAL INSPECTOR'S DAILY REPORT

Weather: Partly sunny 55°
Location: Park Ave. bet. E. 116th St. + E. 117th St.
Borough: Manhattan Contractor: J P PICONE

Date: Wed. 4-23-17
Loc #: 154
Contract #: GE-351

[illegible]

I hereby certify that I inspected the work described hereto, that the time and material records are accurate and correct, that the expeditious manner and the labor and equipment shown here were necessary for the proper execution of the work, except as

NEW YORK CITY DEP.
TIME AND MATERIAL INSPECTOR'S DAILY REPORT

Weather: Clear SS + F

Location: Park Ave, b/t E 111 st & E 112 St

Borough: Manhattan

Contractor: J P PICONE

Date: 4/24/14, Thursday

Loc #: 154

Contract #: 6E351

[illegible]

I hereby certify that I inspected the work described hereto, that the time and material records are accurate and correct, that the work was done in an expeditious manner and the labor and equipment shown here were necessary for the proper execution of the work, except as noted.

**NEW YORK CITY DEP.
TIME AND MATERIAL INSPECTOR'S DAILY REPORT**

Weather: SUNNY 55°
 Location: PARK Ave. bet. E. 116th St. & E. 117th St.
 Borough: MANHATTAN Contractor: J P PICONE

Date: Thurs. 4-24-19
 Loc #: 154
 Contract #: GE-351

LABOR / NAME	LOCAL	TITLE	TIME		DEP.		UTIL 1 CON ED		UTIL 2 ECS		EQUIPMENT	QTY	DEP.	UTIL 1	UTIL 2
			IN	OUT	ST	OT	ST	OT	ST	OT					
1 <u>A. YIMAZ</u>		Super	<u>7:00</u>	<u>11:00</u>							Cat 446 Backhoe	1	<u>4 1/2</u>	<u>6</u>	<u>1</u>
2 <u>H. Pirrone</u>	731	Foreman	<u>7:00</u>	<u>7:00</u>	<u>3 1/2</u>	<u>4</u>	<u>2</u>	<u>1</u>			Compressor 185	1	<u>3 1/2</u>	<u>6</u>	<u>1</u>
3	1536	Timberman									Cut-Off Saw	1	<u>4</u>	<u>4</u>	
4 <u>D. Buonfrisco</u>	731	Laborer	<u>7:00</u>	<u>7:00</u>	<u>3 1/2</u>	<u>4</u>	<u>2</u>	<u>1</u>			Chain Saw				
5 <u>M. Delrio</u>	731	Laborer	<u>7:00</u>	<u>7:00</u>	<u>3 1/2</u>	<u>4</u>	<u>2</u>	<u>1</u>			Target Saw / Size =				
6 <u>D. Dzadosky Jr.</u>	731	Laborer	<u>7:00</u>	<u>7:00</u>	<u>3 1/2</u>	<u>4</u>	<u>2</u>	<u>1</u>			3" Trash Pump (w/ hoses)				
7 <u>J. Urli</u>	731	Laborer	<u>7:00</u>	<u>7:00</u>	<u>3 1/2</u>	<u>4</u>	<u>2</u>	<u>1</u>			3" Mudsucker (w/ hoses)				
8 <u>C. Todd</u>	731	Laborer	<u>7:00</u>	<u>7:00</u>	<u>3 1/2</u>	<u>4</u>	<u>2</u>	<u>1</u>			Roller 5T / Walk Behind				
9											Plate Tamper				
10											Jumping Jack Tamper				
11											Utility Truck	1	<u>4 1/2</u>	<u>6</u>	<u>1</u>
12 <u>A. CASI'NO</u>	15	Backhoe	<u>7:00</u>	<u>7:00</u>	<u>3 1/2</u>	<u>4</u>	<u>2</u>	<u>1</u>			Boom Truck	1	<u>3 1/2</u>	<u>1</u>	
13 <u>D. Dzadosky</u>	282	Boom Truck	<u>11:00</u>	<u>4:00</u>			<u>3 1/2</u>	<u>1</u>			2" Pump (w/ hose)				
14	15	Lights									10-WH Dump Truck	1	<u>4 1/2</u>	<u>6</u>	<u>1</u>
15	15	Pumpman									6-WH Dump Truck				
16 <u>P. Hall</u>	14	Compressor	<u>7:00</u>	<u>6:00</u>	<u>3 1/2</u>	<u>4</u>	<u>2</u>	<u>1</u>			Furnace / Weedburner				
17											Tar Kettle - Trailer				
18											Welder with Truck				
19 <u>C. Pereira</u>	282	Dump Truck	<u>7:00</u>	<u>7:00</u>	<u>3 1/2</u>	<u>4</u>	<u>2</u>	<u>1</u>			Generator 5000 W				
20											Light Stands				
MATERIALS: <u>All City Recycling</u>															
<u>18 yds. debris # 108846</u>															
<u>2 yds. sand # 108846</u>															
<u>6 yds. debris # 108872</u>															
<u>PICONE YARD</u>															
<u>3 - bags cold patch</u>															
<u>3 - super sacks</u>															
<u>CON ED</u>															
<u>50%</u>															
SUBCONTRACTORS: <u>Mr. John</u>															
DESCRIPTION OF WORK: <u>Continued Digging R/W</u>															
<u>truck by hand around rocks +</u>															
<u>stone + 8" C.I. gas main + 12" C.I.</u>															
<u>water main approx 6' x 20' layed</u>															
<u>20' 4" of 12" D.I.P. cleaned up sig</u>															
<u>site + reset plates + made safe.</u>															
UNUSUAL CONDITIONS															
SKETCH:															

I hereby certify that I inspected the work described hereto, that the time and material records are accurate and correct, that the work was done in an expeditious manner and the labor and equipment shown here were necessary for the proper execution of the work, except as noted.

**NEW YORK CITY DEP.
TIME AND MATERIAL INSPECTOR'S DAILY REPORT**

Weather: Clear 60°F
Location: Park Ave 1/4 E 116 St & E 117 St
Borough: Manhattan

Date: 4/25/14, Friday
Loc #: 154
Contract #: 6E357

Contractor: J P PICONE

LABOR / NAME	LOCAL	TITLE	TIME		DEP		UTIL 1		UTIL 2		EQUIPMENT	QTY	DEP	UTIL 1	UTIL 2
			IN	OUT	ST	OT	ST	OT	ST	OT					
1 A. Blum		Super	7:45 AM	3:30 PM	4						Cat Backhoe	1	8 1/2	3	
2 Carlos Alameda	731	Foreman	7 AM	7 PM	6	2 1/2	2	1			Compressor 185	1	8 1/2	2	
3 L. Chizpue	731	Timberman	7 AM	7 PM	6	2 1/2	2	1			Cut-Off Saw				
4 P. Caribaldi	731	Laborer	7 AM	7 PM	6	2 1/2	2	1			Chain Saw	2	8	3	
5 F. Silva	731	Laborer	7 AM	7 PM	6	2 1/2	2	1			Target Saw / Size =				
6 V. Pineda	731	Laborer	7 AM	7 PM	6	2 1/2	2	1			3" Trash Pump (w/ hoses)				
7 F. Arena	731	Laborer	7 AM	7 PM	6	2 1/2	2	1			3" Mudsucker (w/ hoses)				
8 V. Suane	155	Laborer	7 AM	7 PM	6	2 1/2	2	1			Roller 5T / Walk Behind				
9											Plate Tamper				
10											Jumping Jack Tamper				
11											Utility Truck	1	8 1/2	3	
12 R. Mazzaro	15	Backhoe	7 AM	7 PM	6	2 1/2	2	1			Boom Truck				
13	282	Boom Truck									2" Pump (w/ hose)				
14	15	Lights									10-WH Dump Truck	1	8 1/2	3	
15	15	Pumpman									6-WH Dump Truck				
16 P. Hall	14	Compressor	7 AM	1 PM	3 1/2			2			Furnace / Weederburner				
17											Tar Kettle - Trailer				
18											Welder with Truck				
19 R. Cherubini	282	Dump Truck	7 AM	7 PM	6	2 1/2	2	1			Generator 5000 W	1	8 1/2	3	
20											Light Stands				
MATERIALS:															
- AM City Recycling #108921 - 10' x 10' x 20'															
- #108927 - 8' x 2' x 10'															
- 2 ea 12" x 10" x 20'															
- 8 ea 8" x 10" x 10'															
- 4 ea 3" x 10" x 20'															
- 2 ea 12" x 12" x 8'															
- 5 ea 4" x 4" x 1'															
SUBCONTRACTORS: - Mr. John															
DESCRIPTION OF WORK: - Continued excavating trench depth at 13'															
- Can Ed 8" plastic pipe was gouged at 1:20 PM by contractor's CAT 35 hydraulic excavator															
- Supporting Can Ed 8" plastic (EP-723 hrs), Can Ed Inspection															
- CP# 1646 739 2385															
UNUSUAL CONDITIONS - Large amounts of rocks and voids found															
SKETCH:															

I hereby certify that I inspected the work described hereto, that the time and material records are accurate and correct, that the work was done in an expeditious manner and the labor and equipment shown here were necessary for the proper execution of the work, except as noted.

work in an

NEW YORK CITY DEP.
TIME AND MATERIAL INSPECTOR'S DAILY REPORT

Weather: SUNNY 55°
Location: PARK Ave. bet. E. 116th St. & E. 117th St.
Borough: MANHATTAN Contractor: J P PICONE

Date: Fri. 4-25-14
Loc #: 154
Contract #: GE-351

			TIME		DEP		UTIL 1 Con-Ed		UTIL 2						
LABOR / NAME	LOCAL	TITLE	IN	OUT	ST	OT	ST	OT	ST	OT	EQUIPMENT	QTY	DEP	UTIL 1	UTIL 2
1 A. YIMAZ		Super	7:00 AM	11:00 AM	4						Cat 446 Backhoe	1	5	6 1/2	
2 H. Pirrone	731	Foreman	7:00 AM	7:00 PM	3	2	5	1 1/2			Compressor 185	1	4 1/2	1 1/2	
3	1536	Timberman									Cut-Off Saw	1	1 1/2	6 1/2	
4 D. Bucofrisco	731	Laborer	7:00 AM	7:00 PM	3	2	5	1 1/2			Chain Saw				
5 M. Delrio	731	Laborer	7:00 AM	7:00 PM	3	2	5	1 1/2			Target Saw / Size =				
6 D. Dzadosky Jr.	731	Laborer	7:00 AM	3:30 PM	3		5				3" Trash Pump (w/ hoses)				
7 J. Urli	731	Laborer	7:00 AM	7:00 PM	3	2	5	1 1/2			3" Mudsucker (w/ hoses)				
8 C. Todd	731	Laborer	7:00 AM	7:00 PM	3	2	5	1 1/2			Roller 5T / Walk Behind				
9											Plate Tamper				
10											Jumping Jack Tamper				
11											Utility Truck	1	5	6 1/2	
12 A. Casillo	15	Backhoe	7:00 AM	7:00 PM	3	2	5	1 1/2			Boom Truck	1	3	5	
13 D. Dzadosky	282	Boom Truck	7:00 AM	3:30 PM	3		5				2" Pump (w/ hose)				
14	15	Lights									10-WH Dump Truck	1	5	6 1/2	
15	15	Pumpman									6-WH Dump Truck				
16 P. Hall	14	Compressor	1:00 PM	7:00 PM	2 1/2	2		1 1/2			Furnace / Weeburner				
17											Tar Kettle - Trailer				
18											Welder with Truck				
19 C. Pereira	282	Dump Truck	7:00 AM	7:00 PM	3	2	5	1 1/2			Generator 5000 W				
20											Light Stands				

MATERIALS: All City Recycling

3 yds. debris # 108919	CON ED
5 yds. SAND # 108919	50%
14 yds. debris # 108998	
Gaffney Plumbing # 03010377	
1- 3" D.I.P.	
2- 3" 45° bends M.J.	
2- 3" 22 1/2° bends M.J.	
2- 3" sleeves M.J.	
12- 3" star Grip # 3000 Pack	
1- 4" D.I.P.	Picone van
2- 4" 11 1/4° bends M.J.	8- SAND bags
2- 4" sleeves M.J.	1- 14" Magum
12- 4" star Grip # 3000 Pack	Diana

SUBCONTRACTORS: Mr. John

DESCRIPTION OF WORK:	Continued Digging R/W		Move			
	trench by hand around rocks		DOT PERMIT #	H012014083004		
	+ stone + P.C.I. gas main + 12"		CODE 53 #	091046		
	C.I. water main approx 6' x 20' layed					048
	17'6" of 12" D.P.P. with (1) 12" valve H.T.					082
	+ dug out 3' x 4' services for building #1652 Park					
	Ave. to make ready to transfer to new main tomorrow					
UNUSUAL CONDITIONS	cleaned up job site + reset plates + made safe.					

SKETCH:

I hereby certify that I inspected the work described hereto, that the time and material records are accurate and correct, that the expeditious manner and the labor and equipment shown here were necessary for the proper execution of the work, except as

**NEW YORK CITY DEP.
TIME AND MATERIAL INSPECTOR'S DAILY REPORT**

Weather: 66°F Con 1+Clear Date: 4/20/14 Sat
 Location: Park Ave b/t E. 117 St to E. 116 St Loc #: 154
 Borough: Manhattan Contractor: J P PICONE Contract #: GE351

LABOR / NAME	LOCAL	TITLE	TIME		DEP		UTIL 1 ConEd		UTIL 2 EP-7		EQUIPMENT	QTY	DEP	UTIL 1 UTIL 2	
			IN	OUT	ST	OT	ST	OT	ST	OT				ST	OT
1		Super									Cat 446 Backhoe	1	2 1/2	4 1/2	2
2 A. Pirrone	731	Foreman	7AM	4:30pm	2 1/2		4 1/2		2		Compressor 185	1	2 1/2	4 1/2	2
3	1536	Timberman									Cut-Off Saw				
4 D. Buon Frisco	731	Laborer	7AM	4:30pm	2 1/2		4 1/2		2		Chain Saw				
5 D. Dzanowskyj	731	Laborer	7AM	4:30pm	2 1/2		4 1/2		2		Target Saw / Size =				
6 M Del Rio Jr	731	Laborer	7AM	4:30pm	2 1/2		4 1/2		2		3" Trash Pump (w/ hoses)				
7 Carl Todd	731	Laborer	7AM	4:30pm	2 1/2		4 1/2		2		3" Mudsucker (w/ hoses)				
8 James Urti	731	Laborer	7AM	4:30pm	2 1/2		4 1/2		2		Roller 5T / Walk Behind				
9											Plate Tamper	1	2	4	2
10											Jumping Jack Tamper				
11	15	Maintenance									Utility Truck	1	2 1/2	4 1/2	2
12 A. Casillo	15	Backhoe	7AM	4:30pm	2 1/2		4 1/2		2		Boom Truck				
13	282	Boom Truck									2" Pump (w/ hose)				
14	15	Lights									10-WH Dump Truck	1	2 1/2	4 1/2	2
15	15	Pumpman									6-WH Dump Truck				
16	14	Compressor									Furnace / Weedburner				
17											Tar Kettle - Trailer				
18											Welder with Truck				
19 Carlos Pereira	282	Dump Truck	7AM	4:30pm	2 1/2		4 1/2		2		Generator 5000 W	1	2 1/2	4 1/2	2
20											Light Stands				

MATERIALS:

ALL City Recycling Ticket # 109054 6CY Mix Dump
 8 Spikes
 10 Each Cold Patch

Light Tower				
Traffic Signs (sf)	9	8 1/2	4 1/2	2
Arrow Board	1	2 1/2	4 1/2	2
Traffic Cones	30	2 1/2	4 1/2	2
Traffic Barrels				
Bicycle Racks				
Timber Barricade				
Flashing Lights				
Steel Plates 1140SF		12 1/2	4 1/2	2
Wind Stands	1	2 1/2	4 1/2	2

SUBCONTRACTORS:


Mc. John

DESCRIPTION OF WORK:

Pirrone onsite to replace 12" CIP w/ 12" DIP on 1/2 Park Ave b/t E 116 St to E 117 St. 12" CIP w/ 12" DIP shut down @ 8am. 12" Valve S/O E 117 St went holding and maintenance crew called to location to work valve and change nut on valve and fill again & holding shut down suspended and will reschedule to pop up valve. Contractor directed to hand excavate trench to expose 6" GIM Brown ConEd Bricks at the intersection of Park Ave + E 117 St.

UNUSUAL CONDITIONS

SKETCH:

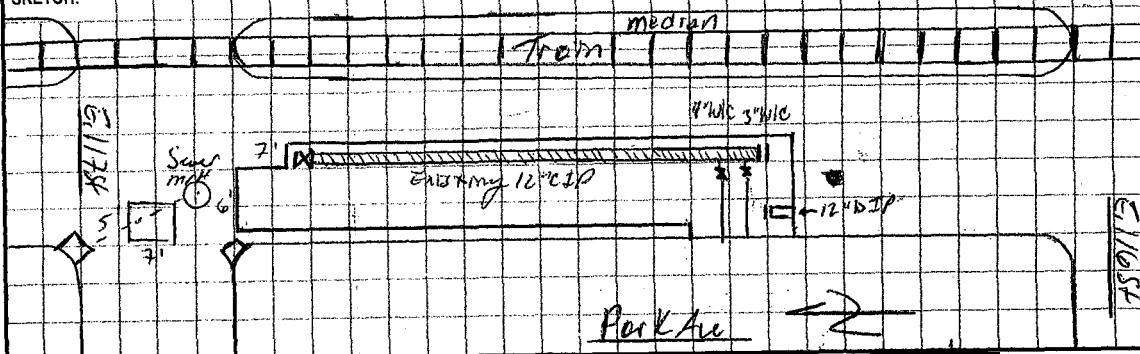

I hereby certify that I inspected the work described hereto, that the time and material records are accurate and correct, that the work was performed in an expeditious manner and the labor and equipment shown here were necessary for the proper execution of the work, except as noted.

NY DEP REP:

CONTRACTOR REP:

**NEW YORK CITY DEP.
TIME AND MATERIAL INSPECTOR'S DAILY REPORT**

Weather: Clear, 65° F
Location: Pine Ave, 616 E 116 St & E 117 St
Borough: Manhattan

Date: 4/28/14, Monday
Loc #: 154
Contract #: 6E351

Contractor: J P PICONE

LABOR / NAME	LOCAL	TITLE	TIME		DEP		UTIL 1 ConEd EP-7		UTIL 2		EQUIPMENT	QTY	DEP	ConEd	
			IN	OUT	ST	OT	ST	OT	ST	OT				UTIL 1 EP-7	UTIL 2
1 A. Vilmar		Super	11 AM	3:30 AM							Cat 400 315 hyd	1	8 1/2	3	
2 Carlos Almeida	1010	Foreman	7 AM	7 PM	6	2 1/2	2	1			Compressor 185	1	8 1/2	2	
3 L. Quigley	1536 856	Timberman	7 AM	7 PM	6	2 1/2	2	1			Cut-Off Saw				
4 P. Silva	731	Laborer	7 AM	7 PM	6	2 1/2	2	1			Chain Saw	2	8 1/2	3	
5 F. Silva	731	Laborer	7 AM	7 PM	6	2 1/2	2	1			Target Saw / Size =				
6 V. Pineda	731	Laborer	7 AM	7 PM	6	2 1/2	2	1			3" Trash Pump (w/ hoses)				
7 F. Anela	731	Laborer	7 AM	7 PM	6	2 1/2	2	1			3" Mudsucker (w/ hoses)				
8 V. Saune	856	Laborer	7 AM	7 PM	6	2 1/2	2	1			Roller 5T / Walk Behind				
9											Plate Tamper				
10											Jumping Jack Tamper				
11											Utility Truck	1	8 1/2	3	
12 R. Murrafero	15	Backhoe	7 AM	7 PM	6	2 1/2	2	1			Boom Truck				
13	282	Boom Truck									2" Pump (w/ hose)				
14	15	Lights									10-WH Dump Truck				
15	15	Pumpman									6-WH Dump Truck				
16 P. Hall	14	Compressor	7 AM	7 AM	3 1/2		2				Furnace / Weederburner				
17											Tar Kettle - Trailer				
18											Welder with Truck				
19	282	Dump Truck									Generator 5000 W	1	8 1/2	3	
20											Light Stands				
MATERIALS:											Light Tower				
All City Recycling # 109087 > 16' 1/2" x 16'											Traffic Signs (sf)				
# 109156 > 1/2" x 1/2" x 1/2"											Arrow Board				
# 109130 > 1/2" x 1/2" x 1/2"											Traffic Cones	15	8 1/2	3	
4 ea 3" x 12" x 16"											Traffic Barrels				
3 ea 2" x 10" x 16"											Bicycle Racks				
											Timber Barricade				
											Flashing Lights				
											Steel Plates	176	2 1/2	3	
											Wind Stands				
											Steel plate				
											4 for 1/4"	176	2 1/2	3	
SUBCONTRACTORS: Mr. Sohn, - Scumella Truck # 152683, 12 1/2 hrs															
											Move Backhoe				
DESCRIPTION OF WORK: - Continued excavating truck, depth is at 16'											Move				
Supply for Con Ed 8" plastic pipe (EP-7 - 3 hrs), Con Ed insp: Brian											DOT PERMIT #				
CP # 646732 2 hrs											CODE 53 #				
UNUSUAL CONDITIONS															
SKETCH:															

I hereby certify that I inspected the work described hereto, that the time and material records are accurate and correct, that the work was done in an expeditious manner and the labor and equipment shown here were necessary for the proper execution of the work, except as noted.

**NEW YORK CITY DEP.
TIME AND MATERIAL INSPECTOR'S DAILY REPORT**

Weather: SUNNY 55°
 Location: PARK Ave. bet. E. 116th St. & E. 117th St.
 Borough: MANHATTAN Contractor: J P PICONE

Date: Mon. 4-28-19
 Loc #: 154
 Contract #: GE-351

LABOR / NAME	LOCAL	TITLE	TIME		DEP		UTIL 1 Con-Ed		UTIL 2		EQUIPMENT	QTY	DEP	UTIL 1	UTIL 2
			IN	OUT	ST	OT	ST	OT	ST	OT					
1 A. Xina		Super	7:00	11:00							Cat 446 Backhoe	1	4 1/2	7	
2 H. Piccone	731	Foreman	7:00	7:00	3	1 1/2	5	2			Compressor 185	1	1 1/2	4 1/2	
3	1536	Timberman									Cut-Off Saw				
4 DuBuonfrisco	731	Laborer	7:00	7:00	3	1 1/2	5	2			Chain Saw	1	1	7	
5 H. De Irio	731	Laborer	7:00	7:00	3	1 1/2	5	2			Target Saw / Size =				
6 D. Dzadosky Jr.	731	Laborer	7:00	7:00	3	1 1/2	5	2			3" Trash Pump (w/ hoses)				
7 J. Urli	731	Laborer	7:00	7:00	3	1 1/2	5	2			3" Mudsucker (w/ hoses)				
8 S. Sinahov	731	Laborer	7:00	7:00	3	1 1/2	5	2			Roller 5T / Walk Behind				
9											Plate Tamper	1	2		
10											Jumping Jack Tamper				
11											Utility Truck	1	4 1/2	7	
12 A. Casillo	15	Backhoe	7:00	7:00	3	1 1/2	5	2			Boom Truck	1	3	5	
13 D. Dzadosky	282	Boom Truck	7:00	3:00	3		5				2" Pump (w/ hose)				
14	15	Lights									10-WH Dump Truck	1	4 1/2	7	
15	15	Pumpman									6-WH Dump Truck				
16 P. Hall	14	Compressor	1:00	7:00		1 1/2	2 1/2	2			Furnace / Weederburner				
17											Tar Kettle - Trailer				
18											Welder with Truck				
19 C. Pereira	282	Dump Truck	7:00	7:00	3	1 1/2	2 1/2	2			Generator 5000 W	1	2		
20											Light Stands				
MATERIALS: All City Recycling 15 yds. debris # 109157 Piccone yard 8-R.R. spikes 2-super sacks Con Ed 500%											Light Tower				
											Traffic Signs (sf)				
											Arrow Board				
											Traffic Cones				
											Traffic Barrels				
											Bicycle Racks				
											Timber Barricade				
											Flashing Lights				
											Steel Plates				
											Wind Stands				
SUBCONTRACTORS: Mr. John															
DESCRIPTION OF WORK: Continued to dig & extend R/W trench another 27' x 6" around stone & rocks to approach 12" C.I. water main & 8" C.I. gas main to make ready for replacement, cleaned up job site & set plates & made safe. also set sheet piling in trench.											Move Backhoe				
											Move				
											DOT PERMIT #				
											CODE 53 #				
UNUSUAL CONDITIONS															
SKETCH:															

I hereby certify that I inspected the work described hereto, that the time and material records are accurate and correct, that expeditious manner and the labor and equipment shown here were necessary for the proper execution of the work, except

Weather: cloudy 50°
Location: Park Ave. bet. E. 116th St. + E. 117th St.
Borough: Manhattan Contractor: J P PICONE

Date: Tues. 4-29-14
Loc #: 154
Contract #: GE-351

[illegible]

I hereby certify that I inspected the work described hereto, that the time and material records are accurate and correct, that the work was done in an expeditious manner and the labor and equipment shown here were necessary for the proper execution of the work, except

in an

**NEW YORK CITY DEP.
TIME AND MATERIAL INSPECTOR'S DAILY REPORT**

Weather: Cloudy, 47°F
Location: Park Ave 6/6 E116 St & E117 St
Borough: Manhattan

Date: 4/29/14, Tuesday
Loc #: 154
Contract #: 6E351

Contractor: J P PICONE

LABOR / NAME	LOCAL	TITLE	TIME		DEP		UTIL 1		UTIL 2		EQUIPMENT	QTY	DEP	UTIL 1	UTIL 2
			IN	OUT	ST	OT	ST	OT	ST	OT					
1		Super									Cat 400 Backhoe 315 exc	1	8 1/2	3	
2 Carlos Almeida	1010	Foreman	7 AM	7 PM	6	2 1/2	2	1			Compressor 185	1	3 1/2	2	
3 L. Quirphe	1010	Timberman	7 AM	7 PM	6	2 1/2	2	1			Cut-Off Saw				
4 P. Caribaldi	731	Laborer	7 AM	7 PM	6	2 1/2	2	1			Chain Saw	1	8 1/2	3	
5 F. Silva	731	Laborer	7 AM	7 PM	6	2 1/2	2	1			Target Saw / Size =				
6 V. Pineda	731	Laborer	7 AM	7 PM	6	2 1/2	2	1			3" Trash Pump (w/ hoses)				
7 F. Arena	731	Laborer	7 AM	7 PM	6	2 1/2	2	1			3" Mudsucker (w/ hoses)				
8 V. Sayne	1356	Laborer	7 AM	7 PM	6	2 1/2	2	1			Roller 5T / Walk Behind				
9											Plate Tamper	1	8 1/2	3	
10											Jumping Jack Tamper				
11											Utility Truck	1	8 1/2	3	
12 R. Mazzaferro	15	Backhoe	7 AM	7 PM	6	2 1/2	2	1			Boom Truck				
13	282	Boom Truck									2" Pump (w/ hose)				
14	15	Lights									10-WH Dump Truck	2			
15	15	Pumpman									6-WH Dump Truck				
16 P. Hall	14	Compressor	7 AM	7 PM	6	3 1/2	2				Furnace / Weederburner				
17											Tar Kettle - Trailer				
18											Welder with Truck				
19	282	Dump Truck									Generator 5000 W	1	8 1/2	3	
20											Light Stands				
MATERIALS:											Light Tower				
All City Recycling # 109241, 6 mtr (cont), 12 bleed (cont)											Traffic Signs (sf)				
# 109220, 1 mtr (cont)											Arrow Board				
3 ea 4"x8"x3/4" plywood											Traffic Cones	4	15		
4 ea 3"x10"x16"											Traffic Barrels				
											Bicycle Racks				
											Timber Barricade				
											Flashing Lights				
											Steel Plates	176	176	21	3
											Wind Stands				
											Blow fan	8 1/2			
											air monitor	8 1/2			
SUBCONTRACTORS: - Mr. John Scaramello truck # 152628											Move Backhoe				
											Move				
DESCRIPTION OF WORK: - Continued excavating sewer trench depth at 17'											DOT PERMIT #				
- Reached top of sewer, clearing off rocks & dirt off sewer											CODE 53 #				
- Support for con Ed 8" plastic pipe (EP-7 3/4) (con Ed Inspection CP # 1646 737 2385)															
- Prepared for rain on Wednesday															
UNUSUAL CONDITIONS - Found large 6' x 2' x 2' rock on top of sewer															
SKETCH:															

I hereby certify that I inspected the work described hereto, that the time and material records are accurate and correct, that the work was done in an expeditious manner and the labor and equipment shown here were necessary for the proper execution of the work, except as noted.

TIME AND MATERIAL INSPECTOR'S DAILY REPORT

Weather: Rain, 45°F

Location: Park Ave b/w E 116 St & E 117 St

Borough: Manhattan

Date: 4/30/14, Wednesday

Loc #: 154

Contract #: CE-351

Contractor: J P PICONE

				TIME		DEP		UTIL 1 CmEd		UTIL 2 CmEd EP-7				CmEd		
LABOR / NAME		LOCAL	TITLE	IN	OUT	ST	OT	ST	OT	ST	OT	EQUIPMENT	QTY	DEP	UTIL 1 CmEd	UTIL 2 EP-7
1			Super									Cat Backhoe 315	1	4 1/2	2 1/2	1
2	C. Almeida	1010	Foreman	7AM	8:30AM	4 1/2		2 1/2		1		Compressor 185	1	4 1/2	2 1/2	1
3	L. Quizphe	ISS6	Timberman	7AM	3:30 PM	4 1/2		2 1/2		1		Cut-Off Saw	1	4 1/2	2 1/2	1
4	P. Garibaldi	731	Laborer	7AM	2:30 PM	4 1/2		2 1/2		1		Chain Saw	1	4 1/2	2 1/2	1
5	F. Silva	731	Laborer	7AM	2:30 PM	4 1/2		2 1/2		1		Target Saw / Size =				
6	V. Pineda	731	Laborer	7AM	3:30 PM	4 1/2		2 1/2		1		3" Trash Pump (w/ hoses)				
7	F. Arena	731	Laborer	7AM	2:30 PM	4 1/2		2 1/2		1		3" Mudsucker (w hoses)				
8	W. Saume	ISS6	Laborer	7AM	3:30 PM	4 1/2		2 1/2		1		Roller ST / Walk Behind				
9												Plate Tamper	1	4 1/2	2 1/2	1
10												Jumping Jack Tamper				
11												Utility Truck	1	4 1/2	2 1/2	1
12	R. Muzzateto	15	Backhoe	7AM	3:30 PM	4 1/2		2 1/2		1		Boom Truck	1	4 1/2	2 1/2	1
13	D. Bzadosky Sr	282	Boom Truck	7AM	3:30 PM	4 1/2		2 1/2		1		2" Pump (w/ hose)				
14		15	Lights									10-WH Dump Truck				
15		15	Pumpman									6-WH Dump Truck				
16		14	Compressor									Furnace / Weedburner				
17												Tar Kettle - Trailer				
18												Welder with Truck				
19		282	Dump Truck									Generator 5000 W				
20												Light Stands				

MATERIALS: AlCl₃ P₂O₅

-All City Recycling: 10 yd³ Mud (low⁴), #109317 (Low Fed pay 1/2)

• PVC pipe - 20' long, 12" Ø

$$b \text{ en } 3^n \times 12^n \times 20^n$$
$$4 \approx 2^2 \times 10^{12} \times 16^7$$

516 160 marks

SUBCONTRACTORS: - Mr. John S. Swannell. Truck # 15 2207 10/1/82

DESCRIPTION OF WORK: - Constructed temporary brace at bottom of sewer trench due to rain, worked outside of sewer trench, hand excavated on Edison 8" cast iron pipe around sewer ~~at~~ MH #011744, found that the pipe off sets around the MH, so no need to break out part of the MH leveled area where new Con Ed 8" plastic pipe will be laid

UNUSUAL CONDITIONS

SKETCH:

I hereby certify that I inspected the work described hereto, that the time and material records are accurate and correct, that the work was done in an expeditious manner and the labor and equipment shown here were necessary for the proper execution of the work, except as noted.

NEW YORK CITY DEPT.
TIME AND MATERIAL INSPECTOR'S DAILY REPORT

Weather: Rain, 45°F
Location: Park Ave, b/t E 116 St & E 117 St
Borough: Manhattan

Date: 4/30/14, Wednesday
Loc #: 154
Contract #: 62-351

[illegible]

I hereby certify that I inspected the work described hereto, that the time and material records are accurate and correct, that the cost was reasonable and the work was completed in an expeditious manner and the labor and equipment shown here were necessary for the proper execution of the work, except as noted.

CONTRACTOR REP:

**NEW YORK CITY DEP.
TIME AND MATERIAL INSPECTOR'S DAILY REPORT**

Weather: Cloudy Clear, 60° F

Location: Park Ave 1/4 E 116 St & E 117 St

Borough: Manhattan

Contractor: J P PICONE

Date: 5/1/14, Thursday

Loc #: 154

Contract #: 6E351

LABOR / NAME	LOCAL	TITLE	TIME		DEP		UTIL 1 Can Ed		UTIL 2 Can Ed		EQUIPMENT	QTY	DEP	UTIL 1 Can Ed		UTIL 2 Can Ed	
			IN	OUT	ST	OT	ST	OT	ST	OT				ST	OT	ST	OT
1		Super									Cat 446 Backhoe	1	3 1/2	7	1		
2	A. P. P. ONE	731 Foreman	7 AM	7 PM	2	1 1/2	5	2	1		Compressor 185	1	1 1/2	4	1		
3		1536 Timberman									Cut-Off Saw						
4	M. Del Rio	731 Laborer	7 AM	7 PM	2	1 1/2	5	2	1		Chain Saw	1	3 1/2	7	1		
5	Carl Todd	731 Laborer	7 AM	7 PM	2	1 1/2	5	2	1		Target Saw / Size =						
6	Safet Sinaadov	731 Laborer	7 AM	7 PM	2	1 1/2	5	2	1		3" Trash Pump (w/ hoses)						
7	Nomoko T	731 Laborer	7 AM	7 PM	2	1 1/2	5	2	1		3" Mudsucker (w/ hoses)						
8											Roller 5T / Walk Behind						
9											Plate Tamper						
10											Jumping Jack Tamper						
11											Utility Truck	1	3 1/2	7	1		
12	A. Casillo	15 Backhoe	7 AM	7 PM	2	1 1/2	5	2	1		Boom Truck	1		3	1		
13	D. Dzadosky SR	282 Boom Truck	7 AM	7 PM				3	1		2" Pump (w/ hose)						
14		15 Lights									10-WH Dump Truck	1	3 1/2	7	1		
15		15 Pumpman									6-WH Dump Truck						
16	P. Hall	14 Compressor	7 AM	1 PM	1/2		4		1		Furnace / Weederburner						
17											Tar Kettle - Trailer						
18											Welder with Truck						
19	C. Lopez	282 Dump Truck	7 AM	7 PM	2	1 1/2	5	2	1		Generator 5000 W						
20											Light Stands						

MATERIALS:

Durante Bros # 128725, 10 yd reg

Light Tower			
Traffic Signs (sf)			
Arrow Board	9	3 1/2	7 1
Traffic Cones	1	16	7 1
Traffic Barrels	30	3 1/2	7 1
Bicycle Racks			
Timber Barricade			
Flashing Lights			
Steel Plates (280)	1280	16	7 1
Wind Stands	1	3 1/2	7 1

SUBCONTRACTORS:

Mr. John

Move Backhoe

Move

DESCRIPTION OF WORK: - Continued hand excavating around Can Ed 8" plastic pipe
for bdy # 1652, Park Ave. - Took out 8" cast iron pipe in sewer MH # M101744.
Repaired MH with brick + mortar (Can Ed pay labor) - 10 AM. Can Ed came.
Cut the Can Ed 8" CIP from pre existing cut to cap pipe at intersection 24 pieces.
Cleared out area where w/c of bdy # 1642 will be installed, placed 4" w/c sleeve on 12" DIP, 9'5" N of
BL.
Installed 20' 4" of 12" DIP from new 12" valve to northward to intersection, 4'5" CL, 3.5' depth.

DOT PERMIT #

CODE 53 #

UNUSUAL CONDITIONS

SKETCH:

I hereby certify that I inspected the work described hereto, that the time and material records are accurate and correct, that the contract was executed in an expeditious manner and the labor and equipment shown here were necessary for the proper execution of the work, except as noted.

NY DEP REP: _____

CONTRACTOR REP: _____

NEW YORK CITY DEP.

Contract #: 6E351

649. *End*

CONTRACTOR REP:

Weather: cloudy 60°
Location: Park Ave. bet. E. 116th St. & E. 117th St.
Borough: MANHATTAN Contractor: J P PICONE

Date: Fri. 5-2-14
Loc #: 154
Contract #: GE-351

LABOR / NAME	LOCAL	TITLE	TIME		DEP		UTIL 1		UTIL 2		EQUIPMENT	QTY	DEP	UTIL 1	UTIL 2
			IN	OUT	ST	OT	ST	OT	ST	OT					
1 A. YIMAZ		Super	7:00	11:00	4						Cat Backhoe	3/5	1	7	3
2 C. ALMEIDA	1010	Foreman	7:00	5:30	6	1	2	1			Compressor 185		1	2	2
3 V. SAIME	1585	Timberman	7:00	5:30	6	1	2	1			Cut-Off Saw				
4 P. GARIBALDI	731	Laborer	7:00	5:30	6	1	2	1			Chain Saw	2	7	3	
5 F. ARENA	731	Laborer	7:00	5:30	6	1	2	1			Target Saw / Size =				
6 F. SILVA	731	Laborer	7:00	5:30	6	1	2	1			3" Trash Pump (w/ hoses)				
7 V. PIVERA	731	Laborer	7:00	5:30	6	1	2	1			3" Mudsucker (w/ hoses)				
8		Laborer									Roller 5T / Walk Behind				
9 L. QUIRYE	1516	Timb	7:00	5:30	6	1	2	1			Plate Tamper				
10											Jumping Jack Tamper				
11		315									Utility Truck	1	7	3	
12 R. MAZZAFERRO	15	Booth	7:00	5:30	6	1	2	1			Boom Truck				
13	282	Boom Truck									2" Pump (w/ hose)				
14	15	Lights									10-WH Dump Truck				
15	15	Pumpman									6-WH Dump Truck				
16 P. HALL	14	Compressor	7:00	11:00	2		2				Furnace / Weedburner				
17											Tar Kettle - Trailer				
18											Welder with Truck				
19	282	Dump Truck									Generator 5000 W	1	7	3	
20											Light Stands				
MATERIALS: Durante											Light Tower				
18 yds. sand # 658592											Traffic Signs (sf)				
10 yds. debris # 658591											Arrow Board				
											Traffic Cones				
											Traffic Barrels				
											Bicycle Racks				
Picone yard											Timber Barricade				
2-bags cement Portland 80/60											Flashing Lights				
18-bricks											Steel Plates	1	7	3	
											Wind Stands				
											Blower	1	7	3	
											FAN	1	7	3	
SUBCONTRACTORS: Mr. John															
(i) SCARAMELLA Truck 7 hrs. DEP															
3 hrs. EP.7											Move Backhoe				
DESCRIPTION OF WORK: Continued to dig trench											Move				
to uncover sewer around											DOT PERMIT #				
to 4 o'clock. found damage &											CODE 53 #				
corrected. cleaned up job site															
& made safe.															
UNUSUAL CONDITIONS															
SKETCH:															

I hereby certify that I inspected the work described hereto, that the time and material records are accurate and correct, that the expeditious manner and that [REDACTED] for the proper execution of the work, except as noted.

is work in an

NY FED DEF.

CONTRACTOR REF.

Weather: cloudy 60°
Location: Park Ave. bet. E. 116th St. & E. 117th St.
Borough: Manhattan Contractor: J P PICONE

Date: Fri 5-2-14
Loc #: 154
Contract #: GE-351

			TIME		DEP		UTIL 1 Cov. Ed		UTIL 2						
LABOR / NAME	LOCAL	TITLE	IN	OUT	ST	OT	ST	OT	ST	OT	EQUIPMENT	QTY	DEP	UTIL 1	UTIL 2
1		Super									Cat 446 Backhoe	1	4 1/2	4 1/2	
2	A. Pirrone	731 Foreman	7:00 AM	4:30 PM	4	1/2	4	1/2			Compressor 185	1	2	2	
3		1536 Timberman									Cut-Off Saw	1	4	4	
4	M. Detric	731 Laborer	7:00 AM	4:30 PM	4	1/2	4	1/2			Chain Saw				
5	D. Dzadosky Jr.	731 Laborer	7:00 AM	4:30 PM	4	1/2	4	1/2			Target Saw / Size =				
6	J. Urli	731 Laborer	7:00 AM	4:30 PM	4	1/2	4	1/2			3" Trash Pump (w/ hoses)				
7	C. Todd	731 Laborer	7:00 AM	4:30 PM	4	1/2	4	1/2			3" Mudsucker (w/ hoses)				
8	S. S. N. Hovic	731 Laborer	7:00 AM	4:30 PM	4	1/2	4	1/2			Roller 5T / Walk Behind				
9											Plate Tamper				
10											Jumping Jack Tamper				
11											Utility Truck	1	4 1/2	4 1/2	
12	G. Miranda	15 Backhoe	7:00 AM	4:30 PM	4	1/2	4	1/2			Boom Truck	1	4 1/2	4 1/2	
13	D. Dzadosky	282 Boom Truck	7:00 AM	4:30 PM	4	1/2	4	1/2			2" Pump (w/ hose)				
14		15 Lights									10-WH Dump Truck	1	2 1/2	2 1/2	
15		15 Pumpman									6-WH Dump Truck				
16	P. Hall	14 Compressor	11:00 AM	3:30 PM	2		2				Furnace / Weedburner				
17											Tar Kettle - Trailer				
18											Welder with Truck				
19	C. Pereira	282 Dump Truck	7:00 AM	12:30 PM	2 1/2		2 1/2				Generator 5000 W				
20											Light Stands				

MATERIALS: All City Recycling Co. Ed
10 yds. SAND # 109358 } 50%

plumbing #0018845
2-4" 45° bends A.J.
2-4" 22 1/2° bends A.J.
1-4" sleeve A.J.
10-star grip 3000 pack

SUBCONTRACTORS: *Mr. John*

DESCRIPTION OF WORK:

DESCRIPTION OF WORK:	Move						
	DOT PERMIT #	1402014083004					
	CODE 53 #	091046					
	Resealed, & removed the plates from truck & removed (4) pieces of P.I. C.I. gas approx 41' total. On Elmer water layer 10.6' of P.I. plastic gas main. Had DEP guys drill 4" wet connection for building # 1622 Park Ave. & then tied in with (2) 4" 45' to the H.J. & 4' 3" of 4" D.I.P. covered gas main with gas. cleaned up & ate + reset plates & made safe.						
UNUSUAL CONDITIONS							

SKETCH:

I hereby certify that I inspected the work described hereto, that the time and material records are accurate and correct, that the work was done in an expeditious manner and that no other equipment or tools were necessary for the proper execution of the work, except as noted.

**NEW YORK CITY DEP.
TIME AND MATERIAL INSPECTOR'S DAILY REPORT**

Weather: 60°F Cool + Clear

Location: Park Ave 6th E 116 St to E 117 St

Borough: Manhattan

Date: 5/3/14 SAT

Loc #: 154

Contractor: J P PICONE

Contract #: GE351

LABOR / NAME	LOCAL	TITLE	TIME		DEP		UTIL 1		UTIL 2		EQUIPMENT	QTY	DEP	UTIL 1	UTIL 2
			IN	OUT	ST	OT	ST	OT	ST	OT					
1		Super									Cat Backhoe / MS 15	1	5 1/2	6	
2	Carlos A. Luque	1010 Foreman	7 AM	7 PM	5 1/2		6				Compressor 185	1	5 1/2	6	
3	Victor Saumle	1536 Timberman	7 AM	7 PM	5 1/2		6				Cut-Off Saw				
4	Fran Arena	731 Laborer	7 AM	7 PM	5 1/2		6				Chain Saw	2	5 1/2	6	
5	Fernando Silva	731 Laborer	7 AM	7 PM	5 1/2		6				Target Saw / Size =				
6	Victor Pineda	731 Laborer	7 AM	7 PM	2		6				3" Trash Pump (w/ hoses)				
7	Yanguin Tavares	1010 Laborer	7 AM	7 PM	5 1/2		6				3" Mudsucker (w/ hoses)				
8		Laborer									Roller 5T / Walk Behind				
9	Daniel Reyes	1556 Timberman	7 AM	7 PM	5 1/2		6				Plate Tamper				
10											Jumping Jack Tamper	1	5 1/2	6	
11		15 Maintenance									Utility Truck	1	5 1/2	6	
12	George Miranda	15 Backhoe	7 AM	7 PM	5 1/2		6				Boom Truck				
13		282 Boom Truck									2" Pump (w/ hose)				
14		15 Lights									10-WH Dump Truck	1	3	6	
15		15 Pumpman									6-WH Dump Truck				
16		14 Compressor									Furnace / Weederburner				
17	Rocco Mazzatiero	15 315	7 AM	7 PM	5 1/2		6				Tar Kettle - Trailer				
18											Welder with Truck				
19	Roger Labarge	282 Dump Truck	7 AM	7 PM	3		6				Generator 5000 W	1	5 1/2	6	
20											Light Stands				

MATERIALS:

Durante Ticket 18 yd Sand m # 658679
 " " " " " # 658678
 " " " " " # 658748
 " " " " " # 658671
 " " " " " # 658721
 " " " " " # 126882

All City Recycling Ticket # 109419 In: 18 yd Item # 4

Light Tower
 Traffic Signs (sf)
 Arrow Board
 Traffic Cones
 Traffic Barrels
 Bicycle Racks
 Timber Barricade
 Flashing Lights
 Steel Plates
 Wind Stands
 CAT 440 1 5 1/2 6

SUBCONTRACTORS:

S. Scaramella Ticket # 152727 12 hr
 Mr. Sohn.

Move Backhoe
 Move


DESCRIPTION OF WORK:

Backfill sewer trench w/ sand and clean fill from Sta Q+64 to Q+86. Remove timber sheeting from trench. Lift gas main exposed for repair.

DOT PERMIT #
 CODE 53 #

UNUSUAL CONDITIONS

SKETCH:

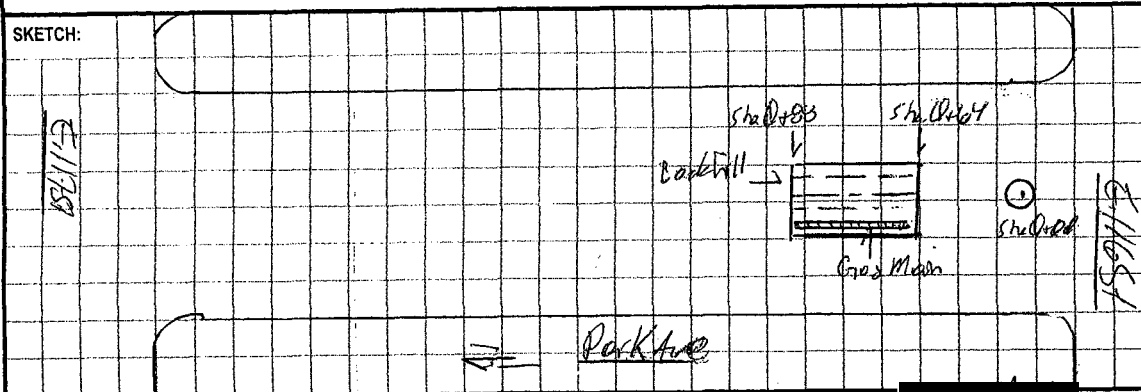

I hereby certify that I inspected the work described hereto, that the time and material records are accurate and correct, that the work was done in an expeditious manner and that the necessary safety measures were necessary for the proper execution of the work, except as noted.

NY DEP REP: _____

CONTRACTOR REP: _____

**NEW YORK CITY DEP.
TIME AND MATERIAL INSPECTOR'S DAILY REPORT**

Weather: 60°F Cool + Clear
Location: Park Ave b/t E 116 St to E 117 St
Borough: Manhattan

Date: 5/13/14 Sat
Loc #: 154
Contract #: 6E351

Contractor: J P PICONE

LABOR / NAME	LOCAL	TITLE	TIME		DEP		UTIL 1 Con EO		UTIL 2 51-7		EQUIPMENT	QTY	DEP	UTIL 1/UTIL 2	
			IN	OUT	ST	OT	ST	OT	ST	OT				UTIL 1	UTIL 2
1		Super									Cat 446 Backhoe	1	4 1/2	6	1
2	A. Pirrone	731 Foreman	7am	7pm	4 1/2		6				Compressor 185	1	4 1/2	6	1
3		1536 Timberman									Cut-Off Saw	1	4 1/2	6	1
4	D. Dzadousky	731 Laborer	7am	7pm	4 1/2		6				Chain Saw	1	4 1/2	6	1
5	M. Del Rio	731 Laborer	7am	7pm	4 1/2		6				Target Saw / Size =				
6	Carl Jodri	731 Laborer	7am	7pm	4 1/2		6				3" Trash Pump (w/ hoses)				
7	Donato Cesta	731 Laborer	7am	7pm	4 1/2		6				3" Mudsucker (w/ hoses)				
8	Safet Simanovici	731 Laborer	7am	7pm	4 1/2		6				Roller 5T / Walk Behind				
9	Sergio Ceirra	1010 Laborer	7am	7pm	4 1/2		6				Plate Tamper				
10	Robert Erga		10am	11:5am	1						Jumping Jack Tamper				
11		15 Maintenance									Utility Truck				
12	Al Vittorini	15 Backhoe	7am	7pm	4 1/2		6				Boom Truck				
13		282 Boom Truck									2" Pump (w/ hose)	2	4 1/2	6	1
14		15 Lights									10-WH Dump Truck	1	4 1/2	6	1
15	Nigel Lee	15 Pumpman	7am	3:30pm	1		6				6-WH Dump Truck				
16	Paul Hall	14 Compressor	7am	3:20pm	1		6				Furnace / Weedburner				
17											Tar Kettle - Trailer				
18											Welder with Truck				
19	Tony Amodea	282 Dump Truck	7AM	7PM	4 1/2		6				Generator 5000 W	1	4	6	1
20											Light Stands				

MATERIALS:

All City Recycling ticket # 109335 18yd Sand In
" " " " # 109402 18yd Sand In
" " " " # 109407 18yd Sand In

12 Sand Bags In

12 each 3"x10"x16' Long Lumber
126 nail 10" diameter

SUBCONTRACTORS:


Mr. Sohn

DESCRIPTION OF WORK:

DEP work and shut down 12" M/M @ 7am on Park Ave b/t
E 117 St to 119 Ave. Tr in new 12" DTP to existing 12" DTP
@ the intersection of Park Ave & E 117 St. also the 12" DTP installed previously
cut around 12" DTP in ground and bulkhead. Backfill w/ sand 1' around 12" DTP
and box out and bulkhead gas for repair. * Low Con paid additional 1hr
EP-7 for bulkhead for gas main *

UNUSUAL CONDITIONS

SKETCH:

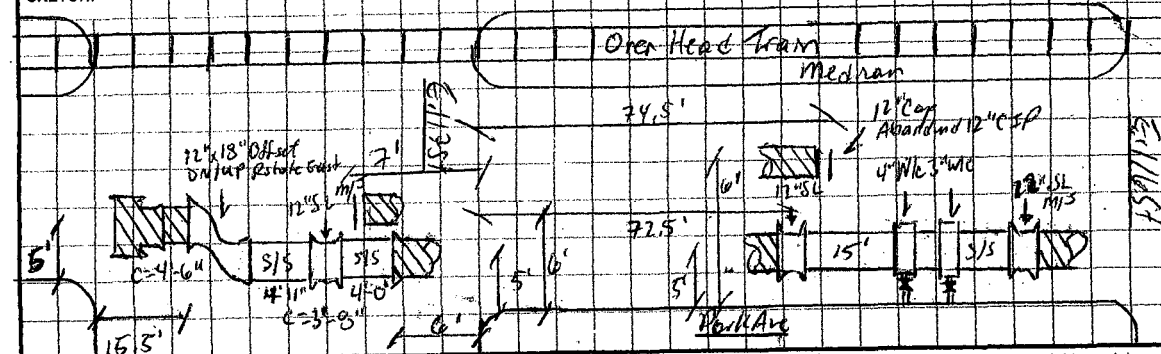

I hereby certify that I inspected the work described hereto, that the time and material records are accurate and correct, that the contractor progressed this work in an expeditious manner and the labor and equipment shown here were necessary for the proper execution of the work, except as noted.

NY DEP REP: _____

CONTRACTOR REP: _____

Weather: Clear

Location: Park Ave, b/t E 117 St & E 116 St

Borough: Marble Hill

Date: 5/5/14, Monday

Loc #:

Contract #: 6E351

[illegible]

I hereby certify that I inspected the work described hereto, that the time and material records are accurate and correct, that the work was done in an expeditious manner and the labor and equipment shown here were necessary for the proper execution of the work, except as noted.

NY DEP REP:

CONTRACTOR REP:

Contract #: GE 35

SKETCH:

CONTRACTOR REP:
