

**NEW YORK CITY DEP.
TIME AND MATERIAL INSPECTOR'S DAILY REPORT**

2.7

Weather: _____
Location: PARK AVE + E 116th ST
Borough: MANHATTAN

Date: 4-3-14
Loc #: 154
Contract #: 66-351

Contractor: J P PICONE

LABOR / NAME	LOCAL	TITLE	TIME		DEP		UTIL 1 (COWED)		UTIL 2 (EP-7)		EQUIPMENT	QTY	DEP	UTIL 1	UTIL 2
			IN	OUT	ST	OT	ST	OT	ST	OT					
1 A. YILMAZ		Super	7AM	11AM	4						Cat 446 Backhoe	1	4	4	2
* 2 A. PIRONE	731	Foreman	7AM	6:30	2	3	4		2		Compressor 185	1	2	4	2
3	1536	Timberman	7AM								Cut-Off Saw	1	2	4	2
* 4 D. BUENFISCO	731	Laborer	7AM	6:30	2	3	4		2		Chain Saw	1	2	4	2
5 M. DEL RIO	731	Laborer	7AM	5:30	2	2	4		2		Target Saw / Size =				
* 6 J. UPLI	731	Laborer	7AM	6:30	2	3	4		2		3" Trash Pump (w/ hoses)				
7 D. DZIWISKI	731	Laborer	7AM	5:30	2	2	4		2		3" Mudsucker (w/ hoses)				
8 C. TODD	73	Laborer	7AM	5:30	2	2	4		2		Roller 5T / Walk Behind				
9											Plate Tamper				
10											Jumping Jack Tamper	1	2	4	2
11											Utility Truck	1	5	4	2
12 H. CHASSILLO	15	Backhoe	7AM	5:30	2	2	4		2		Boom Truck	1	3	4	2
* 13 D. DZIWISKI	282	Boom Truck	7AM	6:30	2	3	4		2		2" Pump (w/ hose)	2	2	4	2
14	15	Lights									10-WH Dump Truck	1	2	4	2
15 N. LEE	15	Pumpman	7AM	5:30	2	2	4		2		6-WH Dump Truck				
16 P. HALL	14	Compressor	7AM	5:30	2		4		2		Furnace / Weedburner				
17											Tar Kettle - Trailer				
18											Welder with Truck				
19 C. PERLERA	282	Dump Truck	7AM	3:30	2		4		2		Generator 5000 W	1	5	4	2
20											Light Stands				

MATERIALS:

ACR 10 yards mix Debris (cont) Ticket # 167380

SAW CUT 30 LF @ 14" Diamond BLADE

* 103rd ST + WEST END AVE MANHATTAN

4 EA. COLD PATCH

STEEL PLATE

4/1 - 4/3

2 DAYS

SUBCONTRACTORS:

MR. JOHN.

Move Backhoe 446

Move

DESCRIPTION OF WORK: TO ELIMINATE PUMPING ON PARK AVE

CREW EXCAVATED AND CUT AN CARPET 12" W/M
ON E 116th ST.


DOT PERMIT #

CODE 53 #

- CREW ORDERED TO REPAIR ROADWAY ON 103rd ST + WEST END AVE
PLACED COLD PATCH

USUAL CONDITIONS CONSID THE 4 HOURS.
COWED EP-7 2 HOURS.

SKETCH:

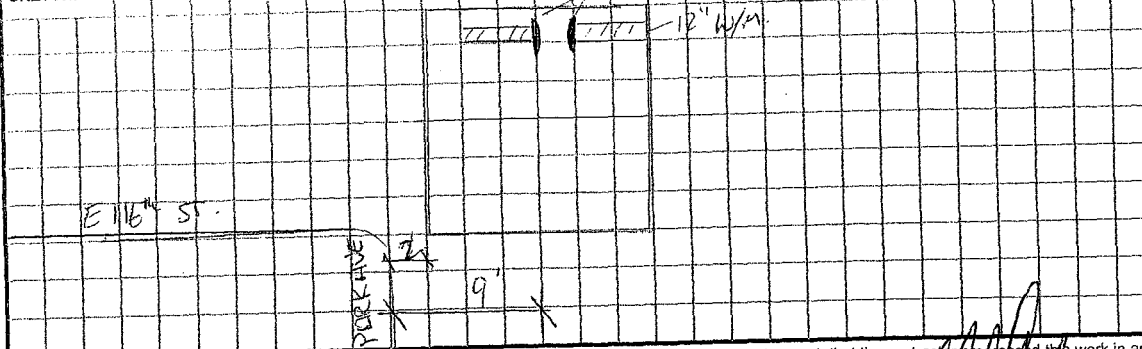

I hereby certify that I inspected the work described here to, that the time and material records are accurate and correct, that the contractor performed this work in an expeditious manner and the labor and equipment shown here were necessary for the proper execution of the work, except as noted:

NY DEP REP: _____

CONTRACTOR REP: _____

NEW YORK CITY DEP.

TIME AND MATERIAL INSPECTOR'S DAILY REPORT

Weather:

Location: PARK AVE + ELLIOT ST.

Borough: MANHATTAN

Contractor: J P PICONE

Date: 4-4-14.

Loc #: 154

Contract #: GE-351

C.E EP-7

MATERIALS:

ACR 13 yd Mix Debris (out) Ticket 167446.

Saw cut 39 LF @ 14" Diamond BLADE

20 Pcs. 3X10X16 Ckt Lumber

16. Pound 16 D NALL

SUBCONTRACTORS:

MR. JOHNS

DESCRIPTION OF WORK:

CREW EXCAVATES TRENCH AND PREPARES
FOR PIPE WORK BY UNDERMINING EXISTING
12" PIPE. SCHEDULED SHUTDOWN FOR MONDAY 4-7-11.
PREPARED WORK SITE FOR INSTALLATION OF NEW 12" VALVE
HYD

DOT PERMIT #

CODE 53 #

USUAL CONDITIONS

EP-7 4 HOURS → BRIAN CONIED
T+E 1 HOUR

SKETCH:

I hereby certify that I inspected the work described hereto, that the time and material records are accurate and correct, that the contractor progressed this work in an expeditious manner and the labor and equipment shown here were necessary for the proper execution of the work, except as noted on the attached sheets.

NEW YORK CITY DEP.
TIME AND MATERIAL INSPECTOR'S DAILY REPORT

Location: PARK AVE + E 116th ST

Contractor: J P PICONE

Loc #: 154

Contract #: GE-351

LABOR / NAME		LOCAL	TITLE	TIME		DEP		UTIL 1 C.E		UTIL 2 EPT.		EQUIPMENT	QTY	DEP	UTIL 1		UTIL 2
				IN	OUT	ST	OT	ST	OT	ST	OT				UTIL 1	UTIL 2	
1	A. KIRNEZ		Super	7AM	4PM			3 1/2	2	3		Cat 446 Backhoe	1	3 1/2	2	3	
2	A. PIRONE	731	Foreman	7AM	4PM			8 1/2	2	3		Compressor 185	1	3	2	3	
3		1536	Timberman									Cut-Off Saw	1	3	2	3	
4	D. BIONFRISCO	731	Laborer	7AM	4PM			3 1/2	2	3		Chain Saw	1	3	2	3	
5	M. DEL RIO	731	Laborer	7AM	4PM			3 1/2	2	3		Target Saw / Size =					
6	J. URLI	731	Laborer	7AM	4PM			3 1/2	2	3		3" Trash Pump (w/ hoses)					
7	D. DZADZOWSKY	731	Laborer	7AM	4PM			3 1/2	2	3		3" Mudsucker (w/ hoses)					
8	C. Todd	731	Laborer	7AM	4PM			3 1/2	2	3		Roller 5T / Walk Behind					
9												Plate Tamper					
10												Jumping Jack Tamper					
11												Utility Truck	1	3 1/2	2	3	
12	G. MIRANDA	15	Backhoe	7AM	3PM			3 1/2	2	3		Boom Truck	1	3 1/2	2	3	
13	M. MACHADO	282	Boom Truck	7AM	4PM			3 1/2	2	3		2" Pump (w/ hose)					
14		15	Lights									10-WH Dump Truck	1	3 1/2	2	3	
15		15	Pumpman									6-WH Dump Truck					
16	P. HALL	14	Compressor	7AM	3PM			3 1/2	2	3		Furnace / Weedburner					
17												Tar Kettle - Trailer					
18												Welder with Truck					
19	A. AMEDEO	282	Dump Truck	7AM	4PM			3 1/2	2	3		Generator 5000 W					
20												Light Stands					

MATERIALS:

20 PC 3x10x16 Lumber

10 Pound NAIL.

SUBCONTRACTORS: MR. John

DESCRIPTION OF WORK: CONTRACTOR CONTINUES EXCAVATION OF TRENCH. PREPARED TRENCH AND UNDERMINES SECTIONS OF PIPE IN ORDER TO PREPARE FOR PIPE WORK ON MONDAY 4-7-14.
- Coordinated w/ Building representatives in regards Monday

UNUSUAL CONDITIONS

SKETCH:

I hereby certify that I inspected the work described hereto, that the time and material records are accurate and correct, that the work was done in an expeditious manner and the labor and equipment shown here were necessary for the proper execution of the work, except as noted.

**NEW YORK CITY DEP.
TIME AND MATERIAL INSPECTOR'S DAILY REPORT**

Weather: CLOUDY 50°F
Location: PARK AVE + E 116th ST.
Borough: MANHATTAN

Date: MONDAY 4-7-14
Loc #: 154
Contract #: GE-351

Contractor: J.P. PICONE

CE CP-7

LABOR / NAME	LOCAL	TITLE	TIME		DEP		UTIL 1 CE		UTIL 2 EP-7		EQUIPMENT	QTY	DEP	UTIL 1	UTIL 2
			IN	OUT	ST	OT	ST	OT	ST	OT					
1 A. Vilma2		Super	7AM	3:30	3		3		2		Cat 446 Backhoe	1	5	3	2
2 A. PIRROVE	731	Foreman	7AM	5:30	3	2	3		2		Compressor 185	1	3	3	2
3	1536	Timberman									Cut-Off Saw	1	3	3	2
4 D. BROWERSCZ	731	Laborer	7AM	5:30	3	2	3		2		Chain Saw	1	3	3	2
5 K. DEL RIO	731	Laborer	7AM	5:30	3	2	3		2		Target Saw / Size =				
6 J. WELT	731	Laborer	7AM	5:30	3	2	3		2		3" Trash Pump (w/ hoses)				
7 D. DZADOWSKY	731	Laborer	7AM	3:30	3		3		2		3" Mudsucker (w/ hoses)				
8 C. TODD	731	Laborer	7AM	5:30	3	2	3		2		Roller 5T / Walk Behind				
9											Plate Tamper				
10											Jumping Jack Tamper				
11											Utility Truck	1	5	3	2
12 A. CASSILLO	15	Backhoe	7AM	5:30	3	2	3		2		Boom Truck	1	3 1/2	3	2
13 D. DZADOWSKY	282	Boom Truck	7AM	4:00	3	1/2	3		2		2" Pump (w/ hose)	2	3	3	2
14	15	Lights									10-WH Dump Truck	1	5	3	2
15	15	Pumpman									6-WH Dump Truck				
16 D. HALL	14	Compressor	7AM	5:30	3		3		2		Furnace / Weedburner				
17											Tar Kettle - Trailer				
18											Welder with Truck				
19 C. PEREIRA	282	Dump Truck	7AM	5:30	3	2	3		2		Generator 5000 W	1	3	3	2
20											Light Stands				

MATERIALS:

ACR 18 yds SAND (in) Ticket # 107510.

ACR 7 yds Mix Debris (out) Ticket 107538.
18 yds Blend (in)

60 Piece 3x10x16"

8 BAG GID PATCH.

Light Tower				
Traffic Signs (sf)	9	5	3	2
Arrow Board				
Traffic Cones	30	5	3	2
Traffic Barrels				
Bicycle Racks				
Timber Barricade				
Flashing Lights				
Steel Plates	560	9	3	2
Wind Stands	1	5	3	2

STEEL PLATES 480 24"
1 DAY 4/6/14

SUBCONTRACTORS: MR. JOHN

DESCRIPTION OF WORK: SET UP HPT.


CHOPPED 5'x6' Feet.

HAND Excavation and cut out EX. HPT. / INSTALL 2 NEW VALVES
12" VALVE + 6" VALVE

UNUSUAL CONDITIONS

C.E = 3 HRS
EP-7 = 2 HRS

SKETCH:

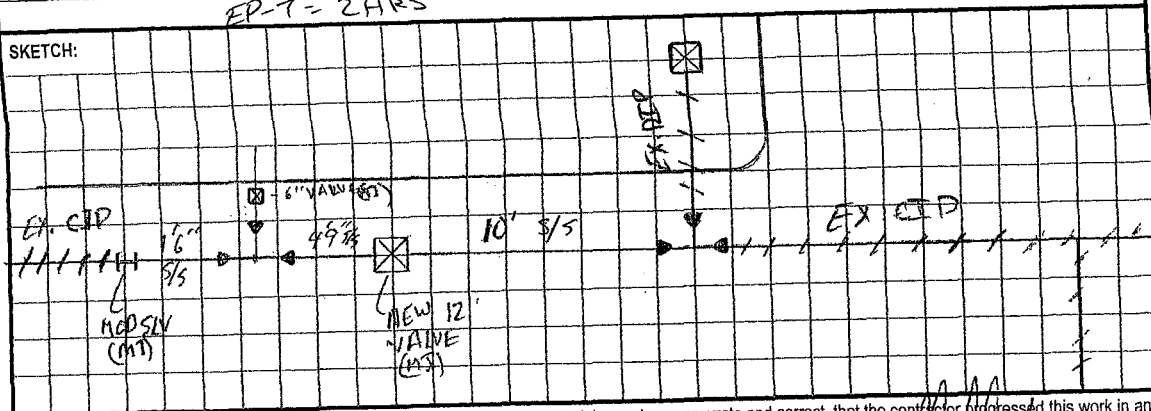

I hereby certify that I inspected the work described hereto, that the time and material records are accurate and correct, that the contractor progressed this work in an expeditious manner and the labor and equipment shown here were necessary for the proper execution of the work, except as

CONTRACTOR REP:

Weather: cloudy 50°
Location: Park Ave + E. 116 St.
Borough: Manhattan

Date: Tues. 4-8-14
Loc #: 154
Contract #: GE-351

I hereby certify that I inspected the work described hereto, that the time and material records are accurate and correct, that the contractor progressed this work in an expeditious manner and the labor and equipment shown here were necessary for the proper execution of the work, except as

Weather: Sunny 55°
Location: Park Ave. + E. 116th St.
Borough: Manhattan

Date: Wed. 4-9-14
Loc #: 154
Contract #: GE-351

MATERIALS:	All City Recycling
10 yds. debris #	107749
6 yds. SAND #	107701

Picone yard
5 cold patch
10 spikes

SUBCONTRACTORS: Mr. John

Move Backhoe					
Move					
DOT PERMIT #	Mo/201408300				
CODE 53 #	09104				

DESCRIPTION OF WORK: <i>Remove plates & lagged 8' of 12"</i>	Move			
<i>D.F. pipe into existing 12" 3-way M.T.</i>	DOT PERMIT #	<i>11012014083009</i>		<i>N/A</i>
<i>boxed out (1) side of trench for gas.</i>	CODE 53 #	<i>091046</i>		<i>N/A</i>
<i>+ shunted. removed other plate & started to</i>			<i>048</i>	<i>N/A</i>
<i>dig out R/W to make ready to install new</i>			<i>082</i>	<i>N/A</i>
<i>12" water & piping. started to sheet trench.</i>				
<i>cleaned up job site + reset shutes & made safe.</i>				

UNUSUAL CONDITIONS

SKETCH:

I hereby certify that I inspected the work described hereto, that the time and material records are accurate and correct, that the contractor progressed this work in an expeditious manner and the labor and equipment shown here were necessary for the proper execution of the work, except as noted.

**NEW YORK CITY DEP.
TIME AND MATERIAL INSPECTOR'S DAILY REPORT**

Weather: Sunny 50°
Location: Park Ave. + E. 116th St.
Borough: MANHATTAN

Date: Thurs. 4-10-14
Loc #: 154
Contract #: GE-351

Contractor: J P PICONE

LABOR / NAME	LOCAL	TITLE	TIME		DEP		UTIL 1 EP-7		UTIL 2 Conv. Ed		EQUIPMENT	QTY	DEP	UTIL 1	UTIL 2
			IN	OUT	ST	OT	ST	OT	ST	OT					
1 T. Canadula		Super	7:00 AM	3:30 PM	6						Cat 446 Backhoe	1	8 1/2	2	2
2 A. Pirrone	731	Foreman	7:00 AM	8:00 AM	6	2 1/2	1	1	1	1	Compressor 185	1	6	1	1
3	1536	Timberman									Cut-Off Saw	1	6	1	1
4 D. Buenfrisco	731	Laborer	7:00 AM	3:30 PM	6		1		1		Chain Saw	1	6	1	1
5 M. Delrio	731	Laborer	7:00 AM	8:00 AM	6	2 1/2	1	1	1	1	Target Saw / Size =				
6 D. Bladosky Jr.	731	Laborer	7:00 AM	8:00 AM	6	2 1/2	1	1	1	1	3" Trash Pump (w/ hoses)				
7 J. Urli	731	Laborer	7:00 AM	8:00 AM	6	2 1/2	1	1	1	1	3" Mudsucker (w/ hoses)				
8 C. Todd	731	Laborer	7:00 AM	8:00 AM	6	2 1/2	1	1	1	1	Roller 5T / Walk Behind				
9											Plate Tamper	1		1	1
10											Jumping Jack Tamper				
11											Utility Truck	1	8 1/2	2	2
12 A. Casillo	15	Backhoe	7:00 AM	8:00 AM	6	2 1/2	1	1	1	1	Boom Truck				
13	282	Boom Truck									2" Pump (w/ hose)	1	4	2	2
14	15	Lights									10-WH Dump Truck	1	8	2	2
15	15	Pumpman									6-WH Dump Truck				
16 P. Hall	14	Compressor	7:00 AM	3:30 PM	6		1		1		Furnace / Weederburner				
17											Tar Kettle - Trailer				
18											Welder with Truck				
19 C. Pereira	282	Dump Truck	7:00 AM	7:30 AM	6	2 1/2	1	1	1	1	Generator 5000 W	1	4	2	2
20											Light Stands				

MATERIALS: All City Recycling
7 yds. debris # 107830
18 yds. sand # 107830

Picone yard
12 bags cold patch
10-16s. NAILS 16#
6- R.R. spike
20-3" x 10" x 8' lumber
7-14" cut off 6/16th MAGNUM 14

SUBCONTRACTORS: Mr. John

DESCRIPTION OF WORK: Removed R/W plates + continued excavating to make ready to install new 12" valve + piping. + continued sheet piling, lagged 27' 9" of 12" O.D. P. with (1) 12" 3-way M.S. + (1) 12" valve M.S. + (1) 12" sleeve M.S. put pressure on main to check joints + started to backfill with sand. cleared up site + reset plates + made safe.
UNUSUAL CONDITIONS: Had 36" of asphalt concrete + rock to break out over pipe at tie in of sleeve.

SKETCH:

I hereby certify that I inspected the work described hereto, that the time and material records are accurate and correct, that the work was done in an expeditious manner and that the work was done in accordance with the contract and the specifications for the work, except as noted.

**NEW YORK CITY DEP.
TIME AND MATERIAL INSPECTOR'S DAILY REPORT**

Weather: cloudy 61°
Location: Park Ave. + E. 116th St.
Borough: Manhattan

Date: Fri. 4-11-14
Loc #: 154
Contract #: GE-351

Contractor: J.P. PICONE

LABOR / NAME	LOCAL	TITLE	TIME		DEP		UTIL 1 Con-Ed		UTIL 2		EQUIPMENT	QTY	DEP	UTIL 1	UTIL 2
			IN	OUT	ST	OT	ST	OT	ST	OT					
1 T. Lapadula		Super	7:00 AM	3:20 PM	8						Cat 446 Backhoe	1	10 1/2	2	
2 H. Pirrone	731	Foreman	7:00 AM	6:00 PM	2	2 1/2	2				Compressor 185	1	8	2	
3	1536	Timberman									Cut-Off Saw	1	8	2	
4 D. Buoncrisico	731	Laborer	7:00 AM	6:00 PM	2	2 1/2	2				Chain Saw	1	8	2	
5 D. Dzadosky Jr.	731	Laborer	7:00 AM	6:00 PM	6	2 1/2	2				Target Saw / Size =				
6 J. Urli	731	Laborer	7:00 AM	6:00 PM	6	2 1/2	2				3" Trash Pump (w/ hoses)				
7 C. Todd	731	Laborer	7:00 AM	6:00 PM	6	2 1/2	2				3" Mudsucker (w/ hoses)				
8 R. Chashtis	1010	Laborer	7:00 AM	6:00 PM	6	2 1/2	2				Roller (ST) Walk Behind	1	8	2	
9											Plate Tamper	1	8	2	
10											Jumping Jack Tamper	1	8	2	
11											Utility Truck	1	10 1/2	2	
12 H. Casillo	15	Backhoe	7:00 AM	6:00 PM	6	2 1/2	2				Boom Truck	1	10 1/2	2	
13 D. Dzadosky	282	Boom Truck	7:00 AM	6:00 PM	6	2 1/2	2				2" Pump (w/ hose)				
14	15	Lights									10-WH Dump Truck	1	10 1/2	2	
15	15	Pumpman									6-WH Dump Truck				
16	14	Compressor									Furnace / Weedburner				
17 J. Devue	15	Roller	7:00 AM	6:00 PM	6	2					Tar Kettle - Trailer	1	8	2	
18											Welder with Truck				
19 C. Pereira	282	Dump Truck	7:00 AM	6:00 PM	6	2 1/2	2				Generator 5000 W				
20											Light Stands				

MATERIALS: All City Recycling
5 yds. debris # 107875
5 yds. blend # 107860
Ferrara Bros. # 1280674
7 yds. concrete 4000 PSI. Hi Early
CANAL ASPH IT
13.64 TONS 6' Etop # 260819
Picone yard
15 - gals A/C
4 - green placement markers
14" diamond blade cut POLIK

Light Tower
Traffic Signs (sf) 9 10 1/2 2
Arrow Board
Traffic Cones 30 10 1/2 2
Traffic Barrels
Bicycle Racks
Timber Barricade
Flashing Lights
Steel Plates
Wind Stands 1 10 1/2 2

SUBCONTRACTORS: Mr. John

Move Backhoe


Move

DOT PERMIT # 4012014083004
CODE 53 # 091046

DESCRIPTION OF WORK: Removed R/W plates + removed sheeting from trench + set gain line valve box. Holed out trench for Con Edison electric + at 3-way + finished backfilling. poured R/W base. did R/W cut breaks + laged 13.64 tons asphalt. top to center R/W 18' x 7' + 9' x 6' + 15' x 10' + 11' x 9' + 5' x 4' 1/2' x 4' 1/2'. All R/W joints switched plates for Con Edison. cleared work job site + made safe.

UNUSUAL CONDITIONS

SKETCH:

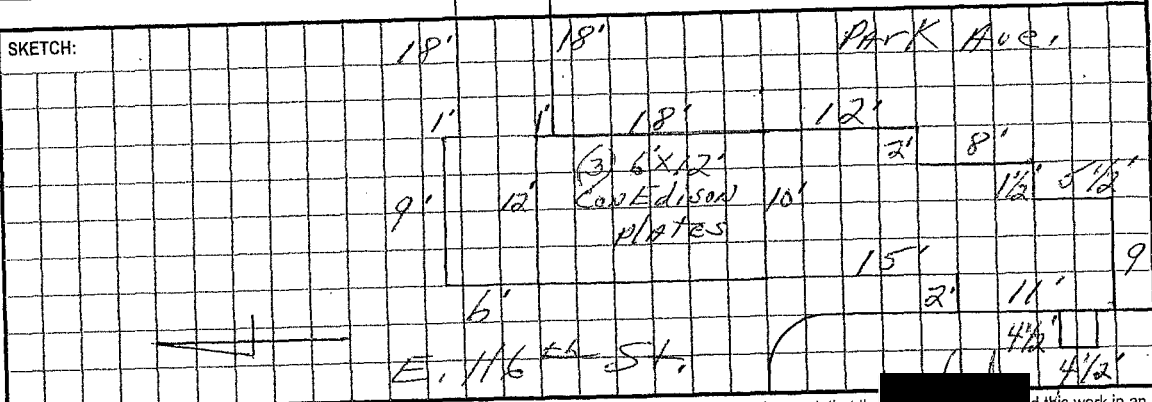

I hereby certify that I inspected the work described hereto, that the time and material records are accurate and correct, that the expeditious manner and the labor and equipment shown here were necessary for the proper execution of the work, except as

15th LOCATIONNEW YORK CITY DEP.
TIME AND MATERIAL INSPECTOR'S DAILY REPORTWeather: _____
Location: E. 116 - PARK AVE
Borough: MANHATTANDate: 4-12-2014
Loc #: _____
Contract #: GE351Contractor: J.P. PICONE

LABOR / NAME	LOCAL	TITLE	TIME		DEP		UTIL 1 CE		UTIL 2		EQUIPMENT	QTY	DEP	UTIL 1 CE	UTIL 2
			IN	OUT	ST	OT	ST	OT	ST	OT					
1		Super									Cat 446 Backhoe				
2	ALMEIDA C.	1010 Foreman	7:00	7:00	8.5	3					Compressor 185	1	8.5	3	
3	VICTOR SAUWE	1536 Timberman	7:00	7:00	8.5	3					Cut-Off Saw	1	8.5	3	
4	GARIBARDI PETER	731 Laborer	7:00	7:00	8.5	3					Chain Saw	1	8.5	3	
5	RENA FRANK	731 Laborer	7:00	7:00	8.5	3					Target Saw / Size =				
6	FERNANDO SILVA	731 Laborer	7:00	4:30	8.5	3					3" Trash Pump (w/ hoses)				
7	VICTOR PINEDA	731 Laborer	7:00	7:00	8.5	3					3" Mudsucker (w/ hoses)				
8		Laborer									Roller 5T / Walk Behind				
9											Plate Tamper				
10	DANIELS REYES	1536 Timb.	7:00	7:00	8.5	3					Jumping Jack Tamper				
11											Utility Truck	1	8.5	3	
12	HAZZATEERO M	15 Backhoe	7:00	7:00	8.5	3					Boom Truck				
13	LABERGE R	282 Boom Truck	7:00	3:30	5	3					2" Pump (w/ hose)				
14		15 Lights									10-WH Dump Truck	1	8.5	3	
15		15 Pumpman									6-WH Dump Truck				
16		14 Compressor									Furnace / Weedburner				
17											Tar Kettle - Trailer				
18											Welder with Truck				
19	PINNAECCHIA JT	282 Dump Truck	7:00	7:00	8.5	3					Generator 5000 W				
20											Light Stands				

MATERIALS: DEBRIS REMOVAL -
- 18 CY # DURANTE BROS Q129331 -
- 16 CY # ACR 107952

LUMBER (SHEETINGS)

3" x 10" x 20' - 48 PCS 40%
3" x 10" x 16' - 11 PCS 40%
12" x 12" x 13' - 8 PCS 40%SUBCONTRACTORS: MR JOHN * CROSSING INTERSECTION CON-ED
P/U 1 HR ELECTRIC - 4 HRS ERT
* SEWER LINE CON-ED P/U 2 HRS ELECTRICDESCRIPTION OF WORK: IN THE INTERSECTION - SET UP THE TRAFFIC
PATTERN. EXCAVATED TRENCH DUG AND EXPOSED 15' OF
OF CIP SHORED AND PLATED THE TRENCH. IFO BLDG 1642
DUG THE HOUSE CONNECTION. INSTALLED SHEETING AND MADE GENERAL CLEAN UP &
SECURED THE JOB AREA

UNUSUAL CONDITIONS

SKETCH:

I hereby certify that I inspected the work described hereto, that the time and material records are accurate and correct, that the contractor progressed this work in an expeditious manner and the labor and equipment shown here were necessary for the proper execution of the work, except as noted.

NEW YORK CITY DEP.
TIME AND MATERIAL INSPECTOR'S DAILY REPORT

Weather:

Location: E. 116 St & PARK AVE

Borough: MANHATTAN

Date: 4-12-2014/GA

Loc #:

Contract #: GE351

LABOR / NAME	LOCAL	TITLE	TIME		DEP	UTIL 1		UTIL 2		EQUIPMENT	QTY	DEP	UTIL 1		UTIL 2	
			IN	OUT		CE	EP	CE	EP							
1		Super								Cat 446 Backhoe	1	6.5	1	4		
2	PIRZONE A	731 Foreman	7:00	7:00	6.5	1	4			Compressor 185	1	6.5	1	4		
3		1536 Timberman	7:00							Cut-Off Saw	1	6.5	1	4		
4	BUONFRISCO D	731 Laborer	7:00	7:00	6.5	1	4			Chain Saw	1	6.5	1	4		
5	DZADASKY JR D	731 Laborer	7:00	7:00	6.5	1	4			Target Saw / Size = 36"	1	3	1	4		
6	DEL RIO M	731 Laborer	7:00	7:00	6.5	1	4			3" Trash Pump (w/ hoses)						
7	TODD C	731 Laborer	7:00	7:00	6.5	1	4			3" Mudsucker (w/ hoses)						
8	IRLY JAMES	731 Laborer	7:00	7:00	6.5	1	4			Roller 5T / Walk Behind						
9										Plate Tamper						
10										Jumping Jack Tamper						
11										Utility Truck	1	6.5	1	4		
12	CASILLAS A	15 Backhoe	7:00	7:00	6.5	1	4			Boom Truck	1	6.5	1	4		
13	MACHADO M	282 Boom Truck	7:00	7:00	6.5	1	4			2" Pump (w/ hose)						
14		15 Lights								10-WH Dump Truck	1	6.5	1	4		
15		15 Pumpman								6-WH Dump Truck						
16	HALL D	14 Compressor	7:00	7:00	6.5	1	4			Furnace / Weedburner						
17										Tar Kettle - Trailer						
18										Welder with Truck						
19	PEREIRA C	282 Dump Truck	7:00	7:00	6.5	1	4			Generator 5000 W						
20										Light Stands						
MATERIALS: DESIG OUT:										Light Tower						
- 3 CY # ACR 129330 -										Traffic Signs (sf)	9	6.5	1	4		
- 16 CY # ACR 107956 -										Arrow Board	2	6.5	1	4		
										Traffic Cones	30	6.5	1	4		
										Traffic Barrels						
										Bicycle Racks						
										Timber Barricade						
										Flashing Lights						
										Steel Plates SE	24	19	1	4		
										Wind Stands						
										XXX	X	X	X	X		
SUBCONTRACTORS: * SEC 1 st LOCATION										Move Backhoe						
* MR JOHN										Move						
DESCRIPTION OF WORK: SEE 1 st LOCATION										DOT PERMIT #						
										CODE 53 #						
UNUSUAL CONDITIONS																
SKETCH:																

I hereby certify that I inspected the work described hereto, that the time and material records are accurate and correct, that the contractor progressed this work in an expeditious manner, and that no special measures were necessary for the proper execution of the work, except as noted above.

**NEW YORK CITY DEP.
TIME AND MATERIAL INSPECTOR'S DAILY REPORT**

Weather: Clear 70
Location: PARK AVE + E 116th ST.
Borough: MANHATTAN

Date: 4-14-14
Loc #: 154
Contract #: 6E-351

Contractor: J P PICONE

LABOR / NAME	LOCAL	TITLE	TIME		DEP		UTIL 1		UTIL 2		EQUIPMENT	QTY	DEP	UTIL 1	UTIL 2
			IN	OUT	ST	OT	ST	OT	ST	OT					
1		Super													
2	731	Foreman	7 AM	7 PM	6	2 1/2	2	1			Cat 446 Backhoe	1	8 1/2		3
3	1536	Timberman	7 AM	7 PM	6	2 1/2	2	1			Compressor 185	1	2		2
4	731	Laborer	7 AM	7 PM	6	2 1/2	2	1			Cut-Off Saw	1	5		3
5	731	Laborer	7 AM	7 PM	6	2 1/2	2	1			Chain Saw	1	5		3
6	731	Laborer	7 AM	7 PM	6	2 1/2	2	1			Target Saw / Size =				
7	731	Laborer	7 AM	7 PM	6	2 1/2	2	1			3' Trash Pump (w/ hoses)				
8	1536	Laborer	7 AM	7 PM	6	2 1/2	2	1			3' Mudsucker (w/ hoses)				
9											Roller 5T / Walk Behind				
10											Plate Tamper				
11											Jumping Jack Tamper				
12	15	Backhoe	7 AM	7 PM	6	2 1/2	2	1			Utility Truck	1	8 1/2		3
13	282	Boom Truck									Boom Truck				
14	15	Lights									2" Pump (w/ hose)				
15	15	Pumpman									10-WH Dump Truck	1	8 1/2		3
16	14	Compressor	7 AM	11 AM	2		2				6-WH Dump Truck				
17											Furnace / Weedburner				
18											Tar Kettle - Trailer				
19	282	Dump Truck	7 AM	7 PM	6	2 1/2	2	1			Welder with Truck				
20											Generator 5000 W				

MATERIALS:

23 P.C. 3"x10"x16' LUMBERS
ACR. 5 yds MIX (out) #108044.
18 yds MIX (out) #108040.
18 yds MIX (out) #108014.

Light Tower
Traffic Signs (sf)
Arrow Board
Traffic Cones
Traffic Barrels
Bicycle Racks
Timber Barricade
Flashing Lights
Steel Plates
Wind Stands

SUBCONTRACTORS:

MR. JOHN

Move Backhoe
Move


DESCRIPTION OF WORK:

OPEN EXCAVATES BY MACHINE AND BY HAND
TO EXPOSE SEWER CONNECTION TO BUILDING #1647.
EXCAVATED FROM DEPTH OF 6' TO DEPTH OF 13'.
CREW ENCOUNTER A NUMEROUS AMOUNT OF BOULDERS

DOT PERMIT #
CODE 53 #

UNUSUAL CONDITIONS

SKETCH:

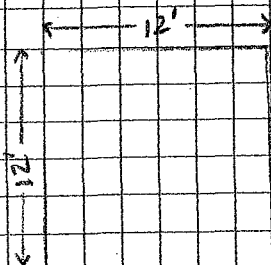

I hereby certify that I inspected the work described hereto, that the time and material records are accurate and correct, that the work was done in an expeditious manner and the labor and equipment shown here were necessary for the proper execution of the work, except as noted.

Weather: SUNNY 61°
Location: Park Ave. & E. 116th St.
Borough: MANHATTAN

Date: Mon. 4-14-14
Loc #: 154
Contract #: GE-351

I hereby certify that I inspected the work described hereto, that the time and material records are accurate and correct, the work in an expeditious manner and that the equipment shown here was necessary for the proper execution of the work, except

NEW YORK CITY DEP.
TIME AND MATERIAL INSPECTOR'S DAILY REPORT

Weather: RAIN
Location: PARK HSC - E 116th ST
Borough: _____

Date: 4-15-14
Loc #: 154
Contract #: GC-351

[illegible]

I hereby certify that I inspected the work described herein, that the time and material records are accurate and correct, that the expeditious manner a [redacted] were necessary for the proper execution of the work, except as [redacted] ed this work in an

CONTRACTOR REP:

Weather: cloudy rain 61°
Location: Park Ave. + E. 116th St.
Borough: Manhattan

Date: Tues. 4-15-14
Loc #: 154
Contract #: GE-351

I hereby certify that I inspected the work described hereto, that the time and material records are accurate and correct, that the cost of the work is reasonable, and that the work was completed in an expeditious manner and in accordance with the contract and the specifications necessary for the proper execution of the work, except as noted below:

**NEW YORK CITY DEP.
TIME AND MATERIAL INSPECTOR'S DAILY REPORT**

Weather: SUNNY 35°
Location: Park Ave. + E. 116th St.
Borough: MANHATTAN

Date: Wed. 4-16-14
Loc #: 154
Contract #: G-E-351

Contractor: J.P. PICONE

UTL 1 ECS	UTL 2 EP-7	TIME		DEP		ST		OT		EQUIPMENT	QTY	DEP	UTL 1	UTL 2	44.7
		IN	OUT	ST	OT	ST	OT	ST	OT						
		LABOR / NAME	LOCAL	TITLE											
		1 A. YIMAZ		Super	7:00 AM	11:00 AM	4			Cat 446 Backhoe	1	2 1/2	3	3	3
		2 H. Pirrone	731	Foreman	7:00 AM	7:00 PM	2 1/2	1 1/2	1 1/2	2	1		1 1/2	2	2
		3	1536	Timberman						Cut-Off Saw					
		4 D. Buonfrisco	731	Laborer	7:00 AM	7:00 PM	2 1/2	1 1/2	1 1/2	2	1		3	2	3
		5 M. DeLrio	731	Laborer	7:00 AM	7:00 PM	2 1/2	1 1/2	1 1/2	2	1				
		6 J. Urli	731	Laborer	7:00 AM	12:00 PM	1			3					
		7 D. Dzadosky Jr.	731	Laborer	7:00 AM	7:00 PM	2 1/2	1 1/2	1 1/2	2	1				
		8 C. Todd	731	Laborer	7:00 AM	7:00 PM	2 1/2	1 1/2	1 1/2	2	1				
		9								Plate Tamper	1	2			
		10								Jumping Jack Tamper					
		11								Utility Truck	1	2 1/2	3	3	3
		12 A. Casillo	15	Backhoe	7:00 AM	7:00 PM	2 1/2	1 1/2	1 1/2	2	1		1	2	2
		13 R. Leberge	282	Boom Truck	7:00 AM	12:00 PM				2					
		14	15	Lights						2" Pump (w/ hose)	1	2 1/2	3	3	3
		15	15	Pumpman						10-WH Dump Truck					
		16 P. Hall	14	Compressor	7:00 AM	1:00 PM				1 1/2	2				
		17								6-WH Dump Truck					
		18								Furnace / Weedburner					
		19 D. Dzadosky	282	Dump Truck	7:00 AM	7:00 PM	2 1/2	1 1/2	1 1/2	2	1		1	2	
		20								Tar Kettle - Trailer					
										Welder with Truck					
										Generator 5000 W					
										Light Stands					

MATERIALS: All City Recycling
6 yds. debris # 108211

Picone yard
6 bags cold patch
4 R.R. spikes
15 - 3" x 10" x 12' lumber

SUBCONTRACTORS: Mr. John

DESCRIPTION OF WORK: Removed R/W plates from
truck + continued digging out by
hand + continued sheeting trench.
Used 9' of 12" D.I.P. cleaned up
job site + reset plates + made safe.

Move Backhoe
Move
DOT PERMIT # M012014083004
CODE 53 # 091046
048
082

UNUSUAL CONDITIONS

SKETCH:

NEW YORK CITY DEP.
TIME AND MATERIAL INSPECTOR'S DAILY REPORT

Weather: RAIN CLEAR
Location: PARK AVE + E 111th ST.
Borough: MANHATTAN

Date: 4-16-14
Loc #: 154
Contract #: GE-351

[illegible]

I hereby certify that I inspected the work described hereto, that the time and material records are accurate and correct, and that the equipment shown here were necessary for the proper execution of the work, except as noted.

CONTRACTOR REP.
